

KIIDC WEEKLY PROGRESS REPORT



KIIDC



PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

**UPGRADATION OF GOVT. ITI
KANNUR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount : Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion : 14-08-2021

Scheduled progress as on 21-08-2021 - 100 %

Achieved progress as on 21-08-2021 - 15 %

Last week progress - 1%

Current week progress - 1%

Current Bill Status : 1st bill submitted

Current Financial Progress - 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 80% completed
- Steel works has to be started for pending columns, staircase, beams, slab etc
- Smart class room tile works finished.

Works done in the last week

- Beam bottom and staircase shuttering work were done



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM BRIDGE ACROSS KUPPAM
RIVER IN KOOVERY-KATTAMPALLY IN CHAPPARAPADAVU
PANCHAYAT , THALIPARAMBA TALUK, KANNUR DISTRICT**

Name of contractor : Infab Infrastructures Ltd
Agreement date : 15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Status of Work in terms of components:

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

Works done in the last week

- Topographical, GPS Survey works for land acquisition works has been done at both banks

Scheduled progress as on 21- 08-2021 - 100 %

Achieved progress as on 21- 08-2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NA

Current Financial Progress - 0 %

Images of works done at Site during last week (with time stamp)



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM
(KIIFB)**

**KIIFB PROJECT-
CONSTRUCTION OF
REGULATOR WITH LOCK
ACROSS ANCHARAKANDY
RIVER AT PARAPRAM IN
PINARAYI PANCHAYATH,
KANNUR DISTRICT**

Name of contractor : PGCC
Agreement date : 06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion :15-05-2022
Expected Date of completion :15-05-2022

Scheduled progress as on 21-08-2021 - 18%

Achieved progress as on 21-08-2021 - 9.75 %

Last week progress - 9.5%

Current week progress - 9.75%

Current Bill Status : First Part Bill submitted-Rs. 2,32,66,073.00

Current Financial Progress : 8%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Wing Wall (Left Bank D/S Retaining wall upto Apron portion): Completed
- Wing Wall (Left Bank U/S Retaining wall upto Apron portion): Completed
- Bank Protection Works (U/S Left Bank): Stem concreting completed (Ch: 8.50m to 20m)

Works done in the last week:

- Pier P1: 10th Lift concreting (+7.65m)
- Pier P2: 9th Lift concreting (+7.40m)
- Abutment A1: 7th lift concreting (+5.40m)
- Bank Protection Works (D/S Left Bank): Base slab concreting (Ch: 16.50m to 28.50m)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

- 1. Andalurkavu**
- 2. Jagannath Temple**
- 3. Kottiyoor tourist Amenities**
- 4. Illikunnu church**
- 5. Lokanarkavu Temple**
- 6. Makreri Subramanyaswami Temple**

Andalurkavu

Name of contractor Vallamattam : Sri. Varkeychan T
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.518 Cr
Agreed Amount With GST : Rs. 1,70,11,777.6
Site Handover date : 08-03-2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Approved components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

Status:

- Agreement Executed.
- Work yet to be started

Jagannath Temple

Name of contractor : Sri. Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.481 Cr
Agreed Amount With GST : Rs. 1,65,96,091.2
Site Handover date : 08-03-2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Approved components:

- Pathway
- Electrification
- Trees and street furniture
- Revival of pond
- Compound wall

Status:

- Agreement Executed.
- Work yet to be started

Kottiyoor tourist Amenities

Name of contractor : Sri. Saji Varghese
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.749 Cr
Agreed Amount With GST : Rs. 1,95,91,008.6
Site Handover date : 08.03.2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Status of Work in terms of components:

- Dormitory and Clock room
- Ticket counter
- Tourist pilgrim shelter
- Electrical works
- Landscaping

Status:

- Agreement Executed.
- Work yet to be started

Illikunnu church

Name of contractor : Sri. Varkeychan T Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 0.798 Cr
Agreed Amount With GST : Rs. 89,38,493.08
Site Handover date : 08.03.2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Status of Work in terms of components:

- Landscaping of cemetery area
- Lighting
- Conservation of ceiling
- Woodwork
- Joinery
- Electrical works

Status:

- Agreement Executed.
- Work yet to be started

Lokanarkavu Temple

Name of contractor : Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3.787 Cr
Agreed Amount With GST : Rs. 4,24,19,523.2
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-06-2022
Expected Date of completion :

Status of Work in terms of components:

- Museum of Folklore
- Oottupura
- Thanthrimadam - Museum of Myth
- Conservation of Small Chira, Kulappura
- Compound wall and step
- Conservation of Big Chira
- Electrical works
- Plumbing and toilet fittings for differentially abled
- Pavement works & Landscaping

Status:

- Agreement Executed.
- Work yet to be started

Makreri Subramanyaswami Temple

Name of contractor : Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 1.835 Cr
Agreed Amount With GST : Rs. 2,05,52,642.3
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-06-2022
Expected Date of completion :

Status of Work in terms of components:

- Oottupura
- Toilet Block
- Landscaping
- Electrical
- Streetscape (Paving of Chuttambalam)
- Water supply and Sanitary Arrangements
- Stone Paving
- Conservation of pond
- Electrification

Status:

- Agreement Executed.
- Work yet to be started
- MoU to be signed.

PROJECTS IN WAYANAD DISTRICT

**KARAPUZHA PHASE
III
(TOURISM)**

**KARAPUZHA PHASE III
CONSTRUCTION OF VIEWING
TOWER, BAMBOO PAVILION
AND BRIDGE**

Name of contractor : JAYAPRAKASHAN P
Agreement date : 22/12/2017
Agreed Amount : ₹ 7248330.00
Agreed Amount With GST : Rs. 725000.00
Site Handover date : 29/12/2017
Project duration : 10 months
Scheduled Date of Completion :29/10/2018
Expected Date of completion :15/07/2021

Status of Work in terms of components:

- Viewing tower-97%
- Bamboo pavilion-100%
- Bridge.-100%

Works done in the last week

- Viewing tower- work has delayed due to contractor own reasons

Scheduled progress as on 21-08-2021 100%

Achieved progress as on 21-08-2021 - 97%

Last week progress in 0%

Current week progress - 0%

Current Bill Status :3rd bills submitted of amount 41,40,724.00

Current Financial Progress :60%

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOZHIKODE DISTRICT

**ITI KOYILANDY
(KASE)**

**UPGRADATION OF GOVT. ITI
KOYILANDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion : 13-08-2021
Expected Date of completion : 13-09-2021

Status of Work in terms of components:

- Main Building Civil works – 77%
- Main Building Electrical works – 77%
- Main Building ELV Works - 63%

Works done in the last week

- Main Building Civil works
- Main Building Plumbing works
- Security Cabin works started

Scheduled progress as on 21-08-2021 - 100%

Achieved progress as on 21-08-2021 - 53%

Last week progress in 52.5%

Current week progress in 53%

Current Bill Status : CC 2nd and part submitted

Current Financial Progress : 25.8%

Images of works done at Site during last week (with time stamp)



**PERUVANNAMOO
ZHI (TOURISM)**

**DEVELOPMENT OF
PERUVANNAMOOZHI DAM
TOURISM PROJECT IN
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N
Agreement date : 06-11-2020
Agreed Amount : ₹ 26359270.97
Agreed Amount With GST : Rs. 31388620.00
Site Handover date : 13/11/2020
Project duration : 9 months
Scheduled Date of Completion : 12-08-2021
Expected Date of completion : 30-09-2021

Status of Work in terms of components:

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate
- Open cafeteria.

Works done in the last week

- Childrens park-site clearing for landscaping
- Construction of new gate-column concrete
- Walk way with handrails-filling quarry waste, handrail work in progress.
- Canteen-gypsum ceiling works

Scheduled progress as on 21-08-2021 - 75%

Achieved progress as on 21-08-2021 - 65%

Last week progress in 30%

Current week progress in 50 %

Current Bill Status : 1st bill-46,10,745.21

Current Financial Progress :20%

Images of works done at Site during last week (with time stamp)



**RCB
PERINCHERIKADA
VU
(KIIFB)**

**CONSTRUCTION OF
REGULATOR CUM BRIDGE AT
U/S OF PERINCHERIKADAVU IN
KUTTIADY RIVER
(GULIKAPUZHA) AT
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 6,11,33,413.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022
Expected Date of completion :16-09-2022

Status of Work in terms of components:

- RCB – 2% (three piles casted)
- Bank Protection works – 1%
- Material collection works are going on.(Coconut posts supplying)

Works done in the last week

- Boring for pile work
- RCC of plile

Scheduled progress as on 21-08-2021 - 53%

Achieved progress as on 21-08-2021 - 2.5%

Last week progress in 2%

Current week progress 2.5%

Current Bill Status : NIL

Current Financial Progress : NIL

Images of works done at Site during last week (with time stamp)



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

**KIIFB Project - Construction of
Regulator at Puzhankavu across
Kadalundi River**

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion :16/06/2021
Expected Date of completion :15/02/2022

Status of Work in terms of components:

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

Works done in the last week

- Work is delayed due rainfall and rise in water level.

Scheduled progress as on 21-08-2021- 100 %

Achieved progress as on 21-08-2021 - 55%

Last week progress in 55 %

Current week progress in 55 %

Current Bill Status : Total Bill submitted ₹3 Crores

Current Financial Progress in %: 8.67%

Images of works done at Site during last week



**RCB
Moothikkayam
(KIIFB)**

**KIIFB Project construction of
regulator cum bridge across
thoothapuzha keezhmurikadavu
moothikkayam in moorkanad
panchayath**

Name of contractor : M/s PGCC Pvt,Ltd
Agreement date : 18/09/2020
Agreed Amount : ₹57.56 Cr
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 26-09-2020
Project duration : 18 months
Scheduled Date of Completion :26-03-2022
Expected Date of completion :26/12/2022

Status of Work in terms of components:

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

Works done in the last week

- No work has done due to monsoon.
- Submitted LA Proposals to KIIDC HQs
- Hand over survey sketch to panchayath for tree cutting

Scheduled progress as on 21/08/2021 - 61%

Achieved progress as on 21/08/2021 - 3%

Last week progress - 3%

Current week progress - 3%

Current Bill Status : First & part bill submitted – Rs 1.03 Cr

Current Financial Progress : 1.75%

Images of works done at Site during last week (with time stamp)



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMBUZHA
(KASE)**

**UPGRADATION OF GOVT. ITI
MALAMPUZHA ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS
Agreement date : 05/03/20
Agreed Amount : ₹11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date : 16/03/2020
Project duration : 18 months
Scheduled Date of Completion : 05/09/2021
Expected Date of completion : 29/06/22

Scheduled progress as on 21/08/2021- 95%

Achieved progress as on 21/08/2021 - 37%

Last week progress - 1%

Current week progress - 1%

Current Bill Status : no of bill submitted - 1, amount:- 68,83,336

Current Financial Progress : 6.3%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building part 2 roof slab completed
- Initial pile load test,routine test
- Smart classroom flooring and painting completed.
- Lower basement plinth beam work completed.
- FF part 1 area column rising completed.
- Part 3 UGF roof slab work under progress.

Works done in the last week

- UGF block work under progress
- LGF retaining wall steel work under progress
- Retaining wall 15% completed
- Block work up to lintel height achieved.
- Ceiling plastering started @UGF
- Part3 UGF slab shuttering under progress.



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-07-2022

Scheduled progress as on 21/08/2021 - 39 %

Achieved progress as on 21/08/2021 - 27 %

Last week progress - 1%

Current week progress - 1%

Current Bill Status : 1 st bill submitted of 1.56 cr

Current Financial Progress : 0%

Images of works done at Site during last week

Status of Work in terms of components:

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(35m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 2 pier and 2nd Lift of 3 pier is completed

Works done in the last week

- No major civil works done



**Moongilmada LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹33288750 Crores
Agreed Amount With GST : Rs. 37283400/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

- Work Stopped due to Rain and soil condition

Scheduled progress as on 21/08/2021 - 48 %

Achieved progress as on 21/08/2021 - 40.5 %

Last week progress in : 40.5%

Current week progress : 0%

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

**Karadippara LIS
(WRD-RKI)**

**KIIDC-Providing Community
micro irrigation at karadipara LIS
in eruthenpathy Panchayath
palakkad district**

Name of contractor :M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹2,34,53,555.40 Crores
Agreed Amount With GST : Rs. 26267982.04/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

- Main Line Installation
- Automation Work

Scheduled progress as on 21/08/2021 - 54 %

Achieved progress as on 21/08/2021 - 99 %

Last week progress in : 95 %

Current week progress in 4%

Current Bill Status : NO

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



**Karadipara
(Civil)**

**KIIDC-Providing Community
micro irrigation at karadipara LIS
in eruthenpathy Panchayath
palakkad district-Civil**

Name of contractor :M/s Vallamattam constructions
Agreement date : 26-02-2021
Agreed Amount : ₹16,41,529.18 Lakhs
Agreed Amount With GST : Rs. 18,38,512.68/-
Site Handover date : 26-02-2021
Project duration : 6 months
Scheduled Date of Completion :26-08-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Construction of Pump House
- Electrification

Works done in the last week

- Painting work

Scheduled progress as on 21/08/2021 - 46 %

Achieved progress as on 21/08/2021 - 99 %

Last week progress in : 96%

Current week progress in 3%

Current Bill Status : No

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)

PROJECTS IN THRISSUR DISTRICT

ITI CHALAKUDY

**UP GRADATION OF GOVT ITI
CHALAKUDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Sidheek, M/S Sitco Associates
Agreement date : 28-10-2020
Agreed Amount : ₹ 7,47,51,405.13
Agreed Amount With GST : ₹ 8,37,21,573.74
Site Handover date : 06-11-2020
Project duration : 12 months
Scheduled Date of Completion : 05-11-2021
Expected Date of Completion :

Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the last week

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

Scheduled progress as on 21-08-2021 - 0 %

Achieved progress as on 21-08-2021 - 0 %


Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

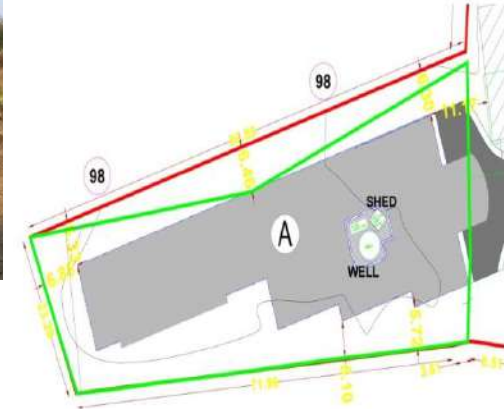

PROJECTS IN ERNAKULAM DISTRICT

**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion :

Status of Work in terms of components:

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

Works done in the last week

- NO WORK

Scheduled progress as on 21-08-2021 - 21 %

Achieved progress as on 21-08-2021- 4%

Last week progress - 4%

Current week progress - 4%

Current Bill Status : Nil

Current Financial Progress :0 %

Images of works done at Site during last week (with time stamp)



**ANTHAKARATHO
DU CANAL
(KIIFB)**

**IMPROVEMENTS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY**

Name of contractor : Southern Tech
Agreement date : 08-10-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration :15 months
Scheduled Date of Completion :07-01-2020
Expected Date of completion :30-08-2021

Status of Work in terms of components:

- Cleaning & desilting- completed
- Side protection work- 81%
- Road and walkway formation- 58%
- Fencing and Handrail work-59%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%(tile work remaining)

Works done in the last week

- Fixing GI post ch690-900 (RB)
- Epoxy painting - fencing post
- Welding & placing the fencing frame

Scheduled progress as on 21-08-2021 - 98%

Achieved progress as on 21-08-2021 - 93.75%

Last week progress - 93.50%

Current week progress -93.75%

Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY—PROVIDING
STREET LIGHTS ALONG THE
PATHWAYS OF
ANTHAKARATHODE**

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 08-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 31-07-2021

Status of Work in terms of components:

- Excavation and supply Laying of cable-50%
- Placing of lamp post, LED & feeder -40%
- Excavation and concreting-65%

Works done in the last week

- Pole and light fixing

Scheduled progress as on 21-08-2021- 85%

Achieved progress as on 21-08-2021- 50%

Last week progress - 44%

Current week progress 50%

Current Bill Status : First and Part Bill prepared

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

**UP GRADATION OF GOVT ITI
KATTAPPANA ON PAR WITH
INTERNATIONAL
STANDARDS**

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 24-02-2022
Expected Date of completion : 24-02-2022

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 20 %
- Grade beam concrete- 3%
- Grade slab Concrete - 2%

Works done in the last week

. PCC for grade beam
Reinforcement works for grade slab
Grade slab concrete
Reinforcement for grade beam.

Scheduled progress as on 21-08-2021 - 32%

Achieved progress as on 21-08-2021 - 25.00%

Last week progress : 23.05%

Current week progress :25%

Current Bill Status : 1st and part bill submitted

Current Financial Progress in %:NIL

Images of works done at Site during last week

**PAVANATHA
COLLAGE
MURIKKASSERY
(RUSA)**

**RUSA II PROJECT -
CONSTRUCTION-PAVANATHMA
COLLEGE MURIKKASSERI,
IDUKKI.**

Name of contractor : Anchanical constructions
Agreement date : 02.12.2019
Agreed Amount : Rs.79,00,000
Agreed Amount With GST : Rs.93,22,000
Site Handover date : 02-06-2020
Project duration : 09 months
Scheduled Date of Completion :31-08-2021
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

Works done in the last week

- No works done.

Scheduled progress as on 21-08-2021 - 96%

Achieved progress as on 21-08-2021 - 89%

Last week progress : 89%

Current week progress in : 89%

Current Bill Status : 2 Bills submitted, RS 54,77,389.30

Current Financial Progress : 69%

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – I
(TOURISM)**

**ADDITIONAL WORK I OF ECO
LODGE CONSTRUCTION AT
IDUKKI (CONSTRUCTION OF
APPROACH ROAD,RETAINING
WALL,DRAIN AND STREET
LIGHTING).**

Name of contractor : M/S VJ Raju and Co.
Agreement date : 11-08-2020
Agreed Amount : Rs.69,50,003.24
Agreed Amount With GST : Rs. 77,84,003.36
Site Handover date : 21-08-2020
Project duration : 04 months
Scheduled Date of Completion : 31-08-2021
Expected Date of completion : 08-07-2021

Status of Work in terms of components:

- Interlocking pathway 100%
- Gate installation 90%
- Providing street lights - 60%
- Pathway concrete - 95%
- Retaining wall - 95 %

Works done in the last week

- Pathway interlocking
- Rain delayed work progress.
- Gate fixing.

Scheduled progress as on 21-08-2021 - 97%

Achieved progress as on 21-08-2021 - 99%

Last week progress : 97.5%

Current week progress : 99%

Current Bill Status : 1 Bill submitted, RS 36,27,077.98.

Current Financial Progress : 52%

Images of works done at Site during last week

PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVT. GUEST HOUSE PEERMADE ,
IDUKKI**

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 13-09-2021

Scheduled progress as on 21-08-2021 - 78 %

Achieved progress as on 21-08-2021 - 28 %

Last week progress in % -26.4%

Current week progress - 28%

Current Bill Status : 1st and part bill submitted

Current Financial Progress : 15%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Roofing works of guest house building is completed
- 95% of roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building and Tiling works started

Works done in the last week

- Floor PCC and Tiling works of guest house building



PANCHALIMEDU
(TOURISM)

PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAMVILLAGE,
PEERMEDU TALUK, IDUKKI DISTRICT

Name of contractor : EASYINFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : 31-12-2021

Scheduled progress as on 21-08-2021 - 50 %

Achieved progress as on 21-08-2021 - 17 %

Last week progress - 17 %

Current week progress - 17 %

Current Bill Status : 1st and part bill submitted

Current Financial Progress : 10 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

Works done in the last week

- Work stopped due to heavy rain and mist.
- Meeting and site visit is conducted to discuss about the construction of check dam.
- Attendance
 - 1) sri K T Binu (district panchayath member)
 - 2) smt.Baby sheeja (DD, tourism dpt.)
 - 3)sri Gireesh (secretary DTPC Idukki)
 - 4) Er. Haran Babu sir(DGM, KIIDC)
 - 5) Er. Sarath sir (PCO, KIIDC)
 - 6)sri Abhiram (Project coordinator, DTPC)
 - 7) sri Atheesh P Mohan (CPE, KIIDC)
 - 8) sri Dileep (contractor)
 - 9) sri Rajesh (site engineer-contractor)



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

**UP GRADATION OF GOVT ITI
ETTUMANOOR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Swathy Construction
Agreement date : 30-07-2020
Agreed Amount : ₹ 6,95,25,557.81
Agreed Amount With GST : ₹ 7,78,68,624.74
Site Handover date : 10-08-2020
Project duration : 12 months
Scheduled Date of Completion : 09-08-2021
Expected Date of Completion : Within this Financial Year

Scheduled progress as on 21/08/2021- 100 %

Achieved progress as on 21/08/2021 - 49 %

Last week progress - 48%

Current week progress - 1%

Current Bill Status : CC 3rd and part is submitted (total : ₹ 2,24,79,461.06)

Current Financial Progress : 32%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (70%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting (0%)
- Fire protection works (0%)
- Furniture for existing smart class room
Converted to smart class rooms (0%)

Works done in the last week -

Main building civil works

- Electrical concealed works
- Outside Plastering
- OHT concrete



**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE
INSTITUTE OF HOTEL
MANAGEMENT STUDIES AT
PALA, KOTTAYAM DISTRICT,
CONSTRUCTION OF ACADEMIC
BLOCK**

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Scheduled progress as on 21/08/2021 - 90%

Achieved progress as on 21/08/2021 - 84%

Last week progress -81%

Current week progress - 3%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 74 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works done in the last week

- Water tank cover slab shuttering and reinforcement works



**CHEEPUNKAL
(TOURISM)**

**KI IDC KUMARAKOM
CHEEPUNKAL DESTINATION
DEVELOPMENT PROJECT AT
AYMANAM PANCHAYAT IN
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1,19,66,517.41
Agreed Amount With GST : ₹ 1,34,02,499.49
Site Handover date : 05-05-2021
Project duration : 12 months
Scheduled Date of Completion : 04-05-2022
Expected Date of Completion : 04-05-2022

Scheduled progress as on 22/08/2021-

Achieved progress as on 22/08/2021 - Nil

Last week progress -

Current week progress -

Current Bill Status : Nil

Current Financial Progress : Nil

Status of Work in terms of components:

- House Boat Jetty (0%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

Works done in the last week - Main building civil works

- Reinforcement work for Pile
- Casting of Precast concrete piles

Images of works done at Site during last week (with time stamp)



PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR
WITH INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

Name of contractor : Creators Construction
Agreement date : 15/10/2020
Agreed Amount : Rs 18 Cr
Agreed Amount With GST : Rs20,64,45672/-
Site Handover date :23/10/2020
Project duration :18 months
Scheduled Date of Completion : 22/04/2022
Expected Date of completion :22/3/2022

Scheduled progress as on 21/08/2021 -55%

Achieved progress as on 21/08/2021 -Nil

Last week progress in - Nil

Current week progress in - Nil

Current Bill Status : (no: of bills submitted with amount) Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)- Nil

Status of Work in terms of components:

- Main building civil works (0%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

Works done in the last week

- Tree cutting has been taken for open tender, and the amount accepted has given to directorate for approval.The accepted amount has been given to government for approval.
- Meeting was arranged on 15/7/2021 by KASE,KIIDC AND CHENGANNUR ITI Principal and discussed the various issue regarding the treecutting and KIIFB query and sorted out conclusion

**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

**MODERNIZING WATER
TRANSPORT IN ALAPPUZHA
CANALS-PHASE 01**

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-09-2021

Scheduled progress as on 21/08/2021 - 100%

Achieved progress as on 21/08/2021 - 93.00%

Last week progress in 92.75%

Current week progress- 0.25%

Current Bill Status : Rs.38,13,65,683.22 upto 4th bill

Current Financial Progress : 70%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Cleaning of Canals Completed
- Deepening of Canals after dewatering Completed
- RR Masonry side protection
 - Main Canals Completed
 - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
 - Culvert Structural Works Completed
 - Approach wall Under progress

Works done in the last week

- Backfilling at Ambanakulangara culvert
- GSB backfilling at Poonkavu and Vellapady culverts
- Rubble works in Ambanakulangara nad Mattathil culverts
- A.S canal bank strengthening using coir geotextiles



**PUNNAMADA
(TOURISM WORK)**

**Punnamada- Starting Point
Pathway and Boat Landing at
Alapuzha District.**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 04-11-2021
Expected Date of completion : 04-11-2021

Status of Work in terms of components:

- Pathway
Solar Lighting

Works done in the last week

- The mobilization works for carrying out the components under progress

Scheduled progress as on 21/08/2021- 20%

Achieved progress as on 21/08/2021 - 0%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

**CHUNGAM
(TOURISM WORK)**

**CHUNGAM(CHAKREPURAKKAL
)- KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 04-02-2022

Scheduled progress as on 21/08/2021 - 15%

Achieved progress as on 21/08/2021 - 0%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- Concrete works for Pile&Slab
- Coconut posts stacking



**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-05-2022

Status of Work in terms of components:

- 20m groynes – (5 nos) - Not Started
- 30M GROYNES - 7nos- 2 completed
- 40M GROYNES – 9 nos - 2 in progress
- 50M GROYNES – 9 nos - 0 in progress
- Sea wall length - 305 m – Not started
- 67571.50 MT boulders reached out of 178922 MT (38 %)
- 2T TETRAPODS – 9611 nos. casted out of 23902 nos.
- 5T TETRAPODS – 756 nos. casted out of 2956 nos.
- Earthwork Excavation – 9359.27m3 completed out of 45955.7 M3

Works done in the last week

- 2T tetrapod casted -9611 nos.
- 5T tetrapod casted - 756 nos.
- Supplying and Laying of Boulders - 4939.98 MT
- laying of boulders for G10 and G21 are in progress.

Scheduled progress as on 21/08/2021 – 60 %

progress as on 21/08/2021 - 29.5 %

Last week progress - 1.7%

Current week progress - 2 %

Current Bill Status : 2 bill submitted for an Amount of Rs. 11,23,21,298

Current Financial Progress : 13.62 %

Images of works done at Site during last week (with time stamp)



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

- 1.20M GROYNES - 6 NOS-Not started
- 2. 25M GROYNES - 15 NOS-Not started
- 3. SEA WALL LENGTH - 40m –Not started
- 4. TOTAL QUANTITY OF BOULDERS - 94497 MT
- 7. 2T TETRAPODS -1610nos casted out of 9874 NOS
- 8. 5T TETRAPODS - 2385 NOS
- 9. GEOMAT - 64739 M2
- 10. EARTHWORK EXCAVATION - 3290 M3

Works done in the last week

-Tetrapod casting is started and Total no of cased tetrapods, 2T-229nos

Scheduled progress as on 21/08/2021 - 66%

Achieved progress as on 21/08/2021 - 5%

Last week progress -2.5%

Current week progress -2.5%

Current Bill Status :1 part bill submitted for an amount of Rs 1715000.00

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of contractor : Ramalingam construction Company Pvt. Lmtd.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-05-2022

Status of Work in terms of components:

1. 20M GROYNES - 2 NOS-One is started and in progress
2. 30MGROYNES - 4 NOS-2 nos are started and in progress
3. 50M GROYNES - 7 NOS- started 2nos
- 4.22884MT boulders reached out of 74546 MT
5. 2T TETRAPODS -4488casted out of 8930NOS
6. 5T TETRAPODS -328nos casted out of 1199NOS
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154 M3

Works done in the last week

- 2T and 5T tetrapod casting is in progress
- The total no.of tetrapods casted 2T-272 and 5T-31nos
- Geomat layed for G4&G5
- Supplying and laying of boulders-3783.35 MT

Scheduled progress as on 21/08/2021 - 66%

Achieved progress as on 21/08/2021 -23%

Last week progress in - 5%

Current week progress in 5%

Current Bill Status : 2 part bills submitted for an amt of Rs 23596744.04

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

1. 20M GROYNES - 2NOS-Not started
2. 30M GROYNES -10 NOS-Not started
3. 40M GROYNES - 4 NOS- Not started
4. TOTAL QUANTITY OF BOULDERS - 101487 MT
5. 2T TETRAPODS - 3437nos casted out of 8941 NOS
6. 5T TETRAPODS 61NOS
7. GEOMAT - 76299M2
8. EARTHWORK EXCAVATION – 6239M3

Works done in the last week

-The total no.of tetrapods casted
2T -184nos and
5T is 29

Scheduled progress as on 21/08/2021 - 66%

Achieved progress as on 21/08/2021 - 10%

Last week progress - 2.5%

Current week progress - 2.5%

Current Status : 2 part bills submitted for an amt of Rs15862000.00

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



**GROYNES SITE AT
KATTOOR
(KIIFB)**

Construction of 34 nos. Groyne at Kattoor
from Ch.168.465KM TO CH 171.627KM (Old CH 96.643KM TO CH
9.535 KM)

Name of contractor : Ramalingam Construction
Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-05-2022

Scheduled progress as on 21-08-2021 – 70%

Achieved progress as on 21-08-2021 - 23.16%

Last week progress - 1.9%

Current week progress - 4 %

Current Bill Status : 2 bill submitted for an Amount of Rs. 7,01,81,077.49

Current Financial Progress : 9.12 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groynes - 3 nos – started(3nos)
- 30m Groynes -7 nos – started(2 nos)
- 40m groynes - 24 nos- started(2)
- Laying of boulders - started
- 2T TETRAPODS – 11945 nos. casted out of 21562 nos.
- 5T TETRAPODS – 898 nos. casted out of 3144 nos.
- Geomat - 112083 m2
- Earthwork Excavation - 42122 M3

Works done in the last week

- 2T tetrapod casted - 505 nos.
- 5T tetrapod casted - 31 nos.
- Supplying and Laying of Boulders - 5287.95 MT
- laying of boulders for G9 - G16 and G22-G25 are in progress.



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion :23-08-2021
Expected Date of completion :31-12-2021

Scheduled progress as on 21/08/2021 - 96%

Achieved progress as on 21/08/2021 - 19%

Last week progress - 2%

Current week progress -3%

Current Bill Status : (no: of bills submitted with amount) - NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works –25%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 18%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

- Main building civil works - Grade slab base concreting completed



**Thenmala
(Tourism Project)**

**IMPROVEMENT AND
DEVELOPING ECO-TOURISM AT
THENMALA DAM IN KOLLAM
DISTRICT**

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹4.5 Cr
Agreed Amount With GST : Rs. 4,49,90,000.00
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 07-01-2022

Scheduled progress as on 21/08/2021 - 49%

Achieved progress as on 21/08/2021 - 13%

Last week progress in -13%

Current week progress -2%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- SHOP (8.5%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (20%)
- Security cabin (2%)
- Toilet and cloak room (2%)

Works done in the last week

- Shop- lintel completed in two span.
- Water tank foundation work completed, plinth work of water tank completed
- Water tank column for 1m concreted completed
- Water tank top beam completed
- Building renovation septic tank excavation completed
- Clearing site for toilet and security cabin
- Dismantling completed of dispensary building
- Pavilion clearing completed
- Water tank vertical wall reinforcement and wall 1.5 m concrete completed



**ITI
DHANUVECHAPU
RAM
(KASE)**

**UPGRADATION OF GOVT. ITI
DHANUVECHAPURAM ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Heather Construction
Agreement date : 25-11-2019
Agreed Amount : ₹11.18 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration : 20 months
Scheduled Date of Completion : Applied for EOT
Expected Date of completion : Applied for EOT

Scheduled progress as on 21-08-2021- 100%

Achieved progress as on 21-08-2021 - 80%

Last week progress - 77%

Current week progress - 80%

Current Bill Status :8bill were passed, Amount up to 9th bill:61209828.93/-
,9th bill submitted amount:5991217.08/-

Current Financial Progress :54.74%

Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 92% completed
- GF primer work 90% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 40% completed
- FF Block Work 95% completed
- FF Ceiling work 70% completed
- FF plastering 90% completed
- Dummy column RCC completed
- FF Electrical concealed work 65% completed
- Parapet plastering 90% completed
- GF Tile work 52%
- FF primer work 75% completed

Works done in the

last week

- Outside Plastering
- GF-Interior painting works.
- FF-Floor tile laying

