

# KIIDC WEEKLY PROGRESS REPORT



KIIDC



# **PROJECTS IN KANNUR DISTRICT**

**ITI KANNUR  
(KASE )**

**UPGRADATION OF GOVT. ITI  
KANNUR ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A  
Agreement date : 26-08-2020  
Agreed Amount : Rs.3,40,93,937.97  
Agreed Amount With GST : Rs.3,64,82,353.00  
Site Handover date : 04-09-2020  
Project duration : 8 months  
Scheduled Date of Completion : 03-05-2021  
Expected Date of completion : 14-08-2021

Scheduled progress as on 27-08-2021 - 100 %

Achieved progress as on 27-08-2021 - 18 %

Last week progress - 1%

Current week progress - 1%

Current Bill Status : 1st bill submitted

Current Financial Progress - 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 80% completed
- Steel works has to be started for pending columns, staircase, beams, slab etc
- Smart class room tile works finished.

**Works done in the last week**

- Beam side and staircase shuttering work were done



**RCB KUPPAM RIVER  
IN  
KOOVERY-KATTAM  
PALLY  
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM BRIDGE ACROSS KUPPAM  
RIVER IN KOOVERY-KATTAMPALLY IN CHAPPARAPADAVU  
PANCHAYAT , THALIPARAMBA TALUK, KANNUR DISTRICT**

Name of contractor : Infab Infrastructures Ltd  
Agreement date : 15-10-2019  
Agreed Amount : ₹ 18,57,64,823.98  
Agreed Amount With GST : 22,03,74,512.96 (as per RE)  
Site Handover date : 07-11-2019  
Project duration : 18 months  
Scheduled Date of Completion : 07-05-2021  
Expected Date of completion : NA

**Status of Work in terms of components:**

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

**Works done in the last week**

- Topographical, GPS Survey works for land acquisition works has been done at both banks

**Scheduled progress as on 28- 08-2021 - 100 %**

**Achieved progress as on 28- 08-2021 - 0 %**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : NA**

**Current Financial Progress - 0 %**

**Images of works done at Site during last week (with time stamp)**





**REGULATOR  
ANCHARAKANDY  
RIVER AT  
PARAPRAM  
(KIIFB)**

**KIIFB PROJECT-  
CONSTRUCTION OF  
REGULATOR WITH LOCK  
ACROSS ANCHARAKANDY  
RIVER AT PARAPRAM IN  
PINARAYI PANCHAYATH,  
KANNUR DISTRICT**

Name of contractor : PGCC  
Agreement date : 06-11-2020  
Agreed Amount : ₹44.49 Cr  
Agreed Amount With GST : Rs. 498,385,551.00  
Site Handover date : 16-11-2020  
Project duration : 18 months  
Scheduled Date of Completion :15-05-2022  
Expected Date of completion :15-05-2022

Scheduled progress as on 27-08-2021 - 18%

Achieved progress as on 27-08-2021 - 9.8 %

Last week progress - 9.75%

Current week progress - 9.8%

Current Bill Status : First Part Bill submitted-Rs. 2,32,66,073.00

Current Financial Progress : 8%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Wing Wall (Left Bank D/S Retaining wall upto Apron portion): Completed
- Wing Wall (Left Bank U/S Retaining wall upto Apron portion): Completed
- Bank Protection Works (U/S Left Bank): Stem concreting completed (Ch: 8.50m to 20m)

- Pier P1: 10th Lift concreting (+7.65m)

- Pier P2: 9th Lift concreting (+7.40m)

**Works done in the last week:**

- Abutment A1: 9th lift concreting (+7.40m)
- Bank Protection Works (D/S Left Bank): First Lift Stem concreting, -0.40m level (Ch: 16.50m to 28.50m)
- Ring Bund work for Side Protection U/S LB in progress





**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

- 1. Andalurkavu**
- 2. Jagannath Temple**
- 3. Kottiyoor tourist Amenities**
- 4. Illikunnu church**
- 5. Lokanarkavu Temple**
- 6. Makreri Subramanyaswami Temple**

## Andalurkavu

**Name of contractor** Vallamattam : Sri. Varkeychan T  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.518 Cr  
**Agreed Amount With GST** : Rs. 1,70,11,777.6  
**Site Handover date** : 08-03-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

### Approved components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

### Status:

- Agreement Executed.
- Work yet to be started

## Jagannath Temple

**Name of contractor** : Sri. Joseph R V  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.481 Cr  
**Agreed Amount With GST** : Rs. 1,65,96,091.2  
**Site Handover date** : 08-03-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

### Approved components:

- Pathway
- Electrification
- Trees and street furniture
- Revival of pond
- Compound wall

### Status:

- Agreement Executed.
- Work yet to be started

### Kottiyoor tourist Amenities

**Name of contractor** : Sri. Saji Varghese  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.749 Cr  
**Agreed Amount With GST** : Rs. 1,95,91,008.6  
**Site Handover date** : 08.03.2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

#### Status of Work in terms of components:

- Dormitory and Clock room
- Ticket counter
- Tourist pilgrim shelter
- Electrical works
- Landscaping

#### Status:

- Agreement Executed.
- Work yet to be started

### Illikunnu church

**Name of contractor** : Sri. Varkeychan T Vallamattam  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 0.798 Cr  
**Agreed Amount With GST** : Rs. 89,38,493.08  
**Site Handover date** : 08.03.2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 08-03-2022  
**Expected Date of completion** :

#### Status of Work in terms of components:

- Landscaping of cemetery area
- Lighting
- Conservation of ceiling
- Woodwork
- Joinery
- Electrical works

#### Status:

- Agreement Executed.
- Work yet to be started

## Lokanarkavu Temple

**Name of contractor** : Saaj constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 3.787 Cr  
**Agreed Amount With GST** : Rs. 4,24,19,523.2  
**Site Handover date** :  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 27-06-2022  
**Expected Date of completion** :

### Status of Work in terms of components:

- Museum of Folklore
- Oottupura
- Thanthrimadam - Museum of Myth
- Conservation of Small Chira, Kulappura
- Compound wall and step
- Conservation of Big Chira
- Electrical works
- Plumbing and toilet fittings for differentially abled
- Pavement works & Landscaping

### Status:

- Agreement Executed.
- Work yet to be started

## Makreri Subramanyaswami Temple

**Name of contractor** : Saaj constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 1.835 Cr  
**Agreed Amount With GST** : Rs. 2,05,52,642.3  
**Site Handover date** :  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 27-06-2022  
**Expected Date of completion** :

### Status of Work in terms of components:

- Oottupura
- Toilet Block
- Landscaping
- Electrical
- Streetscape ( Paving of Chuttambalam)
- Water supply and Sanitary Arrangements
- Stone Paving
- Conservation of pond
- Electrification

### Status:

- Agreement Executed.
- Work yet to be started
- MoU to be signed.

# **PROJECTS IN WAYANAD DISTRICT**

**KARAPUZHA PHASE  
III  
(TOURISM)**

**KARAPUZHA PHASE III  
CONSTRUCTION OF VIEWING  
TOWER, BAMBOO PAVILION  
AND BRIDGE**



Name of contractor : JAYAPRAKASHAN P  
Agreement date : 22/12/2017  
Agreed Amount : ₹ 7248330.00  
Agreed Amount With GST : Rs. 725000.00  
Site Handover date : 29/12/2017  
Project duration : 10 months  
Scheduled Date of Completion :29/10/2018  
Expected Date of completion :15/07/2021

**Status of Work in terms of components:**

- Viewing tower-97%
- Bamboo pavilion-100%
- Bridge.-100%

**Works done in the last week**

- Viewing tower- work has delayed due to contractor own reasons

**Scheduled progress as on 28-08-2021 100%**

**Achieved progress as on 28-08-2021 - 97%**

**Last week progress in 0%**

**Current week progress - 0%**

**Current Bill Status :3rd bills submitted of amount 41,40,724.00**

**Current Financial Progress :60%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN KOZHIKODE DISTRICT

**ITI KOYILANDY  
(KASE)**

**UPGRADATION OF GOVT. ITI  
KOYILANDY ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.  
Agreement date : 14-08-2020  
Agreed Amount : ₹4.22 Cr  
Agreed Amount With GST : Rs. 4,22,86,606  
Site Handover date : 14-08-2020  
Project duration : 12 months  
Scheduled Date of Completion : 13-08-2021  
Expected Date of completion : 13-09-2021

**Status of Work in terms of components:**

- Main Building Civil works – 77%
- Main Building Electrical works – 77%
- Main Building ELV Works - 63%

**Works done in the last week**

- Main Building Civil works
- Main Building Plumbing works
- Security Cabin works started

**Scheduled progress as on 29-08-2021 - 100%**

**Achieved progress as on 29-08-2021 - 53.5%**

**Last week progress in 52.5%**

**Current week progress in 53%**

**Current Bill Status : CC 2<sup>nd</sup> and part submitted**

**Current Financial Progress : 25.8%**

**Images of works done at Site during last week (with time stamp)**



**PERUVANNAMOO  
ZHI (TOURISM)**

**DEVELOPMENT OF  
PERUVANNAMOOZHI DAM  
TOURISM PROJECT IN  
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N  
 Agreement date : 06-11-2020  
 Agreed Amount : ₹ 26359270.97  
 Agreed Amount With GST : Rs. 31388620.00  
 Site Handover date : 13/11?2020  
 Project duration : 9 months  
 Scheduled Date of Completion :12-08-2021  
 Expected Date of completion :30-09-2021

**Status of Work in terms of components:**

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate
- Open cafeteria.

**Works done in the last week**

- Childrens park-site clearing for landscaping
- Construction of new gate-column concrete, solid block masonry
- Walk way with handrails-filling quarry waste, handrail work,laying interlock work in progress.
- Canteen-fixing doors and windows frames
- Interpretation center -fixing doors frames, grills

Scheduled progress as on 28-08-2021 - 80%

Achieved progress as on 28-08-2021 - 65%

Last week progress in 30%

Current week progress in 50 %

Current Bill Status : 1st bill-46,10,745.21

Current Financial Progress :20%

Images of works done at Site during last week (with time stamp)





**RCB  
PERINCHERIKADA  
VU  
(KIIFB)**

**CONSTRUCTION OF  
REGULATOR CUM BRIDGE AT  
U/S OF PERINCHERIKADAVU IN  
KUTTIADY RIVER  
(GULIKAPUZHA) AT  
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium  
Agreement date : 07-09-2020  
Agreed Amount : ₹ 6,11,33,413.18/-  
Agreed Amount With GST : ₹ 68,46,94,229/-  
Site Handover date : 17-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :16-03-2022  
Expected Date of completion :16-09-2022

**Status of Work in terms of components:**

- RCB – 2% (three piles casted)
- Bank Protection works – 1%
- Material collection works are going on.( Coconut posts supplying)

**Works done in the last week**

- Boring for pile work
- RCC of plile

**Scheduled progress as on 29-08-2021 - 53%**

**Achieved progress as on 29-08-2021 - 3%**

**Last week progress in 2%**

**Current week progress 2.5%**

**Current Bill Status : NIL**

**Current Financial Progress : NIL**

**Images of works done at Site during last week (with time stamp)**



**PROJECTS IN  
MALAPPURAM  
DISTRICT**

**Puzhankavu  
Regulator  
(KIIFB)**

**KIIFB Project - Construction of  
Regulator at Puzhankavu across  
Kadalundi River**

Name of contractor : Infab Infrastructure Pvt Ltd  
Agreement date : 17-12-2019  
Agreed Amount : ₹ 9,79,65,435.62  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 17-12-2019  
Project duration : 18 months  
Scheduled Date of Completion :16/06/2021  
Expected Date of completion :15/02/2022

**Status of Work in terms of components:**

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

**Works done in the last week**

- Work is delayed due rainfall and rise in water level.

**Scheduled progress as on 27-08-2021- 100 %**

**Achieved progress as on 27-08-2021 - 55%**

**Last week progress in 55 %**

**Current week progress in 55 %**

**Current Bill Status : Total Bill submitted ₹3 Crores**

**Current Financial Progress in %: 8.67%**

**Images of works done at Site during last week**



**RCB  
Moothikkayam  
(KIIFB)**

**KIIFB Project construction of  
regulator cum bridge across  
thoothapuzha keezhmurikadavu  
moothikkayam in moorkanad  
panchayath**



Name of contractor : M/s PGCC Pvt,Ltd  
Agreement date : 18/09/2020  
Agreed Amount : ₹57.56 Cr  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 26-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :26-03-2022  
Expected Date of completion :26/12/2022

**Status of Work in terms of components:**

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

**Works done in the last week**

- No work has done due to monsoon.
- Submitted LA Proposals to KIIDC HQs
- Hand over survey sketch to panchayath for tree cutting

**Scheduled progress as on 27/08/2021 - 61%**

**Achieved progress as on 27/08/2021 - 3%**

**Last week progress - 3%**

**Current week progress - 3%**

**Current Bill Status : First & part bill submitted – Rs 1.03 Cr**

**Current Financial Progress : 1.75%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMBUZHA  
(KASE)**

**UPGRADATION OF GOVT. ITI  
MALAMPUZHA ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS  
Agreement date : 05/03/20  
Agreed Amount : ₹11,61,93,745/-  
Agreed Amount With GST : Rs. 13,01,36,994.40/-  
Site Handover date : 16/03/2020  
Project duration : 18 months  
Scheduled Date of Completion. : 05/09/2021  
Expected Date of completion : 02/06/22

**Status of Work in terms of components:**

- Main building part 2 roof slab completed
- Initial pile load test,routine test
- Smart classroom flooring and painting completed.
- Lower basement plinth beam work completed.
- FF part 1 area column rising completed.
- Part 3 UGF roof slab completed.

**Works done in the last week**

- UGF block work under progress
- LGF retaining wall steel work under progress
- UGF part 3 slab concreted.
- Block work up to lintel height acheived
- Ceiling plastering started @UGF under progress.

**Scheduled progress as on 28/08/2021- 95%**

**Achieved progress as on 28/08/2021 - 37%**

**Last week progress - 1%**

**Current week progress - 1%**

**Current Bill Status : no of bill submitted - 1, amount:- 68,83,336**

**Current Financial Progress : 6.3%**

**Images of works done at Site during last week (with time stamp)**



VADAKARAPALLY  
REGULATOR  
(KIIFB)

Construction of Regulator across Chittur  
Puzha at Vadakarapally Palathulli in  
Peruvembu Grama Panchayt in Palakkad  
District

**Name of contractor** : Poonam grah nirman Pvt ltd  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹18.95 Cr  
**Agreed Amount With GST** : Rs. 21,23,18,001.2  
**Site Handover date** : 12-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 12-07-2022  
**Expected Date of completion** : 12-07-2022

**Scheduled progress as on 31/08/2021 - 40 %**

**Achieved progress as on 31/08/2021 - 27 %**

**Last week progress - 1%**

**Current week progress - 1%**

**Current Bill Status : 1 st bill submitted of 1.56 cr**

**Current Financial Progress : 0%**

**Images of works done at Site during last week**

**Status of Work in terms of components:**

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(35m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 2 pier and 2nd Lift of 3 pier is completed

**Works done in the last week**

- No major civil works done





**Moongilmada LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

**Name of contractor** : M/s poljo Vyapar kendra Pvt Ltd  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹33288750 Crores  
**Agreed Amount With GST** : Rs. 37283400/-  
**Site Handover date** : 26-02-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :26-02-2022  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

- Work Stopped due to Rain and soil condition

**Scheduled progress as on 30/08/2021 - 50 %**

**Achieved progress as on 30/08/2021 - 40.5 %**

**Last week progress in : 40.5%**

**Current week progress : 0%**

**Current Bill Status : Nil**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**

**Karadippara LIS  
(WRD-RKI )**

**KIIDC-Providing Community  
micro irrigation at karadipara LIS  
in eruthenpathy Panchayath  
palakkad district**

**Name of contractor** :M/s poljo Vyapar kendra Pvt Ltd  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹2,34,53,555.40 Crores  
**Agreed Amount With GST** : Rs. 26267982.04/-  
**Site Handover date** : 26-02-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :26-02-2022  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

- Conducting Trial Run
- Automation Work

**Scheduled progress as on 30/08/2021 - 56 %**

**Achieved progress as on 30/08/2021 - 99 %**

**Last week progress in : 99 %**

**Current week progress in 0%**

**Current Bill Status : NO**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**



**Karadipara  
(Civil)**

**KIIDC-Providing Community  
micro irrigation at karadipara LIS  
in eruthenpathy Panchayath  
palakkad district-Civil**

**Name of contractor** :M/s Vallamattam constructions  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹16,41,529.18 Lakhs  
**Agreed Amount With GST** : Rs. 18,38,512.68/-  
**Site Handover date** : 26-02-2021  
**Project duration** : 6 months  
**Scheduled Date of Completion** :26-08-2022  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Construction of Pump House
- Electrification

**Works done in the last week**

- Conducting Trial Run

**Scheduled progress as on 30/08/2021 - 50 %**

**Achieved progress as on 30/08/2021 - 99 %**

**Last week progress in : 99%**

**Current week progress in 0%**

**Current Bill Status : No**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**

# PROJECTS IN THRISSUR DISTRICT

**ITI CHALAKUDY**

**UP GRADATION OF GOVT ITI  
CHALAKUDY ON PAR WITH  
INTERNATIONAL STANDARDS**



Name of contractor : Sidheek, M/S Sitco Associates

Agreement date : 28-10-2020

Agreed Amount : ₹ 7,47,51,405.13

Agreed Amount With GST : ₹ 8,37,21,573.74

Site Handover date : 06-11-2020

Project duration : 12 months

Scheduled Date of Completion : 05-11-2021

Expected Date of Completion :

Scheduled progress as on 30-8-2021 - 0 %

Achieved progress as on 30-08-2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)


### Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

### Works done in the

#### last week

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

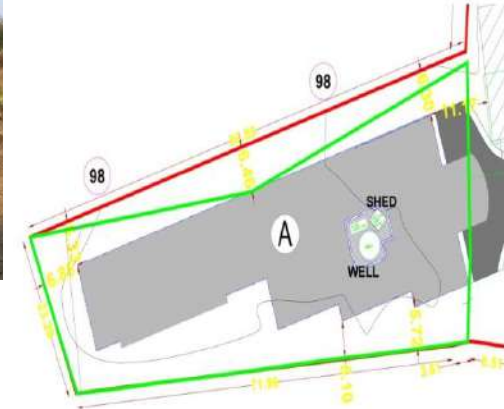

# **PROJECTS IN ERNAKULAM DISTRICT**

**RCB  
KONOTHUPUZHA  
(KIIFB)**

**Construction of Regulator with  
lock across Konothupuzha at  
Puthenkavu in Udayamperoor  
Panchayath in Ernakulam  
District**

Name of contractor : Marymatha construction  
Agreement date : 04-01-2021  
Agreed Amount : ₹24.36 Cr  
Agreed Amount With GST : Rs. 272,843,729.92  
Site Handover date : 14-01-2021  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2022  
Expected Date of completion :

**Status of Work in terms of components:**

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

**Works done in the last week**

- NO WORK

Scheduled progress as on 28-08-2021 - 30 %

Achieved progress as on 28-08-2021- 4%

Last week progress - 4%

Current week progress - 4%

Current Bill Status : Nil

Current Financial Progress :0 %

Images of works done at Site during last week (with time stamp)



**ANTHAKARATHO  
DU CANAL  
(KIIFB)**

**IMPROVEMENTS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY**

Name of contractor : Southern Tech  
Agreement date : 08-10-2018  
Agreed Amount : ₹8.35 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 04-12-2019  
Project duration :15 months  
Scheduled Date of Completion :07-01-2020  
Expected Date of completion :30-08-2021

**Status of Work in terms of components:**

- Cleaning & desilting- completed
- Side protection work- 81%
- Road and walkway formation- 58%
- Fencing and Handrail work-60%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%(tile work remaining)

**Works done in the last week**

- Fixing GI post ch320-690 (LB)
- Epoxy painting - fencing post
- Welding & placing the fencing frame
- Precast pile cutting

**Scheduled progress as on 28-08-2021 - 98%**

**Achieved progress as on 28-08-2021 - 94%**

**Last week progress - 93.75%**

**Current week progress 94%**

**Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00**

**Current Financial Progress : 65%**

**Images of works done at Site during last week (with time stamp)**



**ELECTRICAL  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY—PROVIDING  
STREET LIGHTS ALONG THE  
PATHWAYS OF  
ANTHAKARATHODE**

Name of contractor : Essjay Electro links  
Agreement date : 31-12-2020  
Agreed Amount : ₹50.27 lakhs  
Agreed Amount With GST : Rs. 5630313.00  
Site Handover date : 08-01-2021  
Project duration : 5 months  
Scheduled Date of Completion : 30-05-2021  
Expected Date of completion : 31-07-2021

**Status of Work in terms of components:**

- Excavation and supply Laying of cable-60%
- Placing of lamp post, LED & feeder -55%
- Excavation and concreting-65%

**Works done in the last week**

- Pole and light fixing
- Cable laying
- Feeder post installation

**Scheduled progress as on 28-08-2021- 85%**

**Achieved progress as on 28-08-2021- 54%**

**Last week progress - 50%**

**Current week progress 54%**

**Current Bill Status : First and Part Bill prepared**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**





# PROJECTS IN IDUKKI DISTRICT

**ITI  
KATTAPPANA  
(KASE)**

**UP GRADATION OF GOVT ITI  
KATTAPPANA ON PAR WITH  
INTERNATIONAL  
STANDARDS**

**Name of contractor** : Anchanical constructions  
**Agreement date** : 16.10.2020  
**Agreed Amount** : Rs 4,76,87,560.83  
**Agreed Amount With GST** : Rs 5,34,10,068.1  
**Site Handover date** : 04-12-2019  
**Project duration** : 08 months  
**Scheduled Date of Completion** : 21-12-2021  
**Expected Date of completion** : 21-12-2021

Status of Work in terms of components:

Work slowed down due to rain.

Reinforcement works of grade beam - 28 %

Grade beam concrete- 9%

Grade slab Concrete - 8%

Works done in the last week

. PCC for grade beam

. Reinforcement works for grade slab

Grade slab concrete

. Reinforcement for grade beam.

**Scheduled progress as on 28-08-2021 - 35%**

**Achieved progress as on 28-08-2021 - 28.00%**

**Last week progress : 35%**

**Current week progress :28%**

**Current Bill Status : 1st and part bill submitted**

**Current Financial Progress in %:NIL**

**Images of works done at Site during last week**



**PAVANATHA  
COLLAGE  
MURIKKASSERY  
(RUSA )**

**RUSA II PROJECT -  
CONSTRUCTION-PAVANATHMA  
COLLEGE MURIKKASSERI,  
IDUKKI.**

**Name of contractor** : Anchanical constructions  
**Agreement date** : 02.12.2019  
**Agreed Amount** : Rs.79,00,000  
**Agreed Amount With GST** : Rs.93,22,000  
**Site Handover date** : 02-06-2020  
**Project duration** : 09 months  
**Scheduled Date of Completion** :31-08-2021  
**Expected Date of completion** :31-08-2021

**Status of Work in terms of components:**

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

**Works done in the last week**

- No works done.

**Scheduled progress as on 28-08-2021 - 99%**

**Achieved progress as on 28-08-2021 - 89%**

**Last week progress : 89%**

**Current week progress in : 89%**

**Current Bill Status : 2 Bills submitted, RS 54,77,389.30**

**Current Financial Progress : 69%**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – I  
(TOURISM)**

**ADDITIONAL WORK I OF ECO  
LODGE CONSTRUCTION AT  
IDUKKI (CONSTRUCTION OF  
APPROACH ROAD,RETAINING  
WALL,DRAIN AND STREET  
LIGHTING).**

Name of contractor : M/S VJ Raju and Co.  
Agreement date : 11-08-2020  
Agreed Amount : Rs.69,50,003.24  
Agreed Amount With GST : Rs. 77,84,003.36  
Site Handover date : 21-08-2020  
Project duration : 04 months  
Scheduled Date of Completion : 31-08-2021  
Expected Date of completion : 08-07-2021

**Status of Work in terms of components:**

- Interlocking pathway 100%
- Gate installation 90%
- Providing street lights - 60%
- Pathway concrete - 95%
- Retaining wall - 95 %

**Works done in the last week**

- Pathway interlocking
- Rain delayed work progress.
- Gate fixing.

**Scheduled progress as on 28-08-2021 - 97%**

**Achieved progress as on 28-08-2021 - 99%**

**Last week progress : 97.5%**

**Current week progress : 99%**

**Current Bill Status : 1 Bill submitted, RS 36,27,077.98.**

**Current Financial Progress : 52%**

**Images of works done at Site during last week**



PEERMADE  
GUEST HOUSE  
RENOVATION  
(TOURISM)

**UPGRADATION AND RENOVATION OF  
GOVT. GUEST HOUSE PEERMADE ,  
IDUKKI**



Name of contractor :SRI BIBY SCARIA  
Agreement date : 30-06-2020  
Agreed Amount : Rs.1,45,51,908.00  
Agreed Amount With GST : Rs. 1,71,71,251.44  
Site Handover date : 13-07-2020  
Project duration : 9 months  
Scheduled Date of Completion :13-04-2021  
Expected Date of completion : 13-09-2021

Scheduled progress as on 28-08-2021 - 78 %

Achieved progress as on 28-08-2021 - 30 %

Last week progress in % -28%

Current week progress - 30%

Current Bill Status : 1st and part bill submitted

Current Financial Progress : 15%


Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Roofing works of guest house building is completed
- 95% of roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building and Tiling works started

**Works done in the last week**

- Floor PCC and Tiling works of service building
- Earth work excavation for meeting hall

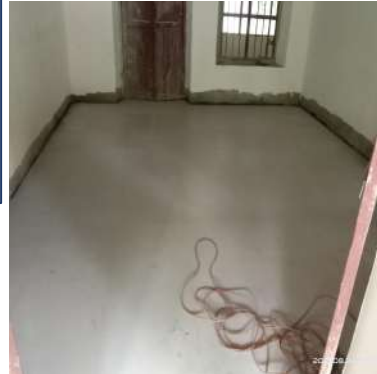

PANCHALIMEDU  
(TOURISM)

PANCHALIMEDU TOURISM PROJECT  
PHASE – 2  
PERUVANTHANAMVILLAGE,  
PEERMEDU TALUK, IDUKKI DISTRICT

**Name of contractor** : EASYINFRA INC, TVM  
**Agreement date** : 22/12/2020  
**Agreed Amount** : ₹2,43,99,440.78  
**Agreed Amount With GST** : Rs. 2,73,27,373.67  
**Site Handover date** : 01-01-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 31-12-2021  
**Expected Date of completion** : 31-12-2021

**Scheduled progress as on 28-08-2021 - 50 %**

**Achieved progress as on 28-08-2021 - 17 %**

**Last week progress - 17 %**

**Current week progress - 17 %**

**Current Bill Status : 1st and part bill submitted**

**Current Financial Progress : 10 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

**Works done in the last week**

Site inspection done by chief engineer, Minor irrigation kattappana and team.



# PROJECTS IN KOTTAYAM DISTRICT

**ITI  
ETTUMANOOR  
(KASE)**

**UP GRADATION OF GOVT ITI  
ETTUMANOOR ON PAR WITH  
INTERNATIONAL STANDARDS**

**Name of contractor** : Swathy Construction  
**Agreement date** : 30-07-2020  
**Agreed Amount** : ₹ 6,95,25,557.81  
**Agreed Amount With GST** : ₹ 7,78,68,624.74  
**Site Handover date** : 10-08-2020  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 09-08-2021  
**Expected Date of Completion** : Within this Financial Year

**Scheduled progress as on 28/08/2021- 100 %**

**Achieved progress as on 28//08/2021 - 51 %**

**Last week progress - 49%**

**Current week progress - 2%**

**Current Bill Status : CC 3<sup>rd</sup> and part is submitted (total : ₹ 2,24,79,461.06)**

**Current Financial Progress : 32%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Main building civil works (70%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting (0%)
- Fire protection works (0%)
- Furniture for existing smart class room  
Converted to smart class rooms (0%)

**Works done in the last week -**

**Main building civil works**

- Electrical and ELV concealed works
- Outside Plastering



**SIHM PALA  
(TOURISM)**

**SETTING UP OF STATE  
INSTITUTE OF HOTEL  
MANAGEMENT STUDIES AT  
PALA, KOTTAYAM DISTRICT,  
CONSTRUCTION OF ACADEMIC  
BLOCK**



Name of contractor : SITCO Associates  
Agreement date : 01-03-2016  
Agreed Amount : ₹13.48 Cr  
Site Handover date : 10-03-2016  
Project duration : 18 months  
Scheduled Date of Completion : 31/10/2017  
Expected Date of completion : 31/12/2021

Scheduled progress as on 27/08/2021 - 90%

Achieved progress as on 27/08/2021 - 84%

Last week progress -81%

Current week progress - 3%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 74 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

**Works done in the last week**

- Water tank cover slab concreting works completed.
- Porch tie beams shuttering and reinforcement works started.
- 



**CHEEPUNKAL  
(TOURISM)**

**KI IDC KUMARAKOM  
CHEEPUNKAL DESTINATION  
DEVELOPMENT PROJECT AT  
AYMANAM PANCHAYAT IN  
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1,19,66,517.41  
Agreed Amount With GST : ₹ 1,34,02,499.49  
Site Handover date : 05-05-2021  
Project duration : 12 months  
Scheduled Date of Completion : 04-05-2022  
Expected Date of Completion : 04-05-2022

Scheduled progress as on 28/08/2021-

Achieved progress as on 28/08/2021 - Nil

Last week progress -

Current week progress -

Current Bill Status : Nil

Current Financial Progress : Nil

**Status of Work in terms of components:**

- House Boat Jetty (0%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

**Works done in the last week - Main building civil works**

- Reinforcement work for Pile
- Casting of Precast concrete piles

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN ALAPPUZHA DISTRICT

**ITI  
CHENGANNUR  
(KASE)**

**UP-GRADATION OF GOVT ITI  
CHENGANNUR ON PAR  
WITH INTERNATIONAL  
STANDARDS - PHASE 1- REV 3**

Name of contractor : Creators Construction  
Agreement date : 15/10/2020  
Agreed Amount : Rs 18 Cr  
Agreed Amount With GST : Rs20,64,45672/-  
Site Handover date :23/10/2020  
Project duration :18 months  
Scheduled Date of Completion : 22/04/2022  
Expected Date of completion :22/3/2022

**Scheduled progress as on 28/08/2021 -65%**

**Achieved progress as on 28/08/2021 -Nil**

**Last week progress in - Nil**

**Current week progress in - Nil**

**Current Bill Status : (no: of bills submitted with amount) Nil**

**Current Financial Progress in %: Nil**

**Images of works done at Site during last week (with time stamp)- Nil**

**Status of Work in terms of components:**

- Main building civil works (0%)
- Existing class room converted to smart class rooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

**Works done in the last week**

- Tree cutting has been taken for open tender, and the amount accepted has given to directorate for approval.The accepted amount has been given to government for approval.
- Meeting was arranged on 15/7/2021 by KASE,KIIDC AND CHENGANNUR ITI Principal and discussed the various issue regarding the treecutting and KIIFB query and sorted out conclusion

**ALAPPUZHA  
CANALS  
PHASE.01  
(KIIFB)**

**MODERNIZING WATER  
TRANSPORT IN ALAPPUZHA  
CANALS-PHASE 01**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 15-02-2019  
Agreed Amount : ₹48.35 Cr  
Agreed Amount With GST : Rs. 54,15,71,596.79  
Site Handover date : 19-02-2019  
Project duration : 12 months  
Scheduled Date of Completion : 18-02-2020  
Expected Date of completion : 30-09-2021

Scheduled progress as on 28/08/2021 - 100%

Achieved progress as on 28/08/2021 - 93.25%

Last week progress in 93.00%

Current week progress- 0.25%

Current Bill Status : Rs.38,13,65,683.22 upto 4th bill

Current Financial Progress : 70%

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- Cleaning of Canals Completed
- Deepening of Canals after dewatering Completed
- RR Masonry side protection
  - Main Canals Completed
  - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
  - Culvert Structural Works Completed
  - Approach wall Under progress

### Works done in the last week

- Backfilling at Devi wire culvert
- GSB backfilling at Mattathil culvert
- A.S canal bank strengthening using coir geotextiles





**PUNNAMADA  
(TOURISM WORK )**

**Punnamada- Starting Point  
Pathway and Boat Landing at  
Alapuzha District.**

**Name of contractor** : TBAS Construction, Aluva  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.11 Cr  
**Agreed Amount With GST** : Rs. 1,23,77,355.31  
**Site Handover date** : 05-05-2021  
**Project duration** : 6 months  
**Scheduled Date of Completion** : 04-11-2021  
**Expected Date of completion** : 04-11-2021

**Status of Work in terms of components:**

- Pathway  
Solar Lighting

**Works done in the last week**

- The mobilization works for carrying out the components under progress

**Scheduled progress as on 28/08/2021- 20%**

**Achieved progress as on 28/08/2021 - 0%**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : NIL**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**

**CHUNGAM  
(TOURISM WORK )**

**CHUNGAM(CHAKREPURAKKAL  
)- KAYALCHIRA PATHWAY  
DEVELOPMENT AND BOAT  
LANDING BY THE SIDE OF  
PUNNAMADA RIVER, At  
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 2.99 Cr  
Agreed Amount With GST : Rs. 3,34,07,087.37  
Site Handover date : 05-05-2021  
Project duration : 9 months  
Scheduled Date of Completion : 04-02-2022  
Expected Date of completion : 04-02-2022

Scheduled progress as on 28/08/2021 - 15%

Achieved progress as on 28/08/2021 - 0%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

**Works done in the last week**

- Concrete works for Pile&Slab
- Coconut posts stacking



**GROYNES AT  
AMBALAPUZHA  
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP  
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at  
Ambalapuzha South, North panchayath and  
Punnapra South Panchayath**

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 51.3 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Status of Work in terms of components:**

- 20m groynes – (5 nos) - Not Started
- 30M GROYNES - 7nos- 2 completed
- 40M GROYNES – 9 nos - 2 in progress
- 50M GROYNES – 9 nos - 1 in progress
- Sea wall length - 305 m – Not started
- 67571.50 MT boulders reached out of 178922 MT (38 %)
- 2T TETRAPODS – 9983 nos. casted out of 23902 nos.
- 5T TETRAPODS – 812 nos. casted out of 2956 nos.
- Earthwork Excavation – 9359.27m3 completed out of 45955.7 M3

**Works done in the last week**

- 2T tetrapod casted -9983 nos.
- 5T tetrapod casted - 812 nos.
- Supplying and Laying of Boulders - 4939.98 MT
- laying of boulders for G20 and G10 are in progress. Mat laying done in G20

**Scheduled progress as on 28/08/2021 – 60 %**

**progress as on 28/08/2021 - 30 %**

**Last week progress - 2%**

**Current week progress - 2 %**

**Current Bill Status** : 2 bill submitted for an Amount of Rs. 11,23,21,298

**Current Financial Progress : 13.62 %**

**Images of works done at Site during last week (with time stamp)**



**GROYNES AT  
ARATTUPUZHA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
21NOS GROYNES AT  
ARATTUPUZHA IN BET.CH.56.6  
TO 57.8 KM AT ARATTUPUZHA**



Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹26. 23Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :29-01-2022  
Expected Date of completion :29-05-2022

**Status of Work in terms of components:**

- 1.20M GROYNES - 6 NOS-Not started
- 2. 25M GROYNES - 15 NOS-Not started
- 3. SEA WALL LENGTH - 40m –Not started
- 4. TOTAL QUANTITY OF BOULDERS - 94497 MT
- 7. 2T TETRAPODS -1839nos casted out of 9874 NOS
- 8. 5T TETRAPODS - 2385 NOS
- 9. GEOMAT - 64739 M2
- 10. EARTHWORK EXCAVATION - 3290 M3

**Works done in the last week**

-Tetrapod casting is started and Total no of cased tetrapod s,2T-229nos

**Scheduled progress as on 28/08/2021 - 66%**

**Achieved progress as on 28/08/2021 - 6%**

**Last week progress -2.5%**

**Current week progress -2.0%**

**Current Bill Status :1 part bill submitted for an amount of Rs 1715000.00**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**





**GROYNE SITE  
AT  
PATHIYANKARA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
13NOS GROUYNE AT  
PATHIYANKARA IN BET.CH.60.1  
TO 61.6KM AT  
THRIKKUNNAPUZHA.**

**Name of contractor** : Ramalingam construction Company Pvt. Lmtd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹20.08Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Status of Work in terms of components:**

1. 20M GROYNES - 2 NOS-One is started and in progress
2. 30MGROYNES - 4 NOS-2 nos are started and in progress
3. 50M GROYNES - 7 NOS- started 2nos
4. 26289.02MT boulders reached out of 74546 MT
5. 2T TETRAPODS - 4658casted out of 8930NOS
6. 5T TETRAPODS - 351nos casted out of 1199NOS
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154 M3

**Works done in the last week**

- 2T and 5T tetrapod casting is in progress
  - The total no.of tetrapods casted 2T-170 and 5T-23nos
- G1,G2,G3,G4,G5 are in progress
- Supplying and laying of boulders-3405.02 MT

**Scheduled progress as on 28/08/2021 - 66%**

**Achieved progress as on 28/08/2021 -27%**

**Last week progress in - 5%**

**Current week progress in 4.5%**

**Current Bill Status** : 2 part bills submitted for an amt of Rs 23596744.04

**Current Financial Progress in %:** Nil

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT.  
VATTACHAL  
(KIIFB)**

**KIIFB  
PROJECT – CONSTRUCTION OF  
16 NOS GROUYNE AT  
VATTACHAL IN BET. CH.53.4 TO  
CH.55.2 KM(1.8KM)  
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹28. 83Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :29-01-2022  
Expected Date of completion :29-05-2022

**Status of Work in terms of components:**

1. 20M GROYNES - 2NOS-Not started
2. 30M GROYNES -10 NOS-Not started
3. 40M GROYNES - 4 NOS- Not started
4. TOTAL QUANTITY OF BOULDERS - 101487 MT
5. 2T TETRAPODS - 3632nos casted out of 8941 NOS
6. 5T TETRAPODS 79NOS
7. GEOMAT - 76299M2
8. EARTHWORK EXCAVATION – 6239M3

**Works done in the last week**

-The total no.of tetrapods casted 2T -1195nos and 5T is 12

**Scheduled progress as on 28/08/2021 - 66%**

**Achieved progress as on 28/08/2021 - 10.5%**

**Last week progress - 2%**

**Current week progress - 1.5%**

**Current Status : 2 part bills submitted for an amt of Rs15862000.00**

**Current Financial Progress in %:Nil**

**Images of works done at Site during last week (with time stamp)**



**GROYNES SITE AT  
KATTOOR  
(KIIFB)**

**Construction of 34 nos. Groyne at Kattoor**  
from Ch.168.465KM TO CH 171.627KM (Old CH 96.643KM TO CH  
9.535 KM)

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.

**Agreement date** : 22-07-2020

**Agreed Amount** : ₹ 49.04 Cr

**Agreed Amount With GST** : Rs.

**Site Handover date** : 30-07-2020

**Project duration** : 18 months

**Scheduled Date of Completion** : 29-01-2022

**Expected Date of completion** : 29-05-2022

**Scheduled progress as on 28-08-2021 – 70%**

**Achieved progress as on 28-08-2021 - 25.82%**

**Last week progress - 2.4%**

**Current week progress - 4 %**

**Current Bill Status** : 2 bill submitted for an Amount of Rs. 7,01,81,077.49

**Current Financial Progress : 9.12 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 20m groynes - 3 nos – started(3nos)
- 30m Groynes -7 nos – started(2 nos)
- 40m groynes - 24 nos- started(2)
- Laying of boulders - started
- 2T TETRAPODS – 12535 nos. casted out of 21562 nos.
- 5T TETRAPODS – 1001 nos. casted out of 3144 nos.

**Works done in the last week**

- 2T tetrapod casted - 12535 nos.
- 5T tetrapod casted - 1001 nos.
- Supplying and Laying of Boulders - 8554.536 MT
- laying of boulders for G9 - G16 and G22-G25 are in progress.



# PROJECTS IN KOLLAM DISTRICT



**ITI CHANDANATHOPE  
(KASE)**

**UPGRADATION OF GOVT. ITI  
CHANDANATHOPE ON PAR  
WITH INTERNATIONAL  
STANDARDS**



**Name of contractor** : Asian Constructions  
**Agreement date** : 16-12-2020  
**Agreed Amount** : ₹3.65 Cr  
**Agreed Amount With GST** : Rs. 4,09,28,822.77  
**Site Handover date** : 24-12-2020  
**Project duration** : 8 months  
**Scheduled Date of Completion** :23-08-2021  
**Expected Date of completion** :31-12-2021

**Scheduled progress as on 28/08/2021 - 100%**

**Achieved progress as on 28/08/2021 - 19%**

**Last week progress - 2%**

**Current week progress -3%**

**Current Bill Status : (no: of bills submitted with amount) - NIL**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Main building civil works –25%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 18%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

**Works done in the last week**

- Main building civil works - Grade slab concreting completed
- 



**Thenmala  
(Tourism Project)**

**IMPROVEMENT AND  
DEVELOPING ECO-TOURISM AT  
THENMALA DAM IN KOLLAM  
DISTRICT**

Name of contractor : Tomy Vallamattom  
Construction  
Agreement date : 29-10-2020  
Agreed Amount : ₹4.5 Cr  
Agreed Amount With GST : Rs. 4,49,90,000.00  
Site Handover date : 09-11-2020  
Project duration : 15 months  
Scheduled Date of Completion : 08-02-2022  
Expected Date of completion : 07-01-2022

Scheduled progress as on 28/08/2021 - 49%

Achieved progress as on 28/08/2021 - 13%

Last week progress in -5%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- SHOP (8.5%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (20%)
- Security cabin (2%)
- Toilet and cloak room (2%)

**Works done in the last week**

- Shop- lintel completed in two span.
- Water tank foundation work completed, plinth work of water tank completed
- Water tank column for 1m concreted completed
- Water tank top beam completed
- Building renovation septic tank excavation completed
- Clearing site for toilet and security cabin
- Water tank cover slab reinforcement work in progress
- Pavilion clearing completed
- Water tank vertical wall reinforcement and wall 3 m concrete completed



**ITI  
DHANUVECHAPU  
RAM  
(KASE)**

**UPGRADATION OF GOVT. ITI  
DHANUVECHAPURAM ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of contractor** : Heather Construction  
**Agreement date** : 25-11-2019  
**Agreed Amount** : ₹11.18 Cr  
**Agreed Amount With GST** : Rs. 12,52,34,417.4  
**Site Handover date** : 04-12-2019  
**Project duration** : 20 months  
**Scheduled Date of Completion** : Applied for EOT  
**Expected Date of completion** : Applied for EOT

**Scheduled progress as on 28-08-2021- 100%**

**Achieved progress as on 28-08-2021 - 82%**

**Last week progress - 80%**

**Current week progress - 82%**

**Current Bill Status** :8bill were passed, Amount up to 9th bill:61209828.93/-  
,9th bill submitted amount:5991217.08/-

**Current Financial Progress :54.74%**

### Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 92% completed
- GF primer work 90% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 40% completed
- FF Block Work 95% completed
- FF Ceiling work 70% completed
- FF plastering 90% completed
- Dummy column RCC completed
- FF Electrical concealed work 65% completed
- Parapet plastering 90% completed
- GF Tile work 52%
- FF primer work 75% completed

### Works done in the

#### last week

- Outside Plastering
- GF-Interior painting works.
- FF-Floor tile laying

