

KIIDC WEEKLY PROGRESS REPORT



KIIDC



PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

**UPGRADATION OF GOVT. ITI
KANNUR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount :Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion :

Scheduled progress as on 16-10-2021 100%

Achieved progress as on 16-10-2021 - 24%

Last week progress in 1%

Current week progress - 2%

Current Bill Status :1 st bill submitted

Current Financial Progress :12.6%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 80% completed
- Steel works has to be started for pending columns, staircase, beams, slab etc

Works done in the last week

- Fire staircase concrete work were done upto landing
- Main stair concreted
- Beam and slab shuttering done
- Soil compaction done.
- Beam reinforcement done.
- Slab reinforcement completed.



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY (KIIFB)**

**CONSTRUCTION OF
REGULATOR CUM BRIDGE
ACROSS KUPPAM RIVER IN
KOOVERY-KATTAMPALLY IN
CHAPPARAPADAVU
PANCHAYAT , THALIPARAMBA
TALUK, KANNUR DISTRICT**

Name of contractor : Infab Infrastructures Ltd
Agreement date : 15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Status of Work in terms of components:

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

Works done in the last week

- Topographical, GPS Survey works for land acquisition works has been done at both banks

Scheduled progress as on 16-10-2021 100%

Achieved progress as on 16-10-2021 - 0%

Last week progress in 0%

Current week progress - 0%

Current Bill Status :NA

Current Financial Progress :0%

Images of works done at Site during last week (with time stamp)



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF
REGULATOR WITH LOCK
ACROSS ANCHARAKANDY
RIVER AT PARAPRAM IN
PINARAYI PANCHAYATH,
KANNUR DISTRICT**

Name of contractor : PGCC
Agreement date :06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion : 15-05-2022
Expected Date of completion : 15-05-2022

Status of Work in terms of components:

- .Wing Wall (Left Bank D/S Retaining wall upto Apron portion): Completed
- Wing Wall (Left Bank U/S Retaining wall upto Apron portion): Completed
- .Pier P1 & P2: Pier Head Concreting completed
- .Abutment A1: 10th lift concreting (+8.40m)

Works done in the last week

- Left Bank :stair concreted
- Left Bank Retaining wall:: U/S side upto Ch.73m C/L of RCB is completed. From Ch.88m to 100m,base concrete completed
- Left Bank D/S Ch:32m- Regulating arrangement of small streams: sluice wall,apron concrete completed.

Scheduled progress as on 16-10-2021 19.25%

Achieved progress as on 16-10-2021 - 15%

Last week progress in 9.9 %

Current week progress - 13%

Current Bill Status :First Part Bill submitted-Rs. 2,32,66,073.00

Current Financial Progress : 8.5%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

- 1. Andalurkavu**
- 2. Jagannath Temple**
- 3. Pindali Kalari**
- 4. Kottiyoor tourist Amenities**
- 5. Illikunnu church**
- 6. Lokanarkavu Temple**
- 7. Makreri Subramanyaswami Temple**

Andalurkavu

Name of contractor Varkeychan : Sri.
T Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.518 Cr
Agreed Amount With GST : Rs. 1,70,11,777.6
Site Handover date : 08-03-2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Approved components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

Jagannath Temple

Name of contractor : Sri. Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.481 Cr
Agreed Amount With GST : Rs. 1,65,96,091.2
Site Handover date : 08-03-2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Approved components:

- Pathway
- Electrification
- Trees and street furniture
- Revival of pond
- Compound wall

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

Pindali Kalari

Name of contractor : M/s Classic Builders
Agreement date : 17-02-2021
Agreed Amount : ₹ 0.6238 Cr
Agreed Amount With GST : Rs. 6987127.71
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-02-2022
Expected Date of completion :

Approved components:

- Conservation of Kalarithara
- Stone paving in pathway
- Pond restoration and Walkway
- Seating
- Landscaping

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

Kottiyoor tourist Amenities

Name of contractor : Sri. Saji Varghese
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.749 Cr
Agreed Amount With GST : Rs. 1,95,91,008.6
Site Handover date : 08.03.2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Status of Work in terms of components:

- Dormitory and Clock room
- Ticket counter
- Tourist pilgrim shelter
- Electrical works
- Landscaping

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

Illikunnu church

Name of contractor : Sri. Varkeychan T Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 0.798 Cr
Agreed Amount With GST : Rs. 89,38,493.08
Site Handover date : 08.03.2021
Project duration : 12 months
Scheduled Date of Completion : 08-03-2022
Expected Date of completion :

Status of Work in terms of components:

- Landscaping of cemetery area
- Lighting
- Conservation of ceiling
- Woodwork
- Joinery
- Electrical works

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

Lokanarkavu Temple

Name of contractor : Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3.787 Cr
Agreed Amount With GST : Rs. 4,24,19,523.2
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-06-2022
Expected Date of completion :

Status of Work in terms of components:

- Museum of Folklore
- Oottupura
- Thanthrimadam - Museum of Myth
- Conservation of Small Chira, Kulappura
- Compound wall and step
- Conservation of Big Chira
- Electrical works
- Plumbing and toilet fittings for differentially abled
- Pavement works & Landscaping

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

Makreri Subramanyaswami Temple

Name of contractor : Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 1.835 Cr
Agreed Amount With GST : Rs. 2,05,52,642.3
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-06-2022
Expected Date of completion :

Status of Work in terms of components:

- Oottupura
- Toilet Block
- Landscaping
- Electrical
- Streetscape (Paving of Chuttambalam)
- Water supply and Sanitary Arrangements
- Stone Paving
- Conservation of pond
- Electrification

Status:

- Agreement Executed.
- Work yet to be started
- GFC Drawings not received from consultant architect

PROJECTS IN WAYANAD DISTRICT

**KARAPUZHA PHASE
III
(TOURISM)**

**KARAPUZHA PHASE III
CONSTRUCTION OF VIEWING
TOWER, BAMBOO PAVILION
AND BRIDGE**

Name of contractor : JAYAPRAKASHAN P
Agreement date : 22/12/2017
Agreed Amount : ₹ 7248330.00
Agreed Amount With GST : Rs. 725000.00
Site Handover date : 29/12/2017
Project duration : 10 months
Scheduled Date of Completion :29/10/2018
Expected Date of completion :15/07/2021

Status of Work in terms of components:

- Viewing tower-99%
- Bamboo pavilion-100%
- Bridge.-100%

Work done in last week

Viewing tower-work started
Plastering floor work in progress.floor painting work in progress
Inside handrail work in progress.

Scheduled progress as on 16-10-2021 100%

Achieved progress as on 16-10-2021 - 99%

Last week progress - 0%

Current week progress - 0%

Current Bill Status :3rd bills submitted of amount 41,40,724.00

Current Financial Progress :60%

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOZHIKODE DISTRICT

**ITI KOYILANDY
(KASE)**

**UPGRADATION OF GOVT. ITI
KOYILANDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion : 13-08-2021
Expected Date of completion : 13-09-2021

Status of Work in terms of components:

- Main Building Civil works – 77.5%
- Main Building Electrical works – 80%
- Main Building ELV Works - 63%

Works done in the last week

- Main Building Civil works
- Main Building Plumbing works
- Security Cabin works started

Scheduled progress as on 16-10-2021 - 100%

Achieved progress as on 16-10-2021 - 62%


Last week progress- 61%

Current week progress - 62%

Current Bill Status : CC 2nd and part submitted

Current Financial Progress : 25.8%

Images of works done at Site during last week (with time stamp)

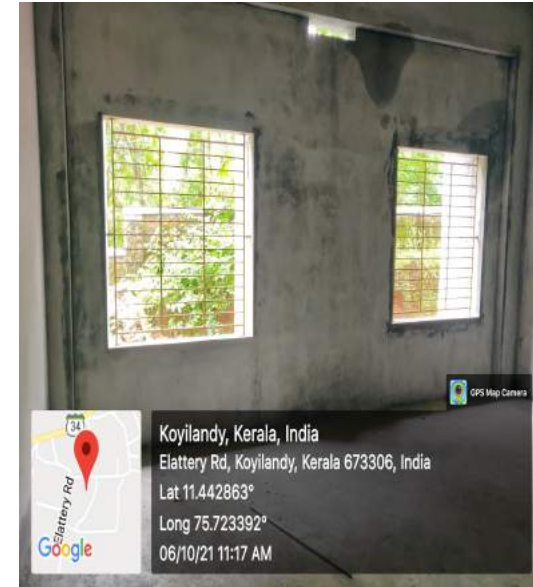

**PERUVANNAMOOZHI
(TOURISM)**

**DEVELOPMENT OF
PERUVANNAMOOZHI DAM
TOURISM PROJECT IN
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N
 Agreement date : 06-11-2020
 Agreed Amount : ₹ 26359270.97
 Agreed Amount With GST : Rs. 31388620.00
 Site Handover date : 13/11/2020
 Project duration : 9 months
 Scheduled Date of Completion :12-08-2021
 Expected Date of completion :30-09-2021

Scheduled progress as on 16-10-2021 - 90%

Achieved progress as on 16-10-2021 - 85%

Last week progress in 50%

Current week progress in 50 %

Current Bill Status : 2nd bill-1,13,91,333.097/-

Current Financial Progress :43%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate
- Open cafeteria.

Works done in the last week

- Childrens park-pargola truss work
- Canteen- laying floor tiles work in progress, outside interlock work
- Walk way with handrails-filling quarry waste, handrail work,laying interlock
- Open cafeteria- truss work in progress completed.
- Interpretation center - laying floor tiles
- Carparking- levelling, earthwork for parking
- Walkway new step-plastering work in progress.
- New gate- centerung and shuttering for room beam.



**RCB
PERINCHERIKADAVU
(KIIFB)**

**CONSTRUCTION OF
REGULATOR CUM BRIDGE AT
U/S OF PERINCHERIKADAVU IN
KUTTIADY RIVER
(GULIKAPUZHA) AT
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 6,11,33,413.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022
Expected Date of completion :16-09-2022

Status of Work in terms of components:

- RCB – 3.5%
- Bank Protection works – 1%
- Material collection works are going on.(Coconut posts supplying)

Works done in the last week

- Boring for pile work
- RCC of pile

Scheduled progress as on 16-10-2021 - 60%

Achieved progress as on 16-10-2021 - 5%

Last week progress in 4.5%

Current week progress 5%

Current Bill Status : NIL

Current Financial Progress : NIL

Images of works done at Site during last week (with time stamp)



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

**KIIFB Project - Construction of
Regulator at Puzhankavu across
Kadalundi River**

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion :16/06/2021
Expected Date of completion :15/02/2022

Scheduled progress as on 16-10-2021- 100 %

Achieved progress as on 16-10-2021 - 55%

Last week progress - 0%

Current week progress - 0 %

Current Bill Status : Total Bill submitted ₹3 Crores

Current Financial Progress in : 8.67%

Images of works done at Site during last week

Status of Work in terms of components:

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

Works done in the last week

- There is no work at site due to rainfall and rise in water level.



**RCB
Moothikkayam
(KIIFB)**

**KIIFB - Construction of Regulator
cum Bridge across thoothapuzha
keezhmurikadavu moothikkayam in
moorkanad panchayath**

Name of contractor : M/s PGCC Pvt,Ltd
Agreement date : 18/09/2020
Agreed Amount : ₹57.56 Cr
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 26-09-2020
Project duration : 18 months
Scheduled Date of Completion :26-03-2022
Expected Date of completion :26/12/2022

Status of Work in terms of components:

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

Works done in the last week

- The river is running full .Hence there is no work since the commencement of the monsoon .
- Submitted LA Proposals to Government
- Handed over survey sketch to Panchayath for tree cutting

Scheduled progress as on 16-10-2021 - 61%

Achieved progress as on 16-10-2021 - 3%

Last week progress - 3%

Current week progress - 3%

Current Bill Status : First & part bill submitted – Rs 1.03 Cr

Current Financial Progress : 1.75%

Images of works done at Site during last week (with time stamp)



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMBUZHA
(KASE)**

**UPGRADATION OF GOVT. ITI
MALAMPUZHA ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS
Agreement date : 05/03/20
Agreed Amount : ₹11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date : 16/03/2020
Project duration : 18 months
Scheduled Date of Completion. : 05/09/2021
Expected Date of completion. : 02/06/22

Scheduled progress as on 16/10/2021- 100%

Achieved progress as on 16/10/2021 - 43%

Last week progress - 42.5%

Current week progress- 43%

Current Bill Status : no of bill submitted - 3, amount:- 68,83,336

Current Financial Progress : 6.3%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building part 2 roof slab completed
- Smart classroom window and ventilator fixing under progress
- FF part 2 area column rising completed.
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.

Works done in the last week

- Ceiling plastering part 1 and part 2- 100 and part 210% completed
- Lift L1 wall upto GF roof acheived.
- Grade slab work completed instru. workshop area.
- FF Roof slab work under progress.
- FF column rising completed



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-07-2022

Status of Work in terms of components:

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(15m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 3 no of pier and 2nd Lift of 3 no of pier is completed

Works done in the last week

- There is no work at site due to rainfall and rise in water level.

Scheduled progress as on 17/10/2021 - 50%

Achieved progress as on 17/10/2021 - 27 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : 2 bill submitted amount of 1.81 cr

Current Financial Progress : 8.3 %

Images of works done at Site during last week



**Moongilmada LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹33288750 Crores
Agreed Amount With GST : Rs. 37283400/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

- Work Stopped due to heavy rain

Scheduled progress as on 17/10/2021 - 60 %

Achieved progress as on 17/10/2021 - 41.5 %

Last week progress in : 41.5%

Current week progress : 0%

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



**Karadippara LIS
(WRD-RKI)**

**KIIDC-Providing Community
micro irrigation at karadipara LIS
in eruthenpathy Panchayath
palakkad district**

Name of contractor :M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹2,34,53,555.40 Crores
Agreed Amount With GST : Rs. 26267982.04/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

- Conducting Trial Run

Scheduled progress as on 17/10/2021 - 66 %

Achieved progress as on 17/10/2021 - 100 %

Last week progress in : 100 %

Current week progress in 100%

Current Bill Status : Bill Submitted

Current Financial Progress in %:

Images of works done at Site during last week (with time stamp)



**Karadipara
(Civil)**

**KIIDC-Providing Community
micro irrigation at karadipara LIS
in eruthenpathy Panchayath
palakkad district-Civil**

Name of contractor :M/s Vallamattam constructions
Agreement date : 26-02-2021
Agreed Amount : ₹16,41,529.18 Lakhs
Agreed Amount With GST : Rs. 18,38,512.68/-
Site Handover date : 26-02-2021
Project duration : 6 months
Scheduled Date of Completion :26-08-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Construction of Pump House
- Electrification

Works done in the last week

- Conducting Trial Run

Scheduled progress as on 17/10/2021 - 70 %

Achieved progress as on 17/10/2021 - 100 %

Last week progress in : 100%

Current week progress in 100%

Current Bill Status : No

Current Financial Progress in %:Nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN THRISSUR DISTRICT

**ITI CHALAKUDY
KIIFB-KASE**

**UP GRADATION OF GOVT ITI
CHALAKUDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Sidheek, M/S Sitco Associates

Agreement date : 28-10-2020

Agreed Amount : ₹ 7,47,51,405.13

Agreed Amount With GST : ₹ 8,37,21,573.74

Site Handover date : 06-11-2020

Project duration : 12 months

Scheduled Date of Completion : 05-11-2021

Expected Date of Completion :

Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the

last week

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

Scheduled progress as on 16-10-2021 - 0 %

Achieved progress as on 16-10-2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



PROJECTS IN ERNAKULAM DISTRICT

**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion :

Status of Work in terms of components:

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

Works done in

the last week

KIIFB inspection team visited the site.

There is no work at site due to rainfall and rise in water level.

Scheduled progress as on 16-10-2021 - 35 %

Achieved progress as on 16-10-2021- 4%

Last week progress - 4%

Current week progress - 4%

Current Bill Status : Nil

Current Financial Progress :0 %

Images of works done at Site during last week (with time stamp)



**ANTHAKARATHO
DU CANAL
(KIIFB)**

**IMPROVEMENTS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY**

Name of contractor : Southern Tech
Agreement date : 08-10-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration :15 months
Scheduled Date of Completion :07-01-2021
Expected Date of completion :30-10-2021

Scheduled progress as on 16-10-2021 - 95%

Achieved progress as on 16-10-2021 - 94.5%

Last week progress - 94.25%

Current week progress 94.5%

Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Cleaning & desilting-completed
- Side protection work- 85%
- Road and walkway formation- 58%
- Fencing and Handrail work- 65%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%

Works done in the last week

- Cleaning and weeds removing works in progress
Heavy rain affected work progress of walkway and other works



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY—PROVIDING
STREET LIGHTS ALONG THE
PATHWAYS OF
ANTHAKARATHODE**

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 08-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 31-10-2021

Status of Work in terms of components:

- Excavation and supply Laying of cable-60%
- Placing of lamp post, LED & feeder -55%
- Excavation and concreting-65%

Works done in the last week

Heavy rain affected complete work

- 58% of the electrical works completed. The remaining works depends upon the civil work (pathway).
- Unexpected rain affected work progress of walkway.

Scheduled progress as on 16-10-2021- 85%

Achieved progress as on 16-10-2021- 58%

Last week progress - 54%

Current week progress 58%

Current Bill Status : First and Part Bill prepared

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



**BEAUTIFICATION
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIIPPUNITHURA
MUNICIPALITY–LANDSCAPING &
ARBORICULTURE, CONSTRUCTION
OF KIOSK AND TOILET AND
OPERATION & MAINTENANCE FOR
ONE YEAR**

Name of contractor : GRIDS,Digital Surveyors and
Engineering Consultants
Agreement date : 24-06-2021
Agreed Amount : ₹76.62 lakhs
Agreed Amount With GST : Rs. 8581690.00
Site Handover date : 03-07-2021
Project duration : 3 months
Scheduled Date of Completion : 02-10-2021
Expected Date of completion :

Status of Work in terms of components:

- Landscaping & tress-0%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

Works done in the last week

- The works depends upon the civil work (pathway).Unexpected rain affected work progress of walkway and beautification work.

Scheduled progress as on 16-10-2021- 40%

Achieved progress as on 16-10-2021- 0%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)

PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

**UP GRADATION OF GOVT ITI
KATTAPPANA ON PAR WITH
INTERNATIONAL
STANDARDS**

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 21-12-2021
Expected Date of completion : 21-12-2021

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 25%
- Grade beam concrete- 20%
- Grade slab Concrete - 18%

Works done in the last week

- PCC for grade beam
- Reinforcement works for grade slab
- Grade slab concrete
- Reinforcement for grade beam.
- Column concreting

Scheduled progress as on 16-10-2021 - 56%

Achieved progress as on 16-10-2021 - 37%

Last week progress : 37%

Current week progress :37.5%

Current Bill Status : 1st and part bill submitted

Current Financial Progress in %:NIL

Images of works done at Site during last week



**PAVANATHMA
COLLEGE
MURIKKASSERY
(RUSA)**

**RUSA II PROJECT -
CONSTRUCTION-PAVANATHMA
COLLEGE MURIKKASSERI,
IDUKKI.**

Name of contractor : Anchanical constructions
Agreement date : 02.12.2019
Agreed Amount : Rs.79,00,000
Agreed Amount With GST : Rs.93,22,000
Site Handover date : 02-06-2020
Project duration : 09 months
Scheduled Date of Completion : 31-08-2021
Expected Date of completion : 31-08-2021

Status of Work in terms of components:

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

Works done in the last week

- No works done.

Scheduled progress as on 16-10-2021 - 100%

Achieved progress as on 16-10-2021 - 89%

Last week progress : 89%

Current week progress in : 89%

Current Bill Status : 2 Bills submitted, Rs. 54,77,389.30

Current Financial Progress : 69%

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – I
(TOURISM)**

**ADDITIONAL WORK I OF ECO
LODGE CONSTRUCTION AT
IDUKKI (CONSTRUCTION OF
APPROACH ROAD,RETAINING
WALL,DRAIN AND STREET
LIGHTING).**

Name of contractor : M/S VJ Raju and Co.
Agreement date : 11-08-2020
Agreed Amount : Rs.69,50,003.24
Agreed Amount With GST : Rs. 77,84,003.36
Site Handover date : 21-08-2020
Project duration : 04 months
Scheduled Date of Completion : 31-08-2021
Expected Date of completion : 31-08-2021

Status of Work in terms of components:

- Interlocking pathway 100%
- Gate installation 100%
- Providing street lights - 100%
- Pathway concrete - 100%
- Retaining wall - 100 %

Works done in the last week

- Work completed

Scheduled progress - 100%

Achieved progress - Work Completed

Current progress : 100%

Current Bill Status : 1 Bill submitted, RS 36,27,077.98.

Current Financial Progress : 52%

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – II
(TOURISM)**

**ADDITIONAL WORK II OF ECO
LODGE CONSTRUCTION AT
IDUKKI (CONSTRUCTION OF
PUMP HOUSE, SECURITY
CABIN, SUMP TANK AND
FENCING).**

Name of contractor : M/S VJ Raju and Co.
Agreement date : 26.02.2021
Agreed Amount : Rs.45,85,722
Agreed Amount With GST : Rs. 77,84,003.36
Site Handover date : 08-03-2021
Project duration : 04 months
Scheduled Date of Completion : 07-10-2021
Expected Date of completion : 07-10-2021

Status of Work in terms of components:

- Pump house - 90%
- Security cabin - 90%
- Fencing - 10%
- Sump tank - 100%
- Plumbing, Electrical and other works - Nil %

Works done in the last week

- Plumbing works
- Electrical works

Scheduled progress as on 16-10-2021- 100%

Achieved progress as on 16-10-2021 - 80%

Last week progress : 80%

Current week progress : 95%

Current Bill Status : None.

Current Financial Progress : NIL

Images of works done at Site during last week



PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVT. GUEST HOUSE PEERMADE ,
IDUKKI**

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 13-11-2021

Scheduled progress as on 16-10-2021 - 80 %

Achieved progress as on 16-10-2021 - 41 %

Last week progress in % -35 %

Current week progress - 40%

Current Bill Status : 1st and part bill submitted RS-12,15,770 (with GST)

Current Financial Progress : 15%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Roofing works of guest house building is completed
- 95% of roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building and Tiling works started
- Foundation works of meeting hall completed

Works done in the last week

- Brick work works of meeting hall completed
- Excavation for water tank foundation
- Plumbing works of service building



PANCHALIMEDU
(TOURISM)

PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAM VILLAGE,
PEERMEDU TALUK, IDUKKI DISTRICT

Name of contractor : EASYINFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : 31-12-2021

Scheduled progress as on 16-10-2021 - 50 %

Achieved progress as on 16-10-2021 - 17 %

Last week progress - 17 %

Current week progress - 17 %

Current Bill Status : 1st and part bill submitted Rs-16,68,292/-(with GST)

Current Financial Progress : 10 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

Works done in the last week

- Site inspection done by chief engineer, Minor irrigation kattappana and team.
- Revised estimate prepared and submitted.



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

**UP GRADATION OF GOVT ITI
ETTUMANOOR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Swathy Construction

Agreement date : 30-07-2020

Agreed Amount : ₹ 6,95,25,557.81

Agreed Amount With GST : ₹ 7,78,68,624.74

Site Handover date : 10-08-2020

Project duration : 12 months

Scheduled Date of Completion : 09-08-2021

Expected Date of Completion : Within this Financial Year

Scheduled progress as on 16-10-2021- 100 %

Achieved progress as on 16-10-2021 - 65%

Last week progress - 64%

Current week progress - 1%

Current Bill Status : CC 4th and part is submitted (total : ₹ 3,02,19,228.06)

Current Financial Progress : 43.46%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (72%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (10%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (25%)
- External lighting (0%)
- Fire protection works (0%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

Works done in the last week -

Main building civil works

- Inside Plastering
- Sump tank wall Concrete works
- Water proofing Main building roof, Screed concrete and top plaster
- Water proofing bathroom sunken portion
- Tile Work on FF
- Electrical works on main building
- Plumbing works on FF



**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE
INSTITUTE OF HOTEL
MANAGEMENT STUDIES AT
PALA, KOTTAYAM DISTRICT,
CONSTRUCTION OF ACADEMIC
BLOCK**

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works were done inEx the last week

- No works have been done. Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.

Scheduled progress as on 16-10-2021 - 90%

Achieved progress as on 16-10-2021 - 85%

Last week progress -85%

Current week progress - 0%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 74 %

Images of works done at Site during last week (with time stamp)



**CHEEPUNKAL
(TOURISM)**

**KI IDC KUMARAKOM
CHEEPUNKAL DESTINATION
DEVELOPMENT PROJECT AT
AYMANAM PANCHAYAT IN
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1,19,66,517.41
Agreed Amount With GST : ₹ 1,34,02,499.49
Site Handover date : 05-05-2021
Project duration : 12 months
Scheduled Date of Completion : 04-05-2022
Expected Date of Completion : 04-05-2022

Status of Work in terms of components:

- House Boat Jetty (7%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

Due to raised level of water level, because of heavy rain delayed work

Works done in the last week - Main building civil works

- Complete casting of 106 Precast Piles were completed on 02-09-2021 and were under curing period of 28 days. The structural work of boat jetty will be commenced after curing period of piles, after that foundation of jetty will be formed by pile driving
- Driven 4 piles of 7 m length

Scheduled progress as on 16-10-2021- 17%

Achieved progress as on 16-10-2021 - 7%

Last week progress - 6%

Current week progress - 1%

Current Bill Status : CC 1st and part bill will be submitted during the time of pile driving

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR WITH
INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

Name of contractor : Creators Construction
Agreement date : 15/10/2020
Agreed Amount : Rs 18 Cr
Agreed Amount With GST : Rs20,64,45672/-
Site Handover date :23/10/2020
Project duration :18 months
Scheduled Date of Completion : 22/04/2022
Expected Date of completion :22/3/2022

Scheduled progress as on 16/10/2021 -70%

Achieved progress as on 16/10/2021 -Nil

Last week progress in - Nil

Current week progress in - Nil

Current Bill Status : (no: of bills submitted with amount) Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)- Nil

Status of Work in terms of components:

- Main building civil works (0%)
- Existing class room converted to smart classrooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

Works done in the last week

- Tree cutting approval have been obtained
- Scheduled to tuesday 28/9/2021
- Tree cutting completed
- Site clearance scheduled on wednesday



**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

**MODERNIZING WATER
TRANSPORT IN ALAPPUZHA
CANALS-PHASE 01**

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-11-2021

Scheduled progress as on 16-10-2021 - 96%

Achieved progress as on 16-10-2021 - 95.75%

Last week progress in 95.75%

Current week progress- 0%

Current Bill Status : Rs.38,13,65,683.22 upto 4th bill

Current Financial Progress : 70%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Cleaning & Deepening of Canals after dewatering Completed
- RR Masonry side protection
 - Main Canals Completed
 - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
 - Culvert Structural Works Completed
 - Approach wall Under progress

Works done in the last week

- Water hyacinth removal at Vadaicanal and Commercial Canal
- No other works due to heavy rain



9-578944296762650-763-1617280299071
Network-07/30/2021 19:14:37 am ISU

**PUNNAMADA
(TOURISM WORK)**

**Punnamada- Starting Point
Pathway and Boat Landing at
Alapuzha District.**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 04-11-2021
Expected Date of completion : 04-11-2021

Status of Work in terms of components:

- Pathway
Solar Lighting

Works done in the last week

- Tie Beam concreting.
- Heavy rain delayed the work

Scheduled progress as on 16/10/2021- 70%

Achieved progress as on 16/10/2021 - 20%

Last week progress - 18%

Current week progress - 2%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)



**CHUNGAM
(TOURISM WORK)**

**CHUNGAM(CHAKREPURAKKAL)-
KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 04-02-2022

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- No work due to heavy rain

Scheduled progress as on 16/10/2021 - 40%

Achieved progress as on 16/10/2021 - 16%

Last week progress - 16%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)



**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-01-2022

Scheduled progress as on 16-10-2021 – 77.77%

Achieved progress as on 16/10/2021 - 53.512 %

Last week progress - 3.20%

Current week progress -2.128 %

Current Bill Status : 4 th bill submitted for an Amount of Rs. 17,73,68708.62

Current Financial Progress : 24.52 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groynes – (5 nos) - 1 in progres
- 30M GROYNES - 7nos- 2 completed
- 40M GROYNES – 9 nos - 2 in progress
- 50M GROYNES – 9 nos -2 inprogress
- Sea wall length - 305 m – Not started
- 122144.753 MT boulders reached out of 178922 MT (68.26%)
- 2T TETRAPODS – 12484 nos. casted out of 23902 nos. (52.22 %)
- 5T TETRAPODS – 1151 nos. casted out of 2956 nos.(38.93%)
- Earthwork Excavation – 19950 m3 completed out of 45955.7 M3 (43%)

Works done in the last week

- 2T tetrapod casted -282 nos
- 5T tetrapod casted - 43 nos
- Supplying and Laying of Boulders - 6384.877 MT
- laying of boulders for,G17,G15,,G8,G6 is in progress.
- Laying of tetrapods in G4 finished and G5 continues,starting in G6.



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹ 26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

- 20M GROYNES - 6 NOS-Not started
- 25M GROYNES - 15 NOS-Not started
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 94497 MT
- 2T TETRAPODS -3188 (32%) nos casted out of 9874 NOS
- 5T TETRAPODS - 2385 NOS
- GEOMAT - 64739 M2
- EARTHWORK EXCAVATION - 3290 M3

Works done in the last week

- 2T tetrapod casted - 143 nos.
- 5T tetrapod casting not started.

Scheduled progress as on 17/10/2021 - 77 %

Achieved progress as on 17/10/2021 - 8.5 %

Last week progress -.38 %

Current week progress - 1 %

Current Bill Status : 1 part bill submitted for an amount of Rs 1,32,65000

Current Financial Progress in % : 5 %

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of contractor : Ramalingam construction Company Pvt. Lmtd.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-01-2022

Status of Work in terms of components:

1. 20M GROYNES - 2 NOS-One is started and in progress
2. 30MGROYNES -4 NOS-3nos are started and in progress
3. 50M GROYNES - 7 NOS- started 4nos
- 4.38017.605MT boulders reached out of 74546 MT(50.99%)
5. 2T TETRAPODS -5816casted out of 8930NOS(65.12%)
6. 5T TETRAPODS - 683nos casted out of 1199NOS(56.96%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

Works done in the last week

- Tetrapod casting is in progress
 - The total no.of tetrapods casted 2T-122& 5T-35nos G1,G2,G3,G4,G5,G9,G11 are in progress
- Conveying of tetrapods at G1 is progressing
- Supplying and laying of boulders-876.82MT

Scheduled progress as on 16/10/2021 - 77%

Achieved progress as on 16/10/2021 -45.68%

Last week progress in - 3.5%

Current week progress in 1.5%

Current Bill Status : 3rd part bills submitted for an amt of Rs 6,29,54,968.01

Current Financial Progress in : 11.74%

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Scheduled progress as on 16/10//2021 - 77%

Achieved progress as on 16/10/2021 - 17.54 %

Last week progress - 0.43 %

Current week progress - 2 %

Current Status : 4 part bills submitted for an amt of Rs 4,93,32,008.36

Current Financial Progress in % : 8.2 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 2 NOS-Not started
- 30M GROYNES - 10 NOS- 2 started
- 40M T GROYNE - 4 Nos - not started
- TOTAL QUANTITY OF BOULDERS - 7631.356 reached out of 101487 MT
- 2T TETRAPODS - 4758 (53 %) nos casted out of 8941 NOS
- 5T TETRAPODS - 274 (7.9 %) nos casted out of 3432 NOS
- GEOMAT - 792.751 m2 layed out of 76299 M2
- EARTHWORK EXCAVATION - done for G3 and G10 for ramp portion and groyne up to 20 m lngth 62380 M3

Works done in the last week

- 2T tetrapod casted - 180 nos.
- 5T tetrapod casted -45 nos.
- Supplying and Laying of Boulders - 203.726 MT
- Work progress was very slow due to heavy rain and unavailability of boulders



**GROYNES SITE AT
KATTOOR
(KIIFB)**

**Construction of 34 nos. Groyne
at Kattoor from Ch.168.465KM
TO CH 171.627KM (Old CH
96.643KM TO CH 9.535 KM)**

Name of contractor : Ramalingam Construction
Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-05-2022

Scheduled progress as on 16-10-2021 – 77%

Achieved progress as on 16-10-2021 - 68%

Last week progress - 2.49%

Current week progress - 1.7%

Current Bill Status : 3 bill submitted for an Amount of Rs. 15,060,31,34./-

Current Financial Progress : 14 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groynes - 3 started out of 3
- 30m Groynes-2 nos started out of 7
- 40m groynes - 12 nos started out of 24
- Laying of boulders - started
- 2T TETRAPODS – 16525nos (76%) casted out of 21562 nos.
- 5T TETRAPODS – 1709(54%) nos. casted out of 3144 nos.
- Geomat - 112083 m2
- Earthwork Excavation - 42122 M3

Works done in the last week

- 2T tetrapod casted - 402nos.
- 5T tetrapod casted - 55nos.
- Supplying and Laying of Boulders-1826.092M T
- laying of boulders for,G20,G30 ,G2are in progress.



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion : 23-08-2021
Expected Date of completion : 31-12-2021

Scheduled progress as on 16/10/2021 - 100%

Achieved progress as on 16/10/2021 - 30%

Last week progress -3%

Current week progress -2%

Current Bill Status : (no: of bills submitted with amount) - 1st bill submitted to KIIDC

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works –38%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

- Main building civil works - 61 Columns 2nd lift completed
- Roof shuttering works in progress



**Thenmala
(Tourism Project)**

**IMPROVEMENT AND
DEVELOPING ECO-TOURISM AT
THENMALA DAM IN KOLLAM
DISTRICT**

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹4.5 Cr
Agreed Amount With GST : Rs. 4,49,90,000.00
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 07-01-2022

Scheduled progress as on 16/10/2021 - 49%

Achieved progress as on 16/10/2021 - 29%

Last week progress in -3%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- SHOP (8.5%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (20%)
- Security cabin (2%)
- Toilet and cloak room (2%)

Works done in the last week

- Building renovation - lintel concrete work completed.
- Water tank foundation work & plinth work completed.
- Concreting of lintel for building Renovation
- Building renovation septic tank excavation completed
- Clearing site for toilet and security cabin
- Water tank cover slab reinforcement work in progress
- Pavilion excavation completed, foundation work in progress, Shuttering work of roof slab of shop completed, reinforcement



**ITI
DHANUVECHAPU
RAM
(KASE)**

**UPGRADATION OF GOVT. ITI
DHANUVECHAPURAM ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Heather Construction
Agreement date : 25-11-2019
Agreed Amount : ₹11.18 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration : 20 months
Scheduled Date of Completion :02-12-2021
Expected Date of completion :01-11-2021

Scheduled progress as on 16-10-2021- 92%

Achieved progress as on 16-10-2021 - 89.75%

Last week progress - 89.50%

Current week progress - 89.75%

Current Bill Status :8bill were passed, Amount up to 9th bill:61209828.93/-
,9th bill submitted amount:5991217.08/-

Current Financial Progress :54.74%

Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 95% completed
- GF primer work 92% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 60% completed
- FF Block Work 95% completed
- FF Ceiling work 70% completed
- FF plastering 93% completed
- Dummy column RCC completed
- FF Elec- concealed work 65% completed
- Parapet plastering 90% completed
- GF Tile work 60%
- FF primer work 80% completed

Works done in the last week

- Outside Plastering
- GF-Interior painting works.
- FF-Floor tile laying
- ELV works
- Car porch staircase concreting and column concreting.

