

# KIIDC WEEKLY PROGRESS REPORT



KIIDC



# PROJECTS IN KANNUR DISTRICT

**ITI KANNUR  
(KASE )**

**UPGRADATION OF GOVT. ITI  
KANNUR ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A  
Agreement date : 26-08-2020  
Agreed Amount :Rs.3,40,93,937.97  
Agreed Amount With GST : Rs.3,64,82,353.00  
Site Handover date : 04-09-2020  
Project duration : 8 months  
Scheduled Date of Completion : 03-05-2021  
Expected Date of completion :

**Scheduled progress as on 11-12-2021 100%**

**Achieved progress as on 11-12-2021 - 35%**

**Last week progress in 1%**

**Current week progress - 1%**

**Current Bill Status :1 st bill submitted**

**Current Financial Progress :12.6%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 96% completed
- 

**Works done in the last week**

- Main stair concreted
- Beam and slab shuttering done
- Soil compaction done.
- Beam reinforcement done.
- Slab and beam part 1 concrete completed.
- Column 2nd lift concreting.
- Dummy column concreting
- Beam and slab shuttering part 2
- Block work started part1



**RCB KUPPAM RIVER  
IN  
KOOVERY-KATTAM  
PALLY (KIIFB)**

**CONSTRUCTION OF  
REGULATOR CUM BRIDGE  
ACROSS KUPPAM RIVER IN  
KOOVERY-KATTAMPALLY IN  
CHAPPARAPADAVU  
PANCHAYAT , THALIPARAMBA  
TALUK, KANNUR DISTRICT**

**Name of contractor** : Infab Infrastructures Ltd  
**Agreement date** :15-10-2019  
**Agreed Amount** : ₹ 18,57,64,823.98  
**Agreed Amount With GST** : 22,03,74,512.96 (as per RE)  
**Site Handover date** : 07-11-2019  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 07-05-2021  
**Expected Date of completion** : NA

**Status of Work in terms of components:**

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

**Works done in the last week**

- Topographical, GPS Survey works for land acquisition works has been done at both banks

**Scheduled progress as on 11-12-2021 100%**

**Achieved progress as on 11-12-2021 - 0%**

**Last week progress in 0%**

**Current week progress - 0%**

**Current Bill Status :NA**

**Current Financial Progress :0%**

**Images of works done at Site during last week (with time stamp)**



**REGULATOR  
ANCHARAKANDY  
RIVER AT  
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF  
REGULATOR WITH LOCK  
ACROSS ANCHARAKANDY  
RIVER AT PARAPRAM IN  
PINARAYI PANCHAYATH,  
KANNUR DISTRICT**

Name of contractor : PGCC  
Agreement date :06-11-2020  
Agreed Amount : ₹44.49 Cr  
Agreed Amount With GST : Rs. 498,385,551.00  
Site Handover date : 16-11-2020  
Project duration : 18 months  
Scheduled Date of Completion : 15-05-2022  
Expected Date of completion : 15-05-2022

**Status of Work in terms of components:**

- Wing Wall (Left Bank U/S & D/S Retaining wall upto Apron portion): Completed.
- Pier P1 & P2: Pier Head Concreting completed.
- Abutment A1: 10th lift concreting (+8.40m).
- Foot slab: Left bank upto P2 completed.
- Stair case: Left Bank completed.

**Works done in the last week**

- LB U/S Retaining Wall: Base concreted upto Ch: 240m
- LB D/S Retaining Wall: Base concrete at Ch: upto 80m

**Scheduled progress as on 11-12-2021 19.5%**

**Achieved progress as on 11-12-2021 - 15.6**

**Last week progress in 15.5 %**

**Current week progress - 15.6%**

**Current Bill Status :First Part Bill submitted-Rs. 2,32,66,073.00**

**Current Financial Progress : 8.5%**

**Images of works done at Site during last week (with time stamp)**





# THALASSERY HERITAGE PROJECT (KIIFB-TOURIS M )

## PHASE -1 (14 no.of projects - 40.95 cr)

### **Agreement executed works:**

1. Andalurkavu
2. Jagannath Temple
3. Pindali Kalari
4. Kottiyoor temple
5. Illikunnu church
6. Lokanarkavu Temple
7. Makreri Subramanyaswami Temple

### **Selection notice issued works:**

- 1.Pazhassi Palace Kottayam Malabar
2. Thiruvangad Ramaswamy temple
3. Thirunelli Temple

### **Selection notice to be issued works:**

- 1.Thrissillery Temple

### **Work to be Retender:**

1. Odathil Mosque - Paris Hotel Street

### **Tender excess approval to be obtained from Government:**

1. Municipal Stadium
2. Kakkulangara Mosque

## PHASE -2 (14 no.of projects - 37.21 cr)

### **Selection notice issued works:**

- 1.Sree Thacholi Manikoth Temple
2. Vadakara Tazhe angadi
3. Peralassery Temple
4. Puralimala Temple
5. Chirakkakav temple
6. Thalakkal Chandu Museum - Panamaram

### **Work to be Retender:**

- 1.Pazhassi Smrithi Mandapam
2. Kadirur Surya Narayana Temple

### **Drawing revision required:**

1. Sree Mridanga Saileswari Temple
2. Thodeekalam Siva Temple
3. Sree Oorpazhachi Kavu Temple
4. Valliyoorkavu temple-Convention centre

### **NOC pending:**

1. Pazhassi Kovilakam (Mattannur)
2. Arakkal Kettu

## Agreement executed works - Phase - 1

### Issues:

- **Approved MoU received from Tourism department only on 28.09.2021. Forwarded to all concerned authorities, It is necessary as per KIIFB norms for starting the work**
- **MoU signed by owners for 4 works**
- **Consultant architect appointed by tourism department did not forwarded the GFC drawings due to issue in consultancy charges**

### Pindali Kalari

**AS amount** : 1.31 Cr  
**TS amount** : Rs. 0.725 Cr  
**Name of contractor** : M/s Classic Builders  
**Agreement date** : 17-02-2021  
**Agreed Amount** : ₹ 0.6238 Cr  
**Agreed Amount With GST** : Rs. 6987127.71  
**Project duration** : 12 months

**Status:** Agreement Executed , MoU signed - work started, GFC drawings issued

### Andalurkavu

**AS amount** : 1.69 Cr  
**TS amount** : Rs 1.51 Cr  
**Name of contractor** : Sri. Varkeychan  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.518 Cr  
**Agreed Amount With GST** : Rs. 1,70,11,777.6

**Project duration** : 12 months  
**Status:** Agreement Executed , MoU signed - work will start on 1st week of November, GFC drawings is being prepared by KIIFB

### Illikunnu church

**AS amount** : 2.47 Cr  
**TS amount** : 0.83 cr  
**Name of contractor** : Sri. Varkeychan  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 0.798 Cr  
**Agreed Amount With GST** : Rs. 89,38,493.08  
**Project duration** : 12 months

**Status:** Agreement Executed , MoU signed - work started, GFC drawings issued

**Lokanarkavu Temple**

**AS amount** : 6.69 Cr  
**TS amount** : Rs.3.91 Cr  
**Name of contractor** : M/s Saaj Constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 3.787 Cr  
**Agreed Amount With GST** : Rs.4,24,19,523.2  
**Project duration** : 12 months

**Status:** Agreement Executed , MoU given to temple authority, GFC drawings is being prepared by KIIDC

**Makreri Subramanyaswami Temple**

**AS amount** : 6.176 Cr  
**TS amount** : Rs 2.02 Cr  
**Name of contractor** : M/s Saaj constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 1.835 Cr  
**Agreed Amount With GST** : Rs. 2,05,52,642.3

**Project duration** : 12 months  
**Status:** Agreement Executed , MoU given to temple authority, GFC drawings is being prepared by KIIDC

**Jagannath Temple**

**AS amount** : 3.79 Cr  
**TS amount** : 1.56 Cr  
**Name of contractor** : Sri.Joseph R V  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.481 Cr  
**Agreed Amount With GST** : Rs. 1,65,96,091.2  
**Project duration** : 12 months

**Status:** Agreement Executed , MoU handed over to temple authority - work will start up on issuing GFC, GFC drawings is being prepared by KIIDC incorporating suggestions from temple authority

**Kottiyoor Temple - Tourist Amenities**

**AS amount** : 3.16 Cr  
**TS amount** : 1.78 Cr  
**Name of contractor** : Sri. Saji Varghese  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.749 Cr  
**Agreed Amount With GST** : Rs. 1,95,91,008.6

**Status:** Agreement Executed , MoU handed over to temple authority - Work will start after signing MoU

**Kottiyoor Temple - Streetscape**

**AS amount** : 2.27 Cr  
**TS amount** : 1.38 Cr  
**Name of contractor** : M/s Rubicon constructions  
**Agreement date** : 05-10-2021  
**Agreed Amount** : ₹ 1.21 Cr  
**Agreed Amount With GST** : Rs. 1,36,06,740.6

**Status:** Agreement Executed , MoU handed over to temple authority - Work will start after signing MoU

**NAME OF PROJECT :  
COMPREHENSIVE  
DEVELOPMENT OF  
MUZHAPPILANGAD AND  
DHARMADOM BEACH IN  
KANNUR DISTRICT**

**IN PRINCIPLE SANCTION : 233.71 Cr**

**FUNDING AGENCY : KIIFB**

**The whole project is divided into 4 Character areas**

**AS Amount for Character Area 1 : 52.541 Cr**

**AS DATE : 01/12/2020**

**TS DATE : TS not issued**

**Issues:**

- Design of sea wall was initially under the scope of Consultant architect CBRE who were appointed by Tourism Department and the design received from their side was not technically feasible for vetting, Accordingly the design of sea wall handed over to IIT Chennai and the same was received on 01.10.2021. DPR and estimate need to be resubmitted to KIIFB for approval

**Status:**

- KIIFB conditionally approved Character Area 1 for an amount of Rs.52.541 Cr. Final financial approval from KIIFB need to be obtained after meeting the conditions such as details of Structural Design of sea defense wall, Soil exploration and sedimentation study. Sea wall design received from IIT Chennai on 01.10.2021. The same is forwarded to CBRE for revising the Architectural drawings.

# **PROJECTS IN WAYANAD DISTRICT**

**KARAPUZHA PHASE  
III  
(TOURISM)**

**KARAPUZHA PHASE III  
CONSTRUCTION OF VIEWING  
TOWER, BAMBOO PAVILION  
AND BRIDGE**

Name of contractor : JAYAPRAKASHAN P  
Agreement date : 22/12/2017  
Agreed Amount : ₹ 7248330.00  
Agreed Amount With GST : Rs. 725000.00  
Site Handover date : 29/12/2017  
Project duration : 10 months  
Scheduled Date of Completion :29/10/2018  
Expected Date of completion :15/07/2021

**Status of Work in terms of components:**

- Viewing tower-100%
- Bamboo pavilion-100%
- Bridge.-100%

**Work done in last week**

Work completed.

**Scheduled progress as on 04-12-2021 100%**

**Achieved progress as on 04-12-2021 - 100%**


**Last week progress - completed**

**Current week progress - 0%**

**Final bill submitted**

**Current Financial Progress :60%**

**Images of works done at Site during last week (with time stamp)**

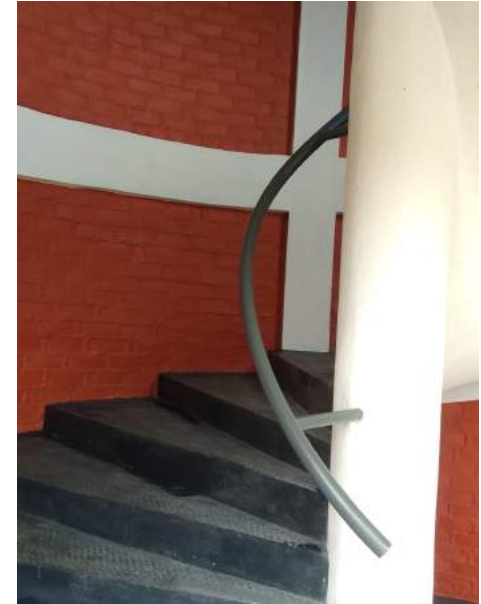

# PROJECTS IN KOZHIKODE DISTRICT



**ITI KOYILANDY  
(KASE)**

**UPGRADATION OF GOVT. ITI  
KOYILANDY ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.  
Agreement date : 14-08-2020  
Agreed Amount : ₹4.22 Cr  
Agreed Amount With GST : Rs. 4,22,86,606  
Site Handover date : 14-08-2020  
Project duration : 12 months  
Scheduled Date of Completion : 13-08-2021  
Expected Date of completion : 13-11-2021

**Scheduled progress as on 11-12-2021 - 100%**

**Achieved progress as on 11-12-2021 - 69%**

**Last week progress- 68%**

**Current week progress - 69%**

**Current Bill Status : CC 3rd and part submitted**

**Current Financial Progress : 34.3%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

**Works done in the last week**

- Main Building Civil works
- Main Building Plumbing works
- Smart classroom painting works



**PERUVANNAMOOZHI  
(TOURISM)**

**DEVELOPMENT OF  
PERUVANNAMOOZHI DAM  
TOURISM PROJECT IN  
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N  
Agreement date : 06-11-2020  
Agreed Amount : ₹ 26359270.97  
Agreed Amount With GST : Rs. 31388620.00  
Site Handover date : 13/11/2020  
Project duration : 9 months  
Scheduled Date of Completion : 12-08-2021  
Expected Date of completion : 30-09-2021

**Status of Work in terms of components:**

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate
- Open cafeteria.

**Works done in the last week**

- Childrens park-fixing childrens playing equipment
- Open cafeteria- truss work in progress completed.
- Interpretation center - painting works
- Carparking- levelling, earthwork for parking
- Walkway new step-plastering work in progress.
- Car parking-laying quarry waste

**Scheduled progress as on 11-12-2021 - 100%**

**Achieved progress as on 11-12-2021 - 95%**

**Last week progress in 50%**

**Current week progress in 50 %**

**Current Bill Status : 2nd bill-1,73,5877/-**

**Current Financial Progress :66%**

**Images of works done at Site during last week (with time stamp)**



**RCB  
PERINCHERIKADAVU  
(KIIFB)**

**CONSTRUCTION OF  
REGULATOR CUM BRIDGE AT  
U/S OF PERINCHERIKADAVU IN  
KUTTIADY RIVER  
(GULIKAPUZHA) AT  
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium  
Agreement date : 07-09-2020  
Agreed Amount : ₹ 6,11,33,413.18/-  
Agreed Amount With GST : ₹ 68,46,94,229/-  
Site Handover date : 17-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :16-03-2022  
Expected Date of completion :16-09-2022

Scheduled progress as on 11-12-2021 - 85%

Achieved progress as on 11-12-2021 - 8.5%

Last week progress in 8%

Current week progress 8.5%

Current Bill Status : NIL

Current Financial Progress : NIL

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- RCB – 6%
- Bank Protection works – 1%
- Material collection works are going on.( Coconut posts supplying)

**Works done in the last week**

- Boring for pile work
- RCC of pile
- Ring bund construction



**PROJECTS IN  
MALAPPURAM  
DISTRICT**

**Puzhankavu  
Regulator  
(KIIFB)**

**KIIFB Project - Construction of  
Regulator at Puzhankavu across  
Kadalundi River**



Name of contractor : Infab Infrastructure Pvt Ltd  
Agreement date : 17-12-2019  
Agreed Amount : ₹ 9,79,65,435.62  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 17-12-2019  
Project duration : 18 months  
Scheduled Date of Completion :16/06/2021  
Expected Date of completion :15/02/2022

**Status of Work in terms of components:**

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

**Works done in the last week**

- Ring bund formation.
- Earthwork excavation for left bank retaining wall for a length of 10m completed

**Scheduled progress as on 12-12-2021- 100 %**

**Achieved progress as on 12-12-2021 - 55%**

**Last week progress - 0%**

**Current week progress - 0 %**

**Current Bill Status : Total Bill submitted ₹3 Crores**

**Current Financial Progress in : 8.67%**

**Images of works done at Site during last week**



**RCB  
Moothikkayam  
(KIIFB)**

**KIIFB - Construction of Regulator  
cum Bridge across thoothapuzha  
keezhmurikadavu moothikkayam in  
moorkanad panchayath**

Name of contractor : M/s PGCC Pvt,Ltd  
Agreement date : 18/09/2020  
Agreed Amount : ₹57.56 Cr  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 26-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :26-03-2022  
Expected Date of completion :26/12/2022

**Status of Work in terms of components:**

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

**Works done in the last week**

- Work restarted
- Ring bund formation
- Earth work excavation for piers

**Scheduled progress as on 12-12-2021 - 61%**

**Achieved progress as on 12-12-2021 - 3%**

**Last week progress - 3%**

**Current week progress - 3%**

**Current Bill Status : First & part bill submitted – Rs 1.03 Cr**

**Current Financial Progress : 1.75%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA  
(KASE)**

**UPGRADATION OF GOVT. ITI  
MALAMPUZHA ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS  
Agreement date : 05/03/20  
Agreed Amount : ₹11,61,93,745/-  
Agreed Amount With GST : Rs. 13,01,36,994.40/-  
Site Handover date : 16/03/2020  
Project duration : 18 months  
Scheduled Date of Completion. : 05/09/2021  
Expected Date of completion. : 02/06/22

Scheduled progress as on 11/12/2021- 100%

Achieved progress as on 11/12/2021 - 52.5%

Last week progress - 51.5%

Current week progress- 52.5%

Current Bill Status : no of bill submitted - 4, amount:- 12655538

Current Financial Progress : 9.72%

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components

- Smart classroom window and ventilator fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

### Works done in the last week

- Ceiling plastering part 1 and part 2- 100% completed
- Grade slab work completed instru. workshop area.
- LGF roof slab shuttering under progress.
- LGF roof slab concreted.
- Lift area roof slab completed
- FF part 1 slab concreted



VADAKARAPALLY  
REGULATOR  
(KIIFB)

Construction of Regulator across Chittur  
Puzha at Vadakarapally Palathulli in  
Peruvembu Grama Panchayt in Palakkad  
District

**Name of contractor** : Poonam grah nirman Pvt ltd  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹18.95 Cr  
**Agreed Amount With GST** : Rs. 21,23,18,001.2  
**Site Handover date** : 12-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 12-07-2022  
**Expected Date of completion** : 12-07-2022

**Status of Work in terms of components:**

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(15m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 3 no of pier and 2nd Lift of 3 no of pier is completed
- Fabrication works for shutter of 5 nos is completed

**Works done in the last week**

- Mechanical fabrication work for shutter

**Scheduled progress as on 13/12/2021 - 60%**

**Achieved progress as on 13/12/2021 - 27%**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : 3rd bill submitted amount of 0.78 cr**

**Current Financial Progress : 17%**

**Images of works done at Site during last week**





**Moongilmada LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd  
Agreement date : 26-02-2021  
Agreed Amount : ₹33288750 Crores  
Agreed Amount With GST : Rs. 37283400/-  
Site Handover date : 26-02-2021  
Project duration : 12 months  
Scheduled Date of Completion :26-02-2022  
Expected Date of completion :31-08-2021

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

- Installation of Submain

**Scheduled progress as on 12/12/2021 - 76 %**

**Achieved progress as on 12/12/2021 - 59 %**

**Last week progress in : 57%**

**Current week progress : 2 %**

**Current Bill Status : Part Bill-1**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN THRISSUR DISTRICT

**ITI CHALAKUDY  
KIIFB-KASE**

**UP GRADATION OF GOVT ITI  
CHALAKUDY ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : Sidheek, M/S Sitco Associates

Agreement date : 28-10-2020

Agreed Amount : ₹ 7,47,51,405.13

Agreed Amount With GST : ₹ 8,37,21,573.74

Site Handover date : 06-11-2020

Project duration : 12 months

Scheduled Date of Completion : 05-11-2021

Expected Date of Completion :

### **Status of Work in terms of components:**

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

### **Works done in the**

#### **last week**

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

**Scheduled progress as on 11/12/2021 - 0 %**

**Achieved progress as on 11/12/2021 - 0 %**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN ERNAKULAM DISTRICT

**RCB  
KONOTHUPUZHA  
(KIIFB)**

**Construction of Regulator with  
lock across Konothupuzha at  
Puthenkavu in Udayamperoor  
Panchayath in Ernakulam  
District**

**Name of contractor** : Marymatha construction  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹24.36 Cr  
**Agreed Amount With GST** : Rs. 272,843,729.92  
**Site Handover date** : 14-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 13-07-2022  
**Expected Date of completion** :

**Status of Work in terms of components:**

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

**Works done in the last week**

The work restarted. But Rain and high water level in the river affected the work.

**Scheduled progress as on 11-12-2021 - 35 %**

**Achieved progress as on 11-12-2021- 4%**

**Last week progress - 4%**

**Current week progress - 4%**

**Current Bill Status : Nil**

**Current Financial Progress :0 %**

**Images of works done at Site during last week (with time stamp)**





**ANTHAKARATHO  
DU CANAL  
(KIIFB)**

**IMPROVEMENTS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY**

Name of contractor : Southern Tech  
Agreement date : 29-09-2018  
Agreed Amount : ₹8.35 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 08-10-2018  
Project duration :15 months  
Scheduled Date of Completion :07-01-2021  
Expected Date of completion :31-12-2021

**Scheduled progress as on 11-12-2021 - 95%**

**Achieved progress as on 11-12-2021 - 94.5%**

**Last week progress - 94.25%**

**Current week progress 94.5%**

**Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00**

**Current Financial Progress : 65%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Cleaning & desilting-completed
- Side protection work- 85%
- Road and walkway formation- 70%
- Fencing and Handrail work- 70%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%

**Works done in the last week**

- Pointing and pitching works for Rubble masonry completed
- Fixing angle iron post
- Tie beam for pile and slab cisting



**ELECTRICAL  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY—PROVIDING  
STREET LIGHTS ALONG THE  
PATHWAYS OF  
ANTHAKARATHODE**

Name of contractor : Essjay Electro links  
Agreement date : 31-12-2020  
Agreed Amount : ₹50.27 lakhs  
Agreed Amount With GST : Rs. 5630313.00  
Site Handover date : 10-01-2021  
Project duration : 5 months  
Scheduled Date of Completion : 30-05-2021  
Expected Date of completion : 31-12-2021

**Status of Work in terms of components:**

- Excavation and supply Laying of cable-75%
- Placing of lamp post, LED & feeder -75%
- Excavation and concreting-75%

**Works done in the last week**

- Pole painting, Plastering work for foundation and glanding works in progress
- The remaining works depends upon the civil work (pathway).

**Scheduled progress as on 11-12-2021- 85%**

**Achieved progress as on 11-12-2021- 79%**

**Last week progress - 78%**

**Current week progress 79%**

**Current Bill Status : Part Bill prepared**

**Current Financial Progress : 42%**

**Images of works done at Site during last week (with time stamp)**



**BEAUTIFICATION  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY–LANDSCAPING &  
ARBORICULTURE, CONSTRUCTION  
OF KIOSK AND TOILET AND  
OPERATION & MAINTENANCE FOR  
ONE YEAR**

**Name of contractor** : GRIDS,Digital Surveyors and  
Engineering Consultants  
**Agreement date** : 24-06-2021  
**Agreed Amount** : ₹76.62 lakhs  
**Agreed Amount With GST** : Rs. 8581690.00  
**Site Handover date** : 03-07-2021  
**Project duration** : 3 months  
**Scheduled Date of Completion** : 02-10-2021  
**Expected Date of completion** : 02-01-2022

**Status of Work in terms of components:**

- Landscaping & tress-0%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

**Works done in the last week**

.Brick work and plastering works for plantar box ( CH 320-500)

- The works depends upon the civil work (pathway).Unexpected rain affected work progress of walkway and beautification work.

**Scheduled progress as on 11-12-2021- 40%**

**Achieved progress as on 11-12-2021- 3%**

**Last week progress - 2%**

**Current week progress - 3%**

**Current Bill Status : NIL**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN IDUKKI DISTRICT

**ITI  
KATTAPPANA  
(KASE)**

**UP GRADATION OF GOVT ITI  
KATTAPPANA ON PAR WITH  
INTERNATIONAL  
STANDARDS**



**Name of contractor** : Anchanical constructions  
**Agreement date** : 16.10.2020  
**Agreed Amount** : Rs 4,76,87,560.83  
**Agreed Amount With GST** : Rs 5,34,10,068.1  
**Site Handover date** : 04-12-2019  
**Project duration** : 08 months  
**Scheduled Date of Completion** : 21-12-2021  
**Expected Date of completion** : 21-12-2021

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 100%
- Grade beam concrete- 100%
- Grade slab Concrete - 100%
- Roof beams and slab - 0%

Works done in the last week

- Column concreting
- Shuttering for FF beams and slab

**Scheduled progress as on 12.12.21- 93%**

**Achieved progress as on 12.12.21 - 40 %**

**Last week progress : 39%**

**Current week progress :40%**

**Current Bill Status : 2nd and part bill submitted**

**Current Financial Progress in %:NIL**

**Images of works done at Site during last week**



**PAVANATHMA  
COLLEGE  
MURIKKASSERY  
(RUSA )**

**RUSA II PROJECT -  
CONSTRUCTION-PAVANATHMA  
COLLEGE MURIKKASSERI,  
IDUKKI.**

Name of contractor : Anchanical constructions  
Agreement date : 02.12.2019  
Agreed Amount : Rs.79,00,000  
Agreed Amount With GST : Rs.93,22,000  
Site Handover date : 02-06-2020  
Project duration : 09 months  
Scheduled Date of Completion : 31-08-2021  
Expected Date of completion : 31-08-2021

**Status of Work in terms of components:**

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

**Works done in the last week**

- No works done.

**Scheduled progress as on 12.12.21 - 100%**

**Achieved progress as on 12.12.21 - 89%**

**Last week progress : 89%**

**Current week progress in : 89%**

**Current Bill Status : 2 Bills submitted, Rs. 54,77,389.30**

**Current Financial Progress : 69%**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – I  
(TOURISM)**

**ADDITIONAL WORK I OF ECO  
LODGE CONSTRUCTION AT  
IDUKKI (CONSTRUCTION OF  
APPROACH ROAD,RETAINING  
WALL,DRAIN AND STREET  
LIGHTING).**

**Name of contractor** : M/S VJ Raju and Co.  
**Agreement date** : 11-08-2020  
**Agreed Amount** : Rs.69,50,003.24  
**Agreed Amount With GST** : Rs. 77,84,003.36  
**Site Handover date** : 21-08-2020  
**Project duration** : 04 months  
**Scheduled Date of Completion** : 31-08-2021  
**Expected Date of completion** : 31-08-2021

**Status of Work in terms of components:**

- Interlocking pathway 100%
- Gate installation 100%
- Providing street lights - 100%
- Pathway concrete - 100%
- Retaining wall - 100 %

**Works done in the last week**

- Work completed

**Scheduled progress - 100%**

**Achieved progress - Work Completed**

**Current progress : 100%**

**Current Bill Status : 1 Bill submitted, RS 36,27,077.98.**

**Current Financial Progress : 52%**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – II  
(TOURISM)**

**ADDITIONAL WORK II OF ECO  
LODGE CONSTRUCTION AT  
IDUKKI (CONSTRUCTION OF  
PUMP HOUSE, SECURITY  
CABIN, SUMP TANK AND  
FENCING).**

Name of contractor : M/S VJ Raju and Co.  
Agreement date : 26.02.2021  
Agreed Amount : Rs.45,85,722  
Agreed Amount With GST : Rs. 77,84,003.36  
Site Handover date : 08-03-2021  
Project duration : 04 months  
Scheduled Date of Completion : 07-10-2021  
Expected Date of completion : 07-10-2021

**Status of Work in terms of components:**

- Pump house - 90%
- Security cabin - 90%
- Fencing - 80%
- Sump tank - 100%
- Plumbing, Electrical and other works - 55 %

**Works done in the last week**

- Rain delayed the work
- fencing
- Electrical works

**Scheduled progress as on 12.12.21- 100%**

**Achieved progress as on 12.12.21 - 97%**

**Last week progress : 98%**

**Current week progress : 99%**

**Current Bill Status : None.**

**Current Financial Progress : NIL**

**Images of works done at Site during last week**



PEERMADE  
GUEST HOUSE  
RENOVATION  
(TOURISM)

**UPGRADATION AND RENOVATION OF  
GOVT. GUEST HOUSE PEERMADE ,  
IDUKKI**



Name of contractor :SRI BIBY SCARIA  
Agreement date : 30-06-2020  
Agreed Amount : Rs.1,45,51,908.00  
Agreed Amount With GST : Rs. 1,71,71,251.44  
Site Handover date : 13-07-2020  
Project duration : 9 months  
Scheduled Date of Completion :13-04-2021  
Expected Date of completion : 13-11-2021

Scheduled progress as on 11-12-2021 - 80 %

Achieved progress as on 11-12-2021 - 41 %

Last week progress in % -35 %

Current week progress - 40%

Current Bill Status : 1st and part bill submitted RS-12,15,770 (with GST)

Current Financial Progress : 15%


Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Roofing works of guest house building is completed
- Roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building and Tiling works completed
- structure of meeting hall completed

**Works done in the last week**

- Wall plastering of meeting hall
- Excavation for water tank foundation
- Plumbing works of service building
- Tiling works of toilets
- Work stopped due to heavy rain

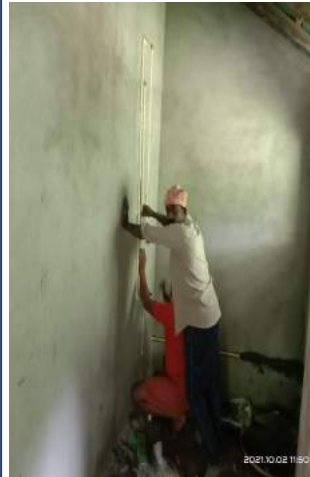

PANCHALIMEDU  
(TOURISM)

PANCHALIMEDU TOURISM PROJECT  
PHASE – 2  
PERUVANTHANAM VILLAGE,  
PEERMEDU TALUK, IDUKKI DISTRICT

Name of contractor : EASYINFRA INC, TVM  
Agreement date : 22/12/2020  
Agreed Amount : ₹2,43,99,440.78  
Agreed Amount With GST : Rs. 2,73,27,373.67  
Site Handover date : 01-01-2021  
Project duration : 12 months  
Scheduled Date of Completion : 31-12-2021  
Expected Date of completion : 31-12-2021

**Status of Work in terms of components:**

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

**Works done in the last week**

- Conducted Soil test for proposed check dam (standard penetration test)

**Scheduled progress as on 11-12-2021 - 50 %**

**Achieved progress as on 11-12-2021 - 17 %**

**Last week progress - 17 %**

**Current week progress - 17 %**

**Current Bill Status : 1st and part bill submitted Rs-16,68,292/-(with GST)**

**Current Financial Progress : 10 %**

**Images of works done at Site during last week (with time stamp)**



PEERMADE  
(TOURISM)

**CONSTRUCTION OF PARKING YARD,  
COMPOUND FENCING, SERVICE  
BLOCK, AMBIENT LIGHTING AND  
MODULAR KITCHEN AT ECOLODGE  
PEERMADE**

**Name of contractor** : Outlook communications pvt.ltd.  
**Agreement date** : 08-10-2021  
**Agreed Amount** : ₹80,27,681.98  
**Agreed Amount With GST** : Rs.9472664.74  
**Site Handover date** : 11-08-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :10-08-2022  
**Expected Date of completion** : 10-08-2022

**Scheduled progress as on 11-12-2021 - 10 %**

**Achieved progress as on 11-12-2021 - 10%**

**Last week progress - 11 %**

**Current week progress - 13 %**

**Current Bill Status : no bill submitted**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Foundation works of service building completed
- Foundation and basement works of security cabin completed
- Foundation and basement of generator room completed

**Works done in the last week**

- Brick work of service building upto lintel level completed
- Brick work of security cabin completed
- Lintel concrete of security cabin completed..



# **PROJECTS IN KOTTAYAM DISTRICT**

**ITI  
ETTUMANOOR  
(KASE)**

**UP GRADATION OF GOVT ITI  
ETTUMANOOR ON PAR WITH  
INTERNATIONAL STANDARDS**

Name of contractor : Swathy Construction

Agreement date : 30-07-2020

Agreed Amount : ₹ 6,95,25,557.81

Agreed Amount With GST : ₹ 7,78,68,624.74

Site Handover date : 10-08-2020

Project duration : 12 months

Scheduled Date of Completion : 09-08-2021

Expected Date of Completion : Within this Financial Year

Scheduled progress as on 11-12-2021- 100 %

Achieved progress as on 11-12-2021 - 79%

Last week progress - 77%

Current week progress - 2%

Current Bill Status : CC 5<sup>th</sup> and part is submitted (total : ₹74,74,040.49 (GST excluded))

Current Financial Progress : 54%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Main building civil works (72%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (20%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (35%)
- External lighting (0%)
- Fire protection works (20%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

**Works done in the last week - Main building civil works**

- Floor tile work.
- Tile Work on FF
- Electrical wiring and cable tray fixing works.
- Plumbing works
- Drain construction works.





**SIHM PALA  
(TOURISM)**

**SETTING UP OF STATE  
INSTITUTE OF HOTEL  
MANAGEMENT STUDIES AT  
PALA, KOTTAYAM DISTRICT,  
CONSTRUCTION OF ACADEMIC  
BLOCK**

Name of contractor : SITCO Associates  
Agreement date : 01-03-2016  
Agreed Amount : ₹13.48 Cr  
Site Handover date : 10-03-2016  
Project duration : 18 months  
Scheduled Date of Completion : 31/10/2017  
Expected Date of completion : 31/12/2021

**Status of Work in terms of components:**

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

**Works were done inEx the last week**

- No works have been done. Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.

**Scheduled progress as on 11-12-2021 - 90%**

**Achieved progress as on 11-12-2021 - 77%**

**Last week progress -77%**

**Current week progress - 0%**

**Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18**

**Current Financial Progress : 77 %**

**Images of works done at Site during last week (with time stamp)**



**CHEEPUNKAL  
(TOURISM)**

**KI IDC KUMARAKOM  
CHEEPUNKAL DESTINATION  
DEVELOPMENT PROJECT AT  
AYMANAM PANCHAYAT IN  
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1,19,66,517.41  
Agreed Amount With GST : ₹ 1,34,02,499.49  
Site Handover date : 05-05-2021  
Project duration : 12 months  
Scheduled Date of Completion : 04-05-2022  
Expected Date of Completion : 04-05-2022

**Status of Work in terms of components:**

- House Boat Jetty (22%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

**Works done in the last week**

- DRM works for the bank
- West side jetty, slab concerning works for about 30 m completed

Due to raised level of water level in river, because of heavy rain delayed work (13th October to 26th October)

**Scheduled progress as on 11-12-2021- 40%**

**Achieved progress as on 11-12-2021 - 30%**

**Last week progress - 21%**

**Current week progress - 9%**

**Current Bill Status : CC 1<sup>st</sup> and part bill will be submitted during the time of pile driving**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**



# **PROJECTS IN ALAPPUZHA DISTRICT**

**ITI  
CHENGANNUR  
(KASE)**

**UP-GRADATION OF GOVT ITI  
CHENGANNUR ON PAR WITH  
INTERNATIONAL  
STANDARDS - PHASE 1- REV 3**

**Name of contractor** : Creators Construction  
**Agreement date** : 15/10/2020  
**Agreed Amount** : Rs 18 Cr  
**Agreed Amount With GST** : Rs20,64,45672/-  
**Site Handover date** :23/10/2020  
**Project duration** :18 months  
**Scheduled Date of Completion** : 22/04/2022  
**Expected Date of completion** :22/3/2022

**Scheduled progress as on 11/12/2021 -70%**

**Achieved progress as on 11/12/2021 -Nil**

**Last week progress in - Nil**

**Current week progress in - Nil**

**Current Bill Status : (no: of bills submitted with amount) Nil**

**Current Financial Progress in %: Nil**

**Images of works done at Site during last week (with time stamp)- Nil**

**Status of Work in terms of components:**

- Main building civil works (0%)
- Existing class room converted to smart classrooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

**Works done in the**

**last week**

- Tree cutting approval have been obtained
- Tree cutting completed
- Levels of site had submitted to KIIFB



**ALAPPUZHA  
CANALS  
PHASE.01  
(KIIFB)**

**MODERNIZING WATER  
TRANSPORT IN ALAPPUZHA  
CANALS-PHASE 01**



Name of contractor : TBAS Construction, Aluva  
Agreement date : 15-02-2019  
Agreed Amount : ₹48.35 Cr  
Agreed Amount With GST : Rs. 54,15,71,596.79  
Site Handover date : 19-02-2019  
Project duration : 12 months  
Scheduled Date of Completion : 18-02-2020  
Expected Date of completion : 30-11-2021

Scheduled progress as on 04-12-2021 - 100%

Achieved progress as on 04-12-2021 - 99.5%

Last week progress in 99%

Current week progress- 0.50%

Current Bill Status : Rs.44,24,29,256.21 upto 5th bill

Current Financial Progress : 81.7%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Cleaning & Deepening of Canals after dewatering Completed
- RR Masonry side protection
  - Main Canals Completed
  - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
  - Culvert Structural Works Completed
  - Approach wall Under progress

**Works done in the last week**

- Water hyacinth removal at Town Canals
- PCC works for culvert approach
- GSB laying at culverts
- Paver Block laying at culverts



**PUNNAMADA  
(TOURISM WORK )**

**Punnamada- Starting Point  
Pathway and Boat Landing at  
Alappuzha District.**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.11 Cr  
Agreed Amount With GST : Rs. 1,23,77,355.31  
Site Handover date : 05-05-2021  
Project duration : 6 months  
Scheduled Date of Completion : 04-11-2021  
Expected Date of completion : 04-11-2021

**Status of Work in terms of components:**

- Pathway
- Solar Lighting

**Works done in the last week**

- Tie Beam, Cross beam concreting
- Backfilling with earth
- Construction of retaining walls near dock area

**Scheduled progress as on 11/12/2021- 60%**

**Achieved progress as on 11/12/2021 - 50%**

**Last week progress - 47%**

**Current week progress - 3%**

**Current Bill Status : NIL**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**



**CHUNGAM  
(TOURISM WORK )**

**CHUNGAM(CHAKREPURAKKAL)-  
KAYALCHIRA PATHWAY  
DEVELOPMENT AND BOAT  
LANDING BY THE SIDE OF  
PUNNAMADA RIVER, At  
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 2.99 Cr  
Agreed Amount With GST : Rs. 3,34,07,087.37  
Site Handover date : 05-05-2021  
Project duration : 9 months  
Scheduled Date of Completion : 04-02-2022  
Expected Date of completion : 04-02-2022

**Status of Work in terms of components:**

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

**Works done in the last week**

- Concrete Pile and slab casting
- Backfilling of earth
- Flooding of Canal bank roads delayed the backfilling activities
- 

**Scheduled progress as on 11/12/2021 - 60%**

**Achieved progress as on 11/12/2021 - 25%**

**Last week progress - 22%**

**Current week progress - 3%**

**Current Bill Status : NIL**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**



**GROYNES AT  
AMBALAPUZHA  
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP  
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at  
Ambalapuzha South, North panchayath and  
Punnapra South Panchayath**

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 51.3 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :29-01-2022  
**Expected Date of completion** :29-01-2022

**Status of Work in terms of components:**

- 20m groynes – 5 nos- 2 in progress
- 30M GROYNES -7nos- 2 in progress, 2 completed.
- 40M GROYNES – 9 nos - 6 in progress, 1 completed.
- 50M GROYNES – 9 nos -7 in progress, 2 completed.
- Sea wall length-305 m – not started
- 142552.66 MT boulders reached out of 178922 MT (79.67%)
- 2T TETRAPODS – 14996 nos. casted out of 23902 nos. (62.73%)
- 5T TETRAPODS – 1476 nos. casted out of 2956 nos.(49.93%)
- Earthwork Excavation – 19950 m3 completed out of 45955.7 M3 (43%)

**Works done in the last week**

- 2T tetrapod casted -377 nos
- 5T tetrapod casted -55 nos
- Supplying and Laying of Boulders 3869.99 MT
- laying of boulders for,G18,G30,G16 is in progress.
- Laying of tetrapods in G4,G5,G6 completed. Going on in G8,G22.

**Scheduled progress as on 11/12/2021 – 89 %**

**Achieved progress as on 11/12/2021 - 63.65 %**


**Last week progress - 1.72%**

**Current week progress - 1.710 %**

**Current Bill Status** :5 th bill submitted for an Amount of Rs. 5,44,55,630.02  
Total bill amount - Rs. 32,08,65,449.06

**Current Financial Progress : 62.5%**

**Images of works done at Site during last week (with time stamp)**

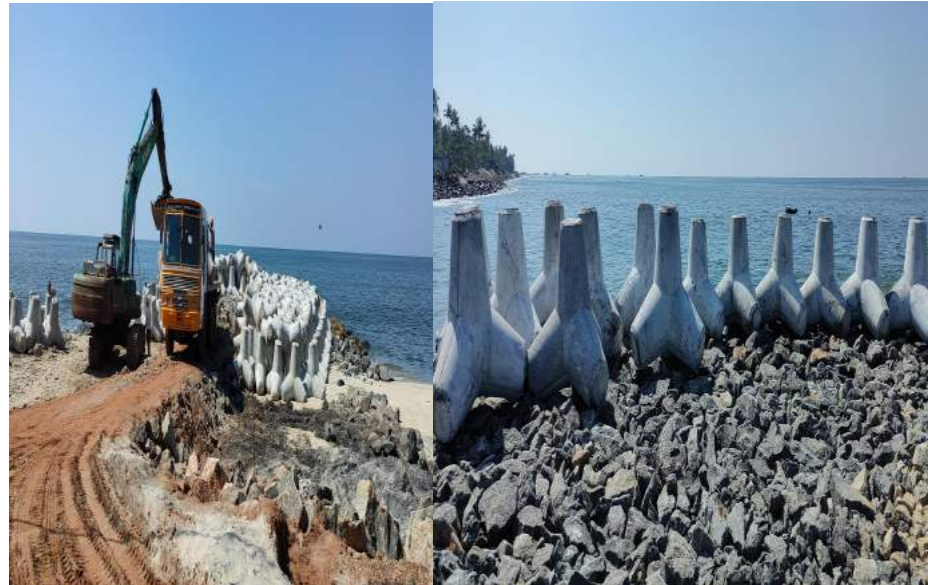

**GROYNES AT  
ARATTUPUZHA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
21NOS GROYNES AT  
ARATTUPUZHA IN BET.CH.56.6  
TO 57.8 KM AT ARATTUPUZHA**



**Name of contractor** : Ramalingam construction Company Pvt. Ltd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹ 26. 23Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :29-01-2022  
**Expected Date of completion** :29-05-2022

**Status of Work in terms of components:**

- 20M GROYNES - 6 NOS-Not started
- 25M GROYNES - 15 NOS-Not started
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 94497 MT
- 2T TETRAPODS -4488 (45.4 % ) nos casted out of 9874 NOS
- 5T TETRAPODS - 2385 NOS
- GEOMAT - 64739 M2
- EARTHWORK EXCAVATION - 3290 M3

**Works done in the last week**

- 2T tetrapod casted -195 nos.
- 5T tetrapod casting not started.
- Groyne work not yet started due to unavailability of boulders

**Scheduled progress as on 12/12/2021 - 89 %**

**Achieved progress as on 12/12/2021 - 11.8 %**

**Last week progress - 0.5 %**

**Current week progress - 0.5 %**

**Current Bill Status : 1 part bill submitted for an amount of Rs 1,32,65000**

**Current Financial Progress in % : 5 %**

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT  
PATHIYANKARA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
13NOS GROUYNE AT  
PATHIYANKARA IN BET.CH.60.1  
TO 61.6KM AT  
THRIKKUNNAPUZHA.**

Name of contractor : Ramalingam construction Company Pvt. Lmtd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹20.08Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion : 29-01-2022  
Expected Date of completion : 29-01-2022

**Status of Work in terms of components:**

1. 20M GROYNES - 2 NOS-One is completed
2. 30MGROYNES -4 NOS-One is completed and 2nos are in progress
3. 50M GROYNES - 7 NOS- started 4nos
- 4.45020.235MT boulders reached out of 74546 MT(60.39%)
5. 2T TETRAPODS -7278casted out of 8930NOS(81.50%)
6. 5T TETRAPODS - 934nos casted out of 1199NOS(77.89%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

**Works done in the last week**

- Tetrapod casting is in progress
- The total no.of tetrapods casted 2T-118& 5T-0nos
- laying of boulders for G4,G5,G6,G9,G11 are in progress
- Conveying of tetrapods at G3 is started .
- Groynes G1&G2 are completed
- Supplying and laying of boulders-1182.20MT

**Scheduled progress as on 12/12/2021 - 89%**

**Achieved progress as on 12/12/2021 -64.23%**

**Last week progress in - 1.5%**

**Current week progress in 2.04%**

**Current Bill Status : 5th part bills submitted for an amt of Rs 127824641.85**

**Current Financial Progress in : 63.64%**

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT.  
VATTACHAL  
(KIIFB)**

**KIIFB  
PROJECT – CONSTRUCTION OF  
16 NOS GROUYNE AT  
VATTACHAL IN BET. CH.53.4 TO  
CH.55.2 KM(1.8KM)  
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹28. 83Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :29-01-2022  
Expected Date of completion :29-05-2022

Scheduled progress as on 12/12/2021 - 89 %

Achieved progress as on 12/12/2021 - 27.5%

Last week progress - 1.00 %

Current week progress - 2 %

Current Status : 5 part bills submitted for an amt of Rs 7,62,61,445.30/-

Current Financial Progress in % : 26.4 %


Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 1 ongoing
- 30M GROYNES - 10 NOS- 3 ongoing
- 40M T GROYNE - 4 Nos - not started
- TOTAL QUANTITY OF BOULDERS - 11774.708 MT ( 11.6 % ) reached out of 101487 MT
- 2T TETRAPODS - 6202 ( 69.3 % ) nos casted out of 8941 NOS
- 5T TETRAPODS - 649 ( 19 % ) nos casted out of 3432 NOS
- GEOMAT - 2017.50 m<sup>2</sup> ( 2.6 % ) layed out of 76299 M<sup>2</sup>
- EARTHWORK EXCAVATION - done for G2, G3, G10 and G16 for ramp portion and groyne up to 20 m lngth (2970.2 out of 62380 M<sup>3</sup>)

### Works done in the last week

- 2T tetrapod casted - 195 nos.
- 5T tetrapod casted - 0nos.
- Supplying and Laying of Boulders - 1269.38 T
- Groyne G2 started - 601.5 m<sup>2</sup> geomat layed
- Excavation for G2 was done

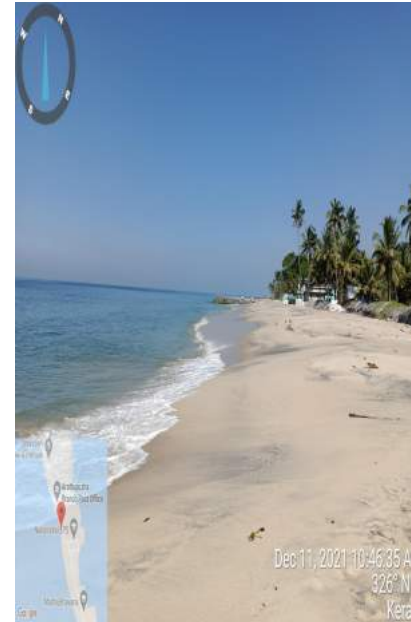

**GROYNES SITE AT  
KATTOOR  
(KIIFB)**

**Construction of 34 nos. Groyne  
at Kattoor from Ch.168.465KM  
TO CH 171.627KM (Old CH  
96.643KM TO CH 9.535 KM)**

**Name of contractor** : Ramalingam Construction  
Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 49.04 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Scheduled progress as on 12-12-2021 – 83 %**

**Achieved progress as on 12-12-2021 - 70%**

**Last week progress - 2.13%**

**Current week progress -2.00%**

**Current Bill Status** : 4 bill submitted for an Amount of Rs. 27,70,85,637/-

**Current Financial Progress : 68.94 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 20m groynes - 3 started out of 3
- 30m Groyne-4nos started out of 7
- 40m groyne - 17nos started out of 24
- Total boulders quantity - 104905.014MT boulders reached out of 174010MT(61%)
- 2T TETRAPODS – 20734nos (98%) casted out of 21562 nos.
- 5T TETRAPODS – 2648(88%) nos. casted out of 3144 nos.
- Geomat - 13517m2
- Earthwork Excavation - 31767.090m3 out of 42122 M3

**Works done in the last week**

- 2T tetrapod casted - 524nos.
- 5T tetrapod casted - 148nos.
- Supplying and Laying of Boulders 2642.01MT
- laying of boulders for, G18, G2, G3 are in progress.
- Laying of tetrapods at G13 and G14, G15 and G2 Groyne is progressing



# PROJECTS IN KOLLAM DISTRICT



**ITI CHANDANATHOPE  
(KASE)**

**UPGRADATION OF GOVT. ITI  
CHANDANATHOPE ON PAR  
WITH INTERNATIONAL  
STANDARDS**

Name of contractor : Asian Constructions  
Agreement date : 16-12-2020  
Agreed Amount : ₹3.65 Cr  
Agreed Amount With GST : Rs. 4,09,28,822.77  
Site Handover date : 24-12-2020  
Project duration : 8 months  
Scheduled Date of Completion : 23-08-2021  
Expected Date of completion : 30-04-2022

Scheduled progress as on 11/12/2021 - 100%

Achieved progress as on 11/12/2021 - 42%

Last week progress -2%

Current week progress - 1%

Current Bill Status : (no: of bills submitted with amount) - 1st bill submitted to KIIDC

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Main building civil works –50%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

**Works done in the last week**

- Dummy column concrete work under progress



**Thenmala  
(Tourism Project)**

**IMPROVEMENT AND  
DEVELOPING ECO-TOURISM AT  
THENMALA DAM IN KOLLAM  
DISTRICT**

Name of contractor : Tomy Vallamattom  
Construction  
Agreement date : 29-10-2020  
Agreed Amount : ₹4.5 Cr  
Agreed Amount With GST : Rs. 4,49,90,000.00  
Site Handover date : 09-11-2020  
Project duration : 15 months  
Scheduled Date of Completion : 08-02-2022  
Expected Date of completion : 07-01-2022

Scheduled progress as on 11/12/2021 - 49%

Achieved progress as on 11/12/2021 - 30%

Last week progress -3%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- SHOP (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)  
pavilion(50%)

**Works done in the last week**

1. Toilet, security room and cloak room-excavation Work completed. footing Work under progress.
2. Shed to shop -roof slab shuttering work under progress.



**ITI  
DHANUVECHAPU  
RAM  
(KASE)**

**UPGRADATION OF GOVT. ITI  
DHANUVECHAPURAM ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of contractor** : Heather Construction  
**Agreement date** : 25-11-2019  
**Agreed Amount** : ₹11.18 Cr  
**Agreed Amount With GST** : Rs. 12,52,34,417.4  
**Site Handover date** : 04-12-2019  
**Project duration** : 20 months  
**Scheduled Date of Completion** :03-04-2022  
**Expected Date of completion** :03-04-2022

**Scheduled progress as on 11-12-2021- 98.81%**

**Achieved progress as on 11-12-2021 - 91.65%**

**Last week progress - 91.60%**

**Current week progress - 91.65%**

**Current Bill Status** :11th bill were passed, Amount up to 11th bill:74791390.19/- ,11th bill submitted amount:6959620.11/-

**Current Financial Progress :66%**

### **Status of Work in terms of components:**

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 100% completed
- GF primer work 98% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 90% completed
- FF Block Work 98% completed
- FF Ceiling work 100% completed
- FF plastering 95% completed
- Dummy column RCC completed
- FF Elec- concealed work 80% completed
- Parapet plastering 100% completed
- GF Tile work 90%
- FF primer work 10% completed

### **Works done in the last week**

- GF-Interior painting works.
- FF-Floor tile laying
- ELV works
- 

