

KIIDC WEEKLY PROGRESS REPORT



KIIDC



PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

**UPGRADATION OF GOVT. ITI
KANNUR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount :Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion :

Scheduled progress as on 24-12-2021 100%

Achieved progress as on 24-12-2021 - 38%

Last week progress in 1%

Current week progress - 1%

Current Bill Status :1 st bill submitted

Current Financial Progress :12.6%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 96% completed
-

Works done in the last week

- Main stair concreted
- Beam reinforcement done.
- Slab and beam part 1 concrete completed.
- Beam and slab concrete completed part 2
- Block work started part1



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY (KIIFB)**

**CONSTRUCTION OF
REGULATOR CUM BRIDGE
ACROSS KUPPAM RIVER IN
KOOVERY-KATTAMPALLY IN
CHAPPARAPADAVU
PANCHAYAT , THALIPARAMBA
TALUK, KANNUR DISTRICT**

Name of contractor : Infab Infrastructures Ltd
Agreement date : 15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Status of Work in terms of components:

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

Works done in the last week

- Topographical, GPS Survey works for land acquisition works has been done at both banks

Scheduled progress as on 24-12-2021 100%

Achieved progress as on 24-12-2021 - 0%

Last week progress in 0%

Current week progress - 0%

Current Bill Status :NA

Current Financial Progress :0%

Images of works done at Site during last week (with time stamp)



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF
REGULATOR WITH LOCK
ACROSS ANCHARAKANDY
RIVER AT PARAPRAM IN
PINARAYI PANCHAYATH,
KANNUR DISTRICT**

Name of contractor : PGCC
Agreement date :06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion : 15-05-2022
Expected Date of completion : 15-05-2022

Status of Work in terms of components:

- Wing Wall (Left Bank U/S & D/S Retaining wall upto Apron portion): Completed.
- Pier P1 & P2: Pier Head Concreting completed.
- Abutment A1: 10th lift concreting (+8.40m).
- Foot slab: Left bank upto P2 completed.
- Stair case: Left Bank completed.

Works done in the last week

- LB U/S Retaining Wall: Base concreted upto Ch: 304m and wall upto Ch : 244m
- LB D/S Retaining Wall: Base concrete at Ch: upto 172.5m Wall concreted Ch: upto 112.5 m

Scheduled progress as on 24-12-2021 19.5%

Achieved progress as on 24-12-2021 - 17

Last week progress in 15.5 %

Current week progress - 15.6%

Current Bill Status :First Part Bill submitted-Rs. 2,32,66,073.00

Current Financial Progress : 8.5%

Images of works done at Site during last week (with time stamp)



THALASSERY HERITAGE PROJECT (KIIFB-TOURISM)

PHASE -1 (14 no.of projects - 40.95 cr)

Agreement executed works:

1. Andalurkavu
2. Jagannath Temple
3. Pindali Kalari
4. Kottiyoor temple
5. Illikunnu church
6. Lokanarkavu Temple
7. Makreri Subramanyaswami Temple

Selection notice issued works:

- 1.Pazhassi Palace Kottayam Malabar
2. Thiruvangad Ramaswamy temple
3. Thirunelli Temple

Selection notice to be issued works:

- 1.Thrissillery Temple

Work to be Retender:

1. Odathil Mosque - Paris Hotel Street

Tender excess approval to be obtained from Government:

1. Municipal Stadium
2. Kakkulangara Mosque

PHASE -2 (14 no.of projects - 37.21 cr)

Selection notice issued works:

- 1.Sree Thacholi Manikoth Temple
2. Vadakara Tazhe angadi
3. Peralassery Temple
4. Puralimala Temple
5. Chirakkakav temple
6. Thalakkal Chandu Museum - Panamaram

Work to be Retender:

- 1.Pazhassi Smrithi Mandapam
2. Kadirur Surya Narayana Temple

Drawing revision required:

1. Sree Mridanga Saileswari Temple
2. Thodeekalam Siva Temple
3. Sree Oorpazhachi Kavu Temple
4. Valliyoorkavu temple-Convention centre

NOC pending:

1. Pazhassi Kovilakam (Mattannur)
2. Arakkal Kettu

Agreement executed works - Phase - 1

Issues:

- Approved MoU received from Tourism department only on 28.09.2021. Forwarded to all concerned authorities, It is necessary as per KIIFB norms for starting the work
- MoU signed by owners for 4 works
- Consultant architect appointed by tourism department did not forwarded the GFC drawings due to issue in consultancy charges

Pindali Kalari

AS amount : 1.31 Cr
TS amount : Rs. 0.725 Cr
Name of contractor : M/s Classic Builders
Agreement date : 17-02-2021
Agreed Amount : ₹ 0.6238 Cr
Agreed Amount With GST : Rs. 6987127.71
Project duration : 12 months

Status: Agreement Executed , MoU signed - work started, GFC drawings issued

Andalurkavu

AS amount : 1.69 Cr
TS amount : Rs 1.51 Cr
Name of contractor : Sri. Varkeychan
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.518 Cr
Agreed Amount With GST : Rs. 1,70,11,777.6

Project duration : 12 months
Status: Agreement Executed , MoU signed - work will start on 1st week of November, GFC drawings is being prepared by KIIFB

Illikunnu church

AS amount : 2.47 Cr
TS amount : 0.83 cr
Name of contractor : Sri. Varkeychan
Agreement date : 26-02-2021
Agreed Amount : ₹ 0.798 Cr
Agreed Amount With GST : Rs. 89,38,493.08
Project duration : 12 months

Status: Agreement Executed , MoU signed - work started, GFC drawings issued

Lokanarkavu Temple

AS amount : 6.69 Cr
TS amount : Rs.3.91 Cr
Name of contractor : M/s Saaj Constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3.787 Cr
Agreed Amount With GST : Rs.4,24,19,523.2
Project duration : 12 months

Status: Agreement Executed , MoU given to temple authority, GFC drawings is being prepared by KIIDC

Makreri Subramanyaswami Temple

AS amount : 6.176 Cr
TS amount : Rs 2.02 Cr
Name of contractor : M/s Saaj constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 1.835 Cr
Agreed Amount With GST : Rs. 2,05,52,642.3

Project duration : 12 months
Status: Agreement Executed , MoU given to temple authority, GFC drawings is being prepared by KIIDC

Jagannath Temple

AS amount : 3.79 Cr
TS amount : 1.56 Cr
Name of contractor : Sri.Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.481 Cr
Agreed Amount With GST : Rs. 1,65,96,091.2
Project duration : 12 months

Status: Agreement Executed , MoU handed over to temple authority - work will start up on issuing GFC, GFC drawings is being prepared by KIIDC incorporating suggestions from temple authority

Kottiyoor Temple - Tourist Amenities

AS amount : 3.16 Cr
TS amount : 1.78 Cr
Name of contractor : Sri. Saji Varghese
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.749 Cr
Agreed Amount With GST : Rs. 1,95,91,008.6

Status: Agreement Executed , MoU handed over to temple authority - Work will start after signing MoU

Kottiyoor Temple - Streetscape

AS amount : 2.27 Cr
TS amount : 1.38 Cr
Name of contractor : M/s Rubicon constructions
Agreement date : 05-10-2021
Agreed Amount : ₹ 1.21 Cr
Agreed Amount With GST : Rs. 1,36,06,740.6

Status: Agreement Executed , MoU handed over to temple authority - Work will start after signing MoU

**NAME OF PROJECT :
COMPREHENSIVE
DEVELOPMENT OF
MUZHAPPILANGAD AND
DHARMADOM BEACH IN
KANNUR DISTRICT**

IN PRINCIPLE SANCTION : 233.71 Cr

FUNDING AGENCY : KIIFB

The whole project is divided into 4 Character areas

AS Amount for Character Area 1 : 52.541 Cr

AS DATE : 01/12/2020

TS DATE : TS not issued

Issues:

- Design of sea wall was initially under the scope of Consultant architect CBRE who were appointed by Tourism Department and the design received from their side was not technically feasible for vetting, Accordingly the design of sea wall handed over to IIT Chennai and the same was received on 01.10.2021. DPR and estimate need to be resubmitted to KIIFB for approval

Status:

- KIIFB conditionally approved Character Area 1 for an amount of Rs.52.541 Cr. Final financial approval from KIIFB need to be obtained after meeting the conditions such as details of Structural Design of sea defense wall, Soil exploration and sedimentation study. Sea wall design received from IIT Chennai on 01.10.2021. The same is forwarded to CBRE for revising the Architectural drawings.

PROJECTS IN WAYANAD DISTRICT

**KARAPUZHA PHASE
III
(TOURISM)**

**KARAPUZHA PHASE III
CONSTRUCTION OF VIEWING
TOWER, BAMBOO PAVILION
AND BRIDGE**

Name of contractor : JAYAPRAKASHAN P
Agreement date : 22/12/2017
Agreed Amount : ₹ 7248330.00
Agreed Amount With GST : Rs. 725000.00
Site Handover date : 29/12/2017
Project duration : 10 months
Scheduled Date of Completion : 29/10/2018
Expected Date of completion : 15/07/2021

Status of Work in terms of components:

- Viewing tower-100%
- Bamboo pavilion-100%
- Bridge.-100%

Work done in last week

Work completed.

Scheduled progress as on 04-12-2021 100%

Achieved progress as on 04-12-2021 - 100%

Last week progress - completed

Current week progress - 0%

Final bill submitted

Current Financial Progress :100%

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS
POONUR
PUZHA-POOLAKAD
AVU (KIIFB)**

**KIIFB PROJECT
CONSTRUCTION OF RCB
ACROSS POONUR PUZHA
NEAR KWA PUMPING HOUSE
AT POOLAKADAVU IN
KURUVATTOOR PANCHAYATH**

Name of contractor : ULCCS Ltd.
Agreement date : 18-08-2021
Agreed Amount : ₹22,68,45,702.29
Agreed Amount With GST : Rs.
Site Handover date : 27-08-2021
Project duration : 18 months
Scheduled Date of Completion :26-02-2023
Expected Date of completion :26-02-2023

Scheduled progress as on 24-12-2021 - 1%

Achieved progress as on 24-12-2021 - 1%

Last week progress- %

Current week progress - %

Current Bill Status : nil

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Initial levels for earth cutting has reported
- Steel liner for pile in progress
- Fusion bound epoxy tmt steel arrived at site,pile work in progress.

Works done in the last week

- Steel liner for pile in progress
- Fusion bound epoxy tmt steel arrived at site,pile work in progress
- Set out for pile points
-

**ITI KOYILANDY
(KASE)**

**UPGRADATION OF GOVT. ITI
KOYILANDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion : 13-08-2021
Expected Date of completion : 13-11-2021

Scheduled progress as on 24-12-2021 - 100%

Achieved progress as on 24-12-2021 - 69%

Last week progress- 68%

Current week progress - 69%

Current Bill Status : CC 3rd and part submitted

Current Financial Progress : 34.3%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

Works done in the last week

- Main Building Civil works
- Main Building Plumbing works
- Smart classroom painting works



**PERUVANNAMOOZHI
(TOURISM)**

**DEVELOPMENT OF
PERUVANNAMOOZHI DAM
TOURISM PROJECT IN
KOZHIKODE DISTRICT**

Name of contractor : AMEER ALI N
Agreement date : 06-11-2020
Agreed Amount : ₹ 26359270.97
Agreed Amount With GST : Rs. 31388620.00
Site Handover date : 13/11/2020
Project duration : 9 months
Scheduled Date of Completion : 12-08-2021
Expected Date of completion : 30-09-2021

Status of Work in terms of components:

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate
- Open cafeteria.

Works done in the last week

- Childrens park-fixing childrens playing equipment
- Open cafeteria- finishing work
- Walkway new step-plastering work in progress.
- Car parking-laying interlock work in progress
- Finishing works

Scheduled progress as on 24-12-2021 - 100%

Achieved progress as on 24-12-2021 - 97%

Last week progress in 50%

Current week progress in 50 %

Current Bill Status : 3rd bill-1,73,5877/-

Current Financial Progress :66%

Images of works done at Site during last week (with time stamp)



**RCB
PERINCHERIKADAVU
(KIIFB)**

**CONSTRUCTION OF
REGULATOR CUM BRIDGE AT
U/S OF PERINCHERIKADAVU IN
KUTTIADY RIVER
(GULIKAPUZHA) AT
KOZHIKODE DISTRICT**

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 6,11,33,413.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022
Expected Date of completion :16-09-2022

Scheduled progress as on 24-12-2021 - 85%

Achieved progress as on 24-12-2021 - 8.5%

Last week progress in 8%

Current week progress 8.5%

Current Bill Status : NIL

Current Financial Progress : NIL

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- RCB – 6%
- Bank Protection works – 1%
- Material collection works are going on.(Coconut posts supplying)

Works done in the last week

- Boring for pile work
- RCC of pile
- Ring bund construction



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

**KIIFB Project - Construction of
Regulator at Puzhankavu across
Kadalundi River**

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion :16/06/2021
Expected Date of completion :15/02/2022

Status of Work in terms of components:

- Two piers completed upto cut water portion.
- Two piers completed upto weir top portion
- Right Abutment completed up to Ground level.
- Left abutment completed up to 3.5m.
- Left side retaining wall 40m completed upto 2m height.
- Right side retaining wall completed.

Works done in the last week

- Ring bund formation.
- Foundation completed for 20m

Scheduled progress as on 20-12-2021- 100 %

Achieved progress as on 20-12-2021 - 55%

Last week progress - 0%

Current week progress - 0 %

Current Bill Status : Total Bill submitted ₹3 Crores

Current Financial Progress in : 8.67%

Images of works done at Site during last week



**RCB
Moothikkayam
(KIIFB)**

**KIIFB - Construction of Regulator
cum Bridge across thoothapuzha
keezhmurikadavu moothikkayam in
moorkanad panchayath**

Name of contractor : M/s PGCC Pvt,Ltd
Agreement date : 18/09/2020
Agreed Amount : ₹57.56 Cr
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 26-09-2020
Project duration : 18 months
Scheduled Date of Completion :26-03-2022
Expected Date of completion :26/12/2022

Status of Work in terms of components:

- 18 out of 64 piles completed
- Open footing 2 out of 6 completed
- pier first lift 2 out of 11 pier
- Raft of right abutment completed

Works done in the last week

- Work restarted
- Ring bund formation
- Foundation for two piers completed.

Scheduled progress as on 20-12-2021 - 61%

Achieved progress as on 20-12-2021 - 3%

Last week progress - 3%

Current week progress - 3%

Current Bill Status : First & part bill submitted – Rs 1.03 Cr

Current Financial Progress : 1.75%

Images of works done at Site during last week (with time stamp)



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA
(KASE)**

**UPGRADATION OF GOVT. ITI
MALAMPUZHA ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : M/S PERFECT ENGINEERS
Agreement date : 05/03/20
Agreed Amount : ₹11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date : 16/03/2020
Project duration : 18 months
Scheduled Date of Completion. : 05/09/2021
Expected Date of completion. : 02/06/22

Scheduled progress as on 24/12/2021- 100%

Achieved progress as on 24/12/2021 - 54%

Last week progress - 53%

Current week progress- 54%

Current Bill Status : no of bill submitted - 4, amount:- 19955538

Current Financial Progress : 14.81%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components

- Smart classroom window and ventilator fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

Works done in the last week

- Ceiling plastering part 1 and part 2- 100% completed
- Grade slab work completed instru. workshop area.
- LGF roof slab shuttering under progress.
- UGF column rising
- Lift area roof slab completed
- FF part 2 roof slab shuttering under progress



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-07-2022

Status of Work in terms of components:

- 6 no of open foundation out of 11 is completed
- 56 m of Apron is completed out of 130 m
- Works for Right side protection wall is ongoing(15m-50m)
- Protection wall raft 20 m to 55m is completed
- 1st Lift of 3 no of pier and 2nd Lift of 3 no of pier is completed
- Fabrication works for shutter of 5 nos is completed

Works done in the last week

- Mechanical fabrication work for shutter

Scheduled progress as on 27/12/2021 - 63%

Achieved progress as on 27/12/2021 - 27%

Last week progress - 1%

Current week progress - 1%

Current Bill Status : 3rd bill submitted amount of 0.78 cr

Current Financial Progress : 17%

Images of works done at Site during last week



**Moongilmada LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹33288750 Crores
Agreed Amount With GST : Rs. 37283400/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :26-02-2022
Expected Date of completion :31-08-2021

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

.Signal calibration
for Automation

Scheduled progress as on 16/12/2021 - 81 %

Achieved progress as on 16/12/2021 - 61 %

Last week progress in : 61%

Current week progress : 0 %

Current Bill Status : Part Bill-1

Current Financial Progress :

Images of works done at Site during last week (with time stamp)



PROJECTS IN THRISSUR DISTRICT

**ITI CHALAKUDY
KIIFB-KASE**

**UP GRADATION OF GOVT ITI
CHALAKUDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Sidheek, M/S Sitco Associates

Agreement date : 28-10-2020

Agreed Amount : ₹ 7,47,51,405.13

Agreed Amount With GST : ₹ 8,37,21,573.74

Site Handover date : 06-11-2020

Project duration : 12 months

Scheduled Date of Completion : 05-11-2021

Expected Date of Completion :

Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the

last week

- As per drawings building setbacks are not available in that site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

Scheduled progress as on 25/12/2021 - 0 %

Achieved progress as on 25/12/2021 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



PROJECTS IN ERNAKULAM DISTRICT

**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion :

Status of Work in terms of components:

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund dismantled(10%)
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

Works done in the last week

Construction of ring bund across river is under progress.

Scheduled progress as on 25-12-2021 - 35 %

Achieved progress as on 25-12-2021- 4%

Last week progress - 4%

Current week progress - 4%

Current Bill Status : Nil

Current Financial Progress :0 %

Images of works done at Site during last week (with time stamp)



**ANTHAKARATHO
DU CANAL
(KIIFB)**

**IMPROVEMENTS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY**

Name of contractor : Southern Tech
Agreement date : 29-09-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 08-10-2018
Project duration :15 months
Scheduled Date of Completion :07-01-2021
Expected Date of completion :31-12-2021

Status of Work in terms of components:

- Cleaning & desilting-completed
- Side protection work- 85%
- Road and walkway formation- 70%
- Fencing and Handrail work- 70%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%

Works done in the last week

- GI chain link fencing fabrication.
- Tie beam for precast pile and slab- shuttering and concreting.
- Skew bridge- Approach road formation

Scheduled progress as on 25-12-2021 - 95%

Achieved progress as on 25-12-2021 - 94.5%

Last week progress - 94.25%

Current week progress 94.5%

Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY—PROVIDING
STREET LIGHTS ALONG THE
PATHWAYS OF
ANTHAKARATHODE**

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 10-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 31-12-2021

Status of Work in terms of components:

- Excavation and supply Laying of cable-75%
- Placing of lamp post, LED & feeder -75%
- Excavation and concreting-75%

Works done in the last week

- Pole painting, Plastering work for foundation
- The remaining works depends upon the civil work (pathway).

Scheduled progress as on 25-12-2021- 85%

Achieved progress as on 25-12-2021- 80%

Last week progress - 79%

Current week progress 1%

Current Bill Status : Part Bill prepared

Current Financial Progress : 42%

Images of works done at Site during last week (with time stamp)



**BEAUTIFICATION
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY–LANDSCAPING &
ARBORICULTURE, CONSTRUCTION
OF KIOSK AND TOILET AND
OPERATION & MAINTENANCE FOR
ONE YEAR**

Name of contractor : GRIDS,Digital Surveyors and Engineering Consultants
Agreement date : 24-06-2021
Agreed Amount : ₹76.62 lakhs
Agreed Amount With GST : Rs. 8581690.00
Site Handover date : 03-07-2021
Project duration : 3 months
Scheduled Date of Completion : 02-10-2021
Expected Date of completion : 02-01-2022

Status of Work in terms of components:

- Landscaping & tress-0%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

Works done in the last week

.Brick work and plastering works for plantar box (CH 320-500)

- The works depends upon the civil work (pathway).Unexpected rain affected work progress of walkway and beautification work.

Scheduled progress as on 25-12-2021- 40%

Achieved progress as on 25-12-2021- 5%

Last week progress - 3%

Current week progress - 2%

Current Bill Status : NIL

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

**UP GRADATION OF GOVT ITI
KATTAPPANA ON PAR WITH
INTERNATIONAL
STANDARDS**

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 21-12-2021
Expected Date of completion : 21-12-2021

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 100%
- Grade beam concrete- 100%
- Grade slab Concrete - 100%
- Roof beams and slab - 45%

Works done in the last week

- Column concreting
Applied for time extension

Scheduled progress as on 26.12.21- 100%

Achieved progress as on 26.12.21 - 40 %

Last week progress : 42%

Current week progress :43%

Current Bill Status : 2nd and part bill submitted

Current Financial Progress in %:NIL

Images of works done at Site during last week



**PAVANATHMA
COLLEGE
MURIKKASSERY
(RUSA)**

**RUSA II PROJECT -
CONSTRUCTION-PAVANATHMA
COLLEGE MURIKKASSERI,
IDUKKI.**

Name of contractor : Anchanical constructions
Agreement date : 02.12.2019
Agreed Amount : Rs.79,00,000
Agreed Amount With GST : Rs.93,22,000
Site Handover date : 02-06-2020
Project duration : 09 months
Scheduled Date of Completion : 31-08-2021
Expected Date of completion : 31-08-2021

Status of Work in terms of components:

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed

Works done in the last week

- No works done.

Scheduled progress as on 26.12.21 - 100%

Achieved progress as on 26.12.21 - 89%

Last week progress : 89%

Current week progress in : 89%

Current Bill Status : 2 Bills submitted, Rs. 54,77,389.30

Current Financial Progress : 69%

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – I
(TOURISM)**

**ADDITIONAL WORK I OF ECO
LODGE CONSTRUCTION AT
IDUKKI (CONSTRUCTION OF
APPROACH ROAD,RETAINING
WALL,DRAIN AND STREET
LIGHTING).**

Name of contractor : M/S VJ Raju and Co.
Agreement date : 11-08-2020
Agreed Amount : Rs.69,50,003.24
Agreed Amount With GST : Rs. 77,84,003.36
Site Handover date : 21-08-2020
Project duration : 04 months
Scheduled Date of Completion : 31-08-2021
Expected Date of completion : 31-08-2021

Status of Work in terms of components:

- Interlocking pathway 100%
- Gate installation 100%
- Providing street lights - 100%
- Pathway concrete - 100%
- Retaining wall - 100 %

Works done in the last week

- Work completed

Scheduled progress - 100%

Achieved progress - Work Completed

Current progress : 100%

Current Bill Status : 1 Bill submitted, RS 36,27,077.98.

Current Financial Progress : 52%

Images of works done at Site during last week



18.09.2021
11.48 a.m.

**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – II
(TOURISM)**

**ADDITIONAL WORK II OF ECO
LODGE CONSTRUCTION AT
IDUKKI (CONSTRUCTION OF
PUMP HOUSE, SECURITY
CABIN, SUMP TANK AND
FENCING).**

Name of contractor : M/S VJ Raju and Co.
Agreement date : 26.02.2021
Agreed Amount : Rs.45,85,722
Agreed Amount With GST : Rs. 77,84,003.36
Site Handover date : 08-03-2021
Project duration : 04 months
Scheduled Date of Completion : 07-10-2021
Expected Date of completion : 07-10-2021

Status of Work in terms of components:

- Pump house - 90%
- Security cabin - 90%
- Fencing - 80%
- Sump tank - 100%
- Plumbing, Electrical and other works - 55 %

Works done in the last week

- Rain delayed the work
- fencing
- Electrical works

Scheduled progress as on 26.12.21- 100%

Achieved progress as on 26.12.21 - 97%

Last week progress : 98%

Current week progress : 99%

Current Bill Status : None.

Current Financial Progress : NIL

Images of works done at Site during last week



PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVT. GUEST HOUSE PEERMADE ,
IDUKKI**

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 13-11-2021

Scheduled progress as on 24-12-2021 - 80 %

Achieved progress as on 24-12-2021 - 41 %

Last week progress in % -35 %

Current week progress - 40%

Current Bill Status : 1st and part bill submitted RS-12,15,770 (with GST)

Current Financial Progress : 15%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Roofing works of guest house building is completed
- Roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building and Tiling works completed
- structure of meeting hall completed

Works done in the last week

- Excavation for water tank foundation
- Tiling works of toilets
- Foundation works of water tank
- Basement and plinth beam concrete of water tank



PANCHALIMEDU
(TOURISM)

PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAM VILLAGE,
PEERMEDU TALUK, IDUKKI DISTRICT

Name of contractor : EASYINFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : 31-12-2021

Status of Work in terms of components:

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

Works done in the last week

- Conducted Soil test for proposed check dam (standard penetration test)

Scheduled progress as on 24-12-2021 - 50 %

Achieved progress as on 24-12-2021 - 17 %


Last week progress - 17 %

Current week progress - 17 %

Current Bill Status : 1st and part bill submitted Rs-16,68,292/-(with GST)

Current Financial Progress : 10 %

Images of works done at Site during last week (with time stamp)

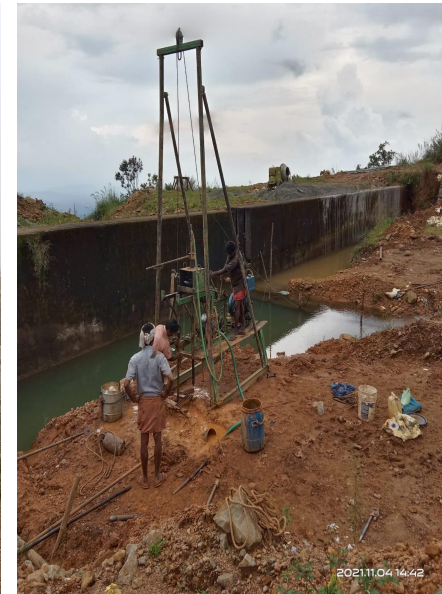

PEERMADE
(TOURISM)

**CONSTRUCTION OF PARKING YARD,
COMPOUND FENCING, SERVICE
BLOCK, AMBIENT LIGHTING AND
MODULAR KITCHEN AT ECOLODGE
PEERMADE**

Name of contractor : Outlook communications pvt.ltd.
Agreement date : 08-10-2021
Agreed Amount : ₹80,27,681.98
Agreed Amount With GST : Rs.9472664.74
Site Handover date : 11-08-2021
Project duration : 12 months
Scheduled Date of Completion :10-08-2022
Expected Date of completion : 10-08-2022

Scheduled progress as on 24-12-2021 - 10 %

Achieved progress as on 24-12-2021 - 10%

Last week progress - 13 %

Current week progress - 15 %

Current Bill Status : no bill submitted

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Foundation works of service building completed
- Foundation and basement works of security cabin completed
- Foundation and basement of generator room completed

Works done in the last week

- Lintel concrete of service building completed
- Roof concrete of security cabin completed
- Modular kitchen work started.
- Diesel generator placed



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

**UP GRADATION OF GOVT ITI
ETTUMANOOR ON PAR WITH
INTERNATIONAL STANDARDS**

Name of contractor : Swathy Construction
Agreement date : 30-07-2020
Agreed Amount : ₹ 6,95,25,557.81
Agreed Amount With GST : ₹ 7,78,68,624.74
Site Handover date : 10-08-2020
Project duration : 12 months
Scheduled Date of Completion : 09-08-2021
Expected Date of Completion : Within this Financial Year

Scheduled progress as on 24-12-2021- 100 %

Achieved progress as on 24-12-2021 - 82%

Last week progress - 80%

Current week progress - 2%

Current Bill Status : CC 5th and part is submitted (total : ₹74,74,040.49 (GST excluded))

Current Financial Progress : 54%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (72%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (20%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (35%)
- External lighting (0%)
- Fire protection works (20%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

Works were done in the last week - Main building civil works

- Electrical wiring.
- External Plumbing works
- Soak pit and waste put construction works.
- Road works



**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE
INSTITUTE OF HOTEL
MANAGEMENT STUDIES AT
PALA, KOTTAYAM DISTRICT,
CONSTRUCTION OF ACADEMIC
BLOCK**

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works were done inEx the last week

- No works have been done. Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.

Scheduled progress as on 24-12-2021 - 90%

Achieved progress as on 24-12-2021 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)



**CHEEPUNKAL
(TOURISM)**

**KI IDC KUMARAKOM
CHEEPUNKAL DESTINATION
DEVELOPMENT PROJECT AT
AYMANAM PANCHAYAT IN
KOTTAYAM DISTRICT**

Name of contractor : Sri Joseph R V
Agreement date : 26-02-2021
Agreed Amount : ₹ 1,19,66,517.41
Agreed Amount With GST : ₹ 1,34,02,499.49
Site Handover date : 05-05-2021
Project duration : 12 months
Scheduled Date of Completion : 04-05-2022
Expected Date of Completion : 04-05-2022

Status of Work in terms of components:

- House Boat Jetty (22%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

Works done in the last week

- Concrete curing works

Due to raised level of water level in river, because of heavy rain delayed work (13th October to 26th October)

Scheduled progress as on 24-12-2021- 45%

Achieved progress as on 24-12-2021 - 40%

Last week progress - 40%

Current week progress - 0%

Current Bill Status : CC 1st and part bill under preparation.

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR WITH
INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

Name of contractor : Creators Construction
Agreement date : 15/10/2020
Agreed Amount : Rs 18 Cr
Agreed Amount With GST : Rs20,64,45672/-
Site Handover date :23/10/2020
Project duration :18 months
Scheduled Date of Completion : 22/04/2022
Expected Date of completion :22/3/2022

Scheduled progress as on 27/12/2021 -70%

Achieved progress as on 27/12/2021 -Nil

Last week progress in - Nil

Current week progress in - Nil

Current Bill Status : (no: of bills submitted with amount) Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)- Nil

Status of Work in terms of components:

- Main building civil works (0%)
- Existing class room converted to smart classrooms (0%)
- Sump tank ,Front gate with security cabin civil works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

Works done in the

last week

- Tree cutting approval have been obtained
- Tree cutting completed
- Levels of site had submitted to KIIFB



**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

**MODERNIZING WATER
TRANSPORT IN ALAPPUZHA
CANALS-PHASE 01**

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-11-2021

Scheduled progress as on 04-12-2021 - 100%

Achieved progress as on 04-12-2021 - 99.5%

Last week progress in 99%

Current week progress- 0.50%

Current Bill Status : Rs.44,24,29,256.21 upto 5th bill

Current Financial Progress : 81.7%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Cleaning & Deepening of Canals after dewatering Completed
- RR Masonry side protection
 - Main Canals Completed
 - Sub Canals Under progress
- Pile&Slab protection work Completed
- Construction of culverts
 - Culvert Structural Works Completed
 - Approach wall Under progress

Works done in the last week

- Water hyacinth removal at Town Canals
- PCC works for culvert approach
- GSB laying at culverts
- Paver Block laying at culverts



**PUNNAMADA
(TOURISM WORK)**

**Punnamada- Starting Point
Pathway and Boat Landing at
Alappuzha District.**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 04-11-2021
Expected Date of completion : 04-11-2021

Status of Work in terms of components:

- Pathway
- Solar Lighting

Works done in the last week

- Tie Beam, Cross beam concreting
- Backfilling with earth
- Construction of retaining walls near dock area

Scheduled progress as on 26/12/2021- 60%

Achieved progress as on 26/12/2021 - 55%

Last week progress - 52%

Current week progress - 3%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)



**CHUNGAM
(TOURISM WORK)**

**CHUNGAM(CHAKREPURAKKAL)-
KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 04-02-2022

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- Backfilling of earth
- Flooding of Canal bank roads delayed the backfilling activities
-

Scheduled progress as on 26/12/2021 - 60%

Achieved progress as on 26/12/2021 - 27%

Last week progress - 25%

Current week progress - 2%

Current Bill Status : NIL

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)



9.494643229991198N 76.3554194290191E
Network time is not synchronized
Local: 22-Dec-2021 4:51:01 pm IST

**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-01-2022

Status of Work in terms of components:

- 20m groynes – 5 nos- 2 in progress
- 30M GROYNES -7nos- 2 in progress, 2 completed.
- 40M GROYNES – 9 nos - 6 in progress, 1 completed.
- 50M GROYNES – 9 nos -7 in progress, 2 completed.
- Sea wall length-305 m – not started
- 145867.563 MT boulders reached out of 178922 MT (81.52%)
- 2T TETRAPODS – 15436 nos. casted out of 23902 nos. (64.58%)
- 5T TETRAPODS – 1598 nos. casted out of 2956 nos.(54.05%)
- Earthwork Excavation – 19950 m3 completed out of 45955.7 M3 (43%)

Works done in the last week

- 2T tetrapod casted - nos
- 5T tetrapod casted - nos
- Supplying and Laying of Boulders -723.92 MT
- laying of boulders for,G29,G9,G7 is in progress (additional qty for G7,G9)
- Laying of tetrapods in G4,G5,G6 completed. Going on in G8,G22.

Scheduled progress as on 25/12/2021 – 89 %

Achieved progress as on 25/12/2021 - 65.622 %

Last week progress - 1.802%

Current week progress - 0.178%

Current Bill Status :5 th bill submitted for an Amount of Rs. 5,44,55,630.02
Total bill amount - Rs. 32,08,65,449.06

Current Financial Progress : 62.5%

Images of works done at Site during last week (with time stamp)



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹ 26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Status of Work in terms of components:

- 20M GROYNES - 6 NOS-Not started
- 25M GROYNES - 15 NOS-Not started
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 94497 MT
- 2T TETRAPODS -4709 (47.7%) nos casted out of 9874 NOS
- 5T TETRAPODS - 2385 NOS
- GEOMAT - 64739 M2
- EARTHWORK EXCAVATION - 3290 M3

Works done in the last week

- 2T tetrapod casted - 83 nos.
- 5T tetrapod casting not started.
- Groyne work not yet started due to unavailability of boulders

Scheduled progress as on 27/12/2021 - 89 %

Achieved progress as on 27/12/2021 - 12.5%

Last week progress - 0.2 %

Current week progress - 0.5 %

Current Bill Status : 2 part bill submitted for an amount of Rs 3,23,82,000/-

Current Financial Progress in % : 12.3 %

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of contractor : Ramalingam construction Company Pvt. Lmted.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-01-2022

Status of Work in terms of components:

1. 20M GROYNES - 2 NOS-One is complitd
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- started 4nos
- 4.50050.665MT boulders reached out of 74546 MT(67.1%)
5. 2T TETRAPODS -7573casted out of 8930NOS(84.8%)
6. 5T TETRAPODS - 934nos casted out of 1199NOS(77.89%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

Works done in the last week

- Tetrapod casting is in progress
- The total no.of tetrapods casted 2T-100& 5T-0nos
- laying of boulders forG4,G5,G6,G9,G11 are in progress
- Conveying of tetrapods at G5 is started .
- Groynes G1,G2&G3 are completed
- Supplying and laying of boulders-2748.61MT

Scheduled progress as on 25/12/2021 - 89%

Achieved progress as on 25/12/2021 -68.5%

Last week progress in - 2%

Current week progress in 2.2%

Current Bill Status : 5th part bills submitted for an amt of Rs 127824641.85

Current Financial Progress in : 63.64%

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Scheduled progress as on 27/12/2021 - 89 %

Achieved progress as on 27/12/2021 - 29.3%

Last week progress - 1.8 %

Current week progress - 2 %

Current Status : 5 part bills submitted for an amt of Rs 7,62,61,445.30/-

Current Financial Progress in % : 26.4 %


Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 ongoing
- 30M GROYNES - 10 NOS- 4 ongoing
- 40M T GROYNE - 4 Nos - not started
- TOTAL QUANTITY OF BOULDERS - 14875.5 MT (14.65 %) reached out of 101487 MT
- 2T TETRAPODS - 6508 (72.78%) nos casted out of 8941 NOS
- 5T TETRAPODS - 649 (19 %) nos casted out of 3432 NOS
- GEOMAT - 2935 m2 (3.8%) layed out of 76299 M2
- EARTHWORK EXCAVATION - done for G2, G3,G8, G9, G10 and G16 for ramp portion and groyne up to 15 m lngth (2970.2 out of 62380 M3)

Works done in the last week

- 2T tetrapod casted - 167 nos.
- 5T tetrapod casted - 0 nos.
- Supplying and Laying of Boulders - 3100.76 T
- Groyne G9 started 680 m2 geomat layed
- Excavation for G8 was done

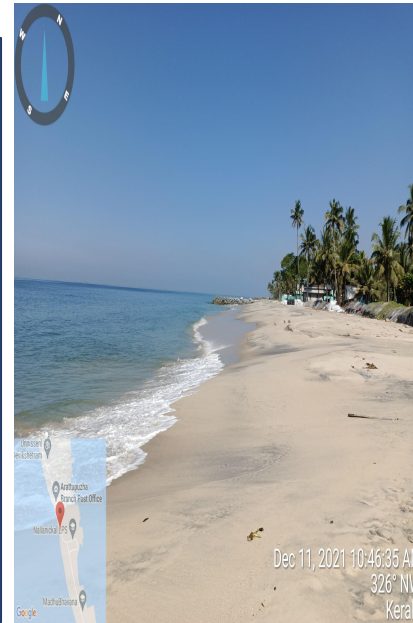

**GROYNES SITE AT
KATTOOR
(KIIFB)**

**Construction of 34 nos. Groyne
at Kattoor from Ch.168.465KM
TO CH 171.627KM (Old CH
96.643KM TO CH 9.535 KM)**

Name of contractor : Ramalingam Construction
Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 29-05-2022

Scheduled progress as on 25-12-2021 – 89 %

Achieved progress as on 25-12-2021 - 72%

Last week progress - 1.42%

Current week progress -0.5%

Current Bill Status : 4 bill submitted for an Amount of Rs. 27,70,85,637/-

Current Financial Progress : 68.94 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groyne - 3 started out of 3
- 30m Groyne-4nos started out of 7
- 40m groyne - 17nos started out of 24
- Total boulders quantity - 110395.45MT boulders reached out of 174010MT(63%)
- 2T TETRAPODS – 21553nos (99%) casted out of 21562 nos.
- 5T TETRAPODS – 3006(95%) nos. casted out of 3144 nos.
- Geomat - 13517m2
- Earthwork Excavation - 31767.090m3 out of 42122 M3

Works done in the last week

- 2T tetrapod casted - 95nos.
- 5T tetrapod casted - 98nos.
- Supplying and Laying of Boulders239.77MT
- laying of boulders for,G17are in progress.
- Laying of tetrapods at G13and G14,G15 and G2 Groyne is progressing



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion : 23-08-2021
Expected Date of completion : 30-04-2022

Scheduled progress as on 25/12/2021 - 100%

Achieved progress as on 25/12/2021 - 42.5%

Last week progress -2%

Current week progress - 1%

Current Bill Status : (no: of bills submitted with amount) - 1st bill submitted to KIIDC

Current Financial Progress in %: NIL

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works –50%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works – 0%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

- Dummy column concrete work completed



**Thenmala
(Tourism Project)**

**IMPROVEMENT AND
DEVELOPING ECO-TOURISM AT
THENMALA DAM IN KOLLAM
DISTRICT**

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹4.5 Cr
Agreed Amount With GST : Rs. 4,49,90,000.00
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 07-01-2022

Scheduled progress as on 25/12/2021 - 49%

Achieved progress as on 25/12/2021 - 30.5%

Last week progress -3%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- SHOP (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)
pavilion(50%)

Works done in the last week

1. Toilet, security room and cloak room-excavation Work completed.footing Work under progress.
2. Shed to shop -roof slab shuttering work under progress.
3. Pavilion-step Work progress



**ITI
DHANUVECHAPU
RAM
(KASE)**

**UPGRADATION OF GOVT. ITI
DHANUVECHAPURAM ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of contractor : Heather Construction
Agreement date : 25-11-2019
Agreed Amount : ₹11.18 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration : 20 months
Scheduled Date of Completion : 03-04-2022
Expected Date of completion : 03-04-2022

Scheduled progress as on 25-12-2021- 98.91%

Achieved progress as on 25-12-2021 - 91.80%

Last week progress - 91.70%

Current week progress - 91.80%

Current Bill Status :11th bill were passed, Amount up to 11th bill:74791390.19/- ,11th bill submitted amount:6959620.11/-

Current Financial Progress :66%

Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering 100% completed
- GF primer work 98% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 90% completed
- FF Block Work 98% completed
- FF Ceiling work 100% completed
- FF plastering 95% completed
- Dummy column RCC completed
- FF Elec- concealed work 80% completed
- Parapet plastering 100% completed
- GF Tile work 90%
- FF primer work 10% completed

Works done in the last week

- GF-Interior painting works.
- Handrail works
- FF-Brick works
- External plumbing works
-

