

# KIIDC WEEKLY PROGRESS REPORT



KIIDC



# **PROJECTS IN KANNUR DISTRICT**

**ITI KANNUR  
(KASE )**

# **UPGRADATION OF GOVT. ITI KANNUR ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: Joel J Varghese**

Name of contractor : Shameer M A  
Agreement date : 26-08-2020  
Agreed Amount :Rs.3,40,93,937.97  
Agreed Amount With GST : Rs.3,64,82,353.00  
Site Handover date : 04-09-2020  
Project duration : 8 months  
Scheduled Date of Completion : 03-05-2021  
Expected Date of completion : 17-05-2022

**Scheduled progress as on 02-04-2022 50%**

**Achieved progress as on 02-04-2022 20%**

**Last week progress in 25%**

**Current week progress - 25%**

**Current Bill Status :1 st bill submitted**

**Current Financial Progress :12.6%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Footing works 100 % completed
- Stub columns, Grade beam concreting 100% completed
- Ground floor columns concreting 100% completed
- Block Work 75%
- 

**Works done in the last week**

.Block work ongoing part 2  
Lintel Part 2 ongoing



**RCB KUPPAM RIVER  
IN  
KOOVERY-KATTAM  
PALLY (KIIFB)**

**CONSTRUCTION OF REGULATOR  
CUM BRIDGE ACROSS KUPPAM  
RIVER IN KOOVERY-KATTAMPALLY  
IN CHAPPARAPADAVU PANCHAYAT ,  
THALIPARAMBA TALUK, KANNUR  
DISTRICT**

**Name of Project Engineer: Akhil P A**

Name of contractor : Infab Infrastructures Ltd  
Agreement date : 15-10-2019  
Agreed Amount : ₹ 18,57,64,823.98  
Agreed Amount With GST : 22,03,74,512.96 (as per RE)  
Site Handover date : 07-11-2019  
Project duration : 18 months  
Scheduled Date of Completion : 07-05-2021  
Expected Date of completion : NA

**Status of Work in terms of components:**

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

**Works done in the last week**

- Topographical, GPS Survey works for land acquisition works has been done at both banks

**Scheduled progress as on 02-04-2022 100%**

**Achieved progress as on 02-04-2022 - 0%**

**Last week progress in 0%**

**Current week progress - 0%**

**Current Bill Status :NA**

**Current Financial Progress :0%**

**Images of works done at Site during last week (with time stamp)**



**REGULATOR  
ANCHARAKANDY  
RIVER AT  
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF  
REGULATOR WITH LOCK ACROSS  
ANCHARAKANDY RIVER AT  
PARAPRAM IN PINARAYI  
PANCHAYATH, KANNUR DISTRICT**

**Name of Project Engineer : Akhil P A**

Name of contractor : PGCC  
 Agreement date : 06-11-2020  
 Agreed Amount : ₹44.49 Cr  
 Agreed Amount With GST : Rs. 498,385,551.00  
 Site Handover date : 16-11-2020  
 Project duration : 18 months  
 Scheduled Date of Completion : 15-05-2022  
 Expected Date of completion : 15-05-2022

Scheduled progress as on 02-04-2022 90%

Achieved progress as on 02-04-2022 - 43%

Last week progress in 1 %

Current week progress - 0.5%

Current Bill Status : Fourth Part Bill submitted

Current Financial Progress : 29%


Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- eWing Wall (Left Bank U/S & D/S Retaining wall upto Apron portion): Completed.
- Pier P1 & P2: Pier Head Concreting completed.
- Abutment A1: 10th lift concreting (+8.40m).
- Foot slab: Left bank upto P2 completed.
- Stair case: Left Bank completed.

**Works done in the last week**

- Main Regulator pile are reached 100%
- Retaining wall at D/S pile work progressing.
- P5 lock line pile cap concrete completed.
- Apron between P3 and P4 reached 75%
- Lock wall Concrete progressing at P3 line.





# THALASSERY HERITAGE PROJECT (KIIFB-TOURIS M )

## PHASE -1 (14 no.of projects - 40.95 cr)

### **Agreement executed works:**

1. Andalurkavu
2. Jagannath Temple
3. Pindali Kalari
4. Kottiyoor temple
5. Illikunnu church
6. Lokanarkavu Temple
7. Makreri Subramanyaswami Temple

### **Selection notice issued works:**

- 1.Pazhassi Palace Kottayam Malabar
2. Thiruvangad Ramaswamy temple
3. Thirunelli Temple

### **Selection notice to be issued works:**

- 1.Thrissillery Temple

### **Work to be Retender:**

1. Odathil Mosque - Paris Hotel Street

### **Tender excess approval to be obtained from Government:**

1. Municipal Stadium
2. Kakkulangara Mosque

## PHASE -2 (14 no.of projects - 37.21 cr)

### **Selection notice issued works:**

- 1.Sree Thacholi Manikoth Temple
2. Vadakara Tazhe angadi
3. Peralassery Temple
4. Puralimala Temple
5. Chirakkakav temple
6. Thalakkal Chandu Museum - Panamaram

### **Work to be Retender:**

- 1.Pazhassi Smrithi Mandapam
2. Kadirur Surya Narayana Temple

### **Drawing revision required:**

1. Sree Mridanga Saileswari Temple
2. Thodeekalam Siva Temple
3. Sree Oorpazhachi Kavu Temple
4. Valliyoorkavu temple-Convention centre

### **NOC pending:**

1. Pazhassi Kovilakam (Mattannur)
2. Arakkal Kettu

## Agreement executed works - Phase - 1

### Issues:

- Approved MoU received from Tourism department only on 28.09.2021. Forwarded to all concerned authorities, It is necessary as per KIIFB norms for starting the work
- MoU signed by owners for 4 works
- Consultant architect appointed by tourism department did not forwarded the GFC drawings due to issue in consultancy charges

### Pindali Kalari

**AS amount** : 1.31 Cr  
**TS amount** : Rs. 0.725 Cr  
**Name of contractor** : M/s Classic Builders  
**Agreement date** : 17-02-2021  
**Agreed Amount** : ₹ 0.6238 Cr  
**Agreed Amount With GST** : Rs. 6987127.71  
**Project duration** : 12 months  
**Status:** Work started

### Andalurkavu

**AS amount** : 1.69 Cr  
**TS amount** : Rs 1.51 Cr  
**Name of contractor** : Sri. Varkeychan  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.518 Cr  
**Agreed Amount With GST** : Rs. 1,70,11,777.6  
**Project duration** : 12 months  
**Status:** Work started

### Illikunnu church

**AS amount** : 2.47 Cr  
**TS amount** : 0.83 cr  
**Name of contractor** : Sri. Varkeychan  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 0.798 Cr  
**Agreed Amnt With GST**: Rs. 89,38,493.08  
**Project duration** : 12 months  
**Status:** Work started

**Lokanarkavu Temple**

**AS amount** : 6.69 Cr  
**TS amount** : Rs.3.91 Cr  
**Name of contractor** : M/s Saaj Constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 3.787 Cr  
**Agreed Amount With GST** : Rs.4,24,19,523.2  
**Project duration** : 12 months

**Status:** Agreement Executed , MoU given to temple authority, GFC drawings is being prepared by KIIDC

**Makreri Subramanyaswami Temple**

**AS amount** : 6.176 Cr  
**TS amount** : Rs 2.02 Cr  
**Name of contractor** : M/s Saaj constructions  
**Agreement date** : 17-06-2021  
**Agreed Amount** : ₹ 1.835 Cr  
**Agreed Amount With GST** : Rs. 2,05,52,642.3  
**Project duration** : 12 months

**Status:** Agreement Executed , MoU given to temple authority, GFC drawings is being prepared by KIIDC

**Jagannath Temple**

**AS amount** : 3.79 Cr  
**TS amount** : 1.56 Cr  
**Name of contractor** : Sri.Joseph R V  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.481 Cr  
**Agreed Amount With GST** : Rs. 1,65,96,091.2  
**Project duration** : 12 months

**Status:** Work started

**Kottiyoor Temple - Tourist Amenities**

**AS amount** : 3.16 Cr  
**TS amount** : 1.78 Cr  
**Name of contractor** : Sri. Saji Varghese  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.749 Cr  
**Agreed Amount With GST** : Rs. 1,95,91,008.6

**Status:** Agreement Executed , MoU handed over to temple authority - Work will start after signing MoU

**Kottiyoor Temple - Streetscape**

**AS amount** : 2.27 Cr  
**TS amount** : 1.38 Cr  
**Name of contractor** : M/s Rubicon constructions  
**Agreement date** : 05-10-2021  
**Agreed Amount** : ₹ 1.21 Cr  
**Agreed Amount With GST** : Rs. 1,36,06,740.6

**Status:** Work started

**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT - THALASSERY  
HERITAGE PROJECT - PHASE 1  
-Pazhassi Circuit - Pindali Kalari  
House(Pathway,Conservation of  
Kalarithara,Pond restoration ,Seating,  
Landscaping ,Electrification)at  
Iritty,Kannur**

**Name of Project Engineer:Joel J Varghese**

Name of contractor : M/s Classic Builders  
Agreement date : 17-02-2021  
Agreed Amount : ₹ 0.6238 Cr  
Agreed Amount With GST : Rs. 6987127.71  
Site Handover date :  
Project duration : 12 months  
Scheduled Date of Completion : 27-02-2022  
Expected Date of completion :

Scheduled progress as on 02-04-2022 : 50%

Achieved progress as 02-04-2022 - 25%

Last week progress - 25%

Current week progress -30%

Current Bill Status : Ready for Part 1 bill

Current Financial Progress : 23%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of Work done in last week : setting up kalarithara basement and laying of MS Post**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 - Cultural Circuit -Andalur Kavvu**

**Name of Project Engineer: Akhil P A**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.5189 Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 1.701 Cr  
Project duration : 12 months  
Scheduled Date of Completion : 26-02-2022  
Expected Date of completion :

**Status of Work in terms of components:**

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

**Work done in last week**

- Sadrahalli stone pavement progressing

**Scheduled progress as on 02-04-2022 : 100%**

**Achieved progress as 02-04-2022 - 17 %**

**Last week progress - 1%**

**Current week progress -%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -illikunnu**

**Name of Project Engineer: Akhil P A**



Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26/02/2021  
Agreed Amount : ₹ 8300000  
Agreed Amount With GST : Rs  
Site Handover date :  
Project duration : 12 months  
Scheduled Date of Completion : 26/02/2022  
Expected Date of completion :

**Status of Work in terms of components of cemetery :**

- Land scaping of cemetery area
- Lighting
- Conservation of ceiling, wood work, joinery

**Work done in last week**

- Compound laterite work in progressing
- Excavation done for the GSB laying

**Scheduled progress as on 02-04-2022 : 100%**

**Achieved progress as 02-04-2022 - 25%**

**Last week progress - 1%**

**Current week progress -1%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -Jaganath Temple**

**Name of Project Engineer: Akhil P A**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26/02/2021  
Agreed Amount : ₹ 1,48,17,938.56  
Agreed Amount With GST : 1.56cr

Site Handover date : 08/03/2021  
Project duration : 12 months  
Scheduled Date of Completion : 08/03/2022  
Expected Date of completion :

**Status of Work in terms of components :**

- Pathway
- Rivival of pond
- Compound wall
- Landscaping

**Work done in last week**  
**Compound laterite work in progressing**

- GSB work progressing for pathway
- Sadrahalli stone laying progressing

**Scheduled progress as on 02-04-2022 : 100%**

**Achieved progress as 02-04-2022 - 15%**

**Last week progress - 0%**

**Current week progress -1%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT –THALASSERY HERITAGE  
PROJECT-PHASE 1-pazhassi circuit –kottiyoor  
shiva  
temple(streetscape,landscaping,agrashala,car  
parking,stage and electrical work at kottiyoor  
shiva temple in irrity,Kannur district)**

**Name of Project Engineer:Basil George**

Name of contractor : M/s Rubicon construction  
Agreement date : 05/10/2021  
Agreed Amount : ₹ 1.21 cr  
Agreed Amount With GST : RS 1,36,06,740.60  
Site Handover date : 22/11/2021  
Project duration : 12 months  
Scheduled Date of Completion : 27-10-2022  
Expected Date of completion : 27/10/2022

**Status of Work in terms of components:**

- Streetscape
- Landscaping
- Agrashala
- Car parking
- Stage
- electrification

**Work done in last week**

Ootupura-foundation work in progress  
Laying narasapuram stone-streetscape work  
Exposed laterite masonry work-stage

**Scheduled progress as on 02-04.2022 : 60%**

**Achieved progress as 02-04-2022 - 45%**

**Last week progress - 30%**

**Current week progress -30%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**NAME OF PROJECT :  
COMPREHENSIVE  
DEVELOPMENT OF  
MUZHAPPILANGAD AND  
DHARMADOM BEACH IN  
KANNUR DISTRICT**

**IN PRINCIPLE SANCTION : 233.71 Cr**

**FUNDING AGENCY : KIIFB**

**The whole project is divided into 4 Character areas**

**AS Amount for Character Area 1 : 52.541 Cr**

**AS DATE : 01/12/2020**

**TS DATE : TS not issued**

**Issues:**

- Design of sea wall was initially under the scope of Consultant architect CBRE who were appointed by Tourism Department and the design received from their side was not technically feasible for vetting, Accordingly the design of sea wall handed over to IIT Chennai and the same was received on 01.10.2021. DPR and estimate need to be resubmitted to KIIFB for approval

**Status:**

- KIIFB conditionally approved Character Area 1 for an amount of Rs.52.541 Cr. Final financial approval from KIIFB need to be obtained after meeting the conditions such as details of Structural Design of sea defense wall, Soil exploration and sedimentation study. Sea wall design received from IIT Chennai on 01.10.2021. The same is forwarded to CBRE for revising the Architectural drawings.

# **PROJECTS IN WAYANAD DISTRICT**

**KARAPUZHA PHASE  
III  
(TOURISM)**

**KARAPUZHA PHASE III  
CONSTRUCTION OF VIEWING  
TOWER, BAMBOO PAVILION  
AND BRIDGE**

**Name of Project Engineer: Basil George**



Name of contractor : JAYAPRAKASHAN P  
Agreement date : 22/12/2017  
Agreed Amount : ₹ 7248330.00  
Agreed Amount With GST : Rs. 725000.00  
Site Handover date : 29/12/2017  
Project duration : 10 months  
Scheduled Date of Completion : 29/10/2018  
Expected Date of completion : 15/07/2021

**Status of Work in terms of components:**

- Viewing tower-100%
- Bamboo pavilion-100%
- Bridge.-100%

**Work done in last week**

Work completed.

**Scheduled progress as on 04-12-2021 100%**

**Achieved progress as on 04-12-2021 - 100%**


**Last week progress - completed**

**Current week progress - 0%**

**Final bill submitted**

**Current Financial Progress :100%**

**Images of works done at Site during last week (with time stamp)**

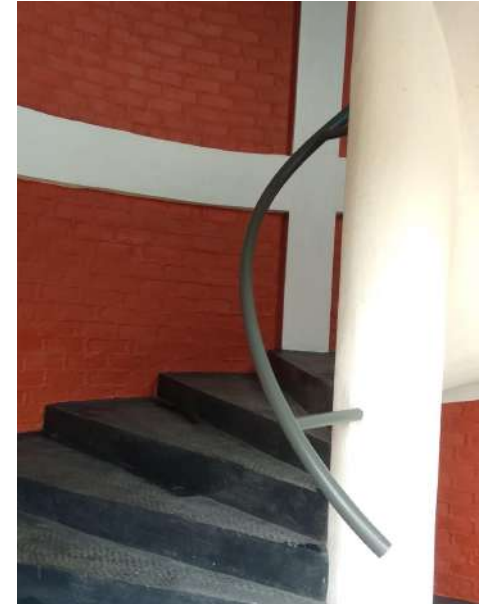

# PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS  
POONUR  
PUZHA-POOLAKAD  
AVU (KIIFB)**

**KIIFB PROJECT CONSTRUCTION  
OF RCB ACROSS POONUR PUZHA  
NEAR KWA PUMPING HOUSE AT  
POOLAKADAVU IN KURUVATTOOR  
PANCHAYATH**

**Name of Project Engineer: Athul Ashar**

Name of contractor : ULCCS Ltd.  
Agreement date : 18-08-2021  
Agreed Amount : ₹22,68,45,702.29  
Agreed Amount With GST : Rs.  
Site Handover date : 27-08-2021  
Project duration : 18 months  
Scheduled Date of Completion : 26-02-2023  
Expected Date of completion : 26-02-2023

**Status of Work in terms of components:**

- 33 no of pile foundation is completed out of 48

**Works done in the last week**

- Piling work for P1,P2 & P3 are complete
- Piling work for A1 & A2 are ongoing
- Land survey for acquisition purpose is completed.

**Scheduled progress as on 02-04-2022 - 25%**

**Achieved progress as on 02-04-2022- 10%**

**Last week progress- 2 %**

**Current week progress - 1 %**

**Current Bill Status : nil**

**Current Financial Progress : nil**

**Images of works done at Site during last week (with time stamp)**



**ITI KOYILANDY  
(KASE)**

**UPGRADATION OF GOVT. ITI  
KOYILANDY ON PAR WITH  
INTERNATIONAL STANDARDS**

**Name of Project Engineer: Basil George**

Name of contractor : ULCCS Ltd.  
Agreement date : 14-08-2020  
Agreed Amount : ₹4.22 Cr  
Agreed Amount With GST : Rs. 4,22,86,606  
Site Handover date : 14-08-2020  
Project duration : 12 months  
Scheduled Date of Completion :13-08-2021  
Expected Date of completion :13-11-2021

**Status of Work in terms of components:**

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

**Works done in the last week**

- Work delayed

**Scheduled progress as on 02-04-2022- 100%**

**Achieved progress as on 02-04-2022 - 85%**

**Last week progress- 0%**

**Current week progress - 0%**

**Current Bill Status : CC 3rd and part submitted**

**Current Financial Progress : 34.3%**

**Images of works done at Site during last week (with time stamp)**



**PERUVANNAMOOZHI  
(TOURISM)**

**DEVELOPMENT OF  
PERUVANNAMOOZHI DAM  
TOURISM PROJECT IN  
KOZHIKODE DISTRICT**

**Name of Project Engineer: Basil George**

Name of contractor : AMEER ALI N  
Agreement date : 06-11-2020  
Agreed Amount : ₹ 26359270.97  
Agreed Amount With GST : Rs. 31388620.00  
Site Handover date : 13/11/2020  
Project duration : 9 months  
Scheduled Date of Completion : 12-08-2021  
Expected Date of completion : 30-09-2021

**Status of Work in terms of components:**

- Interpretation center and toilet block.
- Canteen
- Walk way with handrail.
- Childrens park.
- Construction of new gate
- Open cafeteria.

**Works done in the last week**

- Work has completed

**Scheduled progress as on 26-02-2022 - 100%**

**Achieved progress as on 26-02-2022- 100%**

**Last week progress in 0%**

**Current week progress in 0 %**

**Current Bill Status : 3rd bill-1,73,5877/-**

**Current Financial Progress :66%**

**Images of works done at Site during last week (with time stamp)**





**RCB  
PERINCHERIKADAVU  
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM  
BRIDGE AT U/S OF  
PERINCHERIKADAVU IN KUTTIADY  
RIVER (GULIKAPUZHA) AT KOZHIKODE  
DISTRICT**

**Name of Project Engineer: Basil George**

Name of contractor : TBAS – EKK Consortium  
Agreement date : 07-09-2020  
Agreed Amount : ₹ 61,13,34,133.18/-  
Agreed Amount With GST : ₹ 68,46,94,229/-  
Site Handover date : 17-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :16-03-2022  
Expected Date of completion :16-09-2022

**Status of Work in terms of components:**

- RCB – 10%
- Bank Protection works – 1%
- Material collection works are going on.( Coconut posts supplying)

**Works done in the last week**

- Boring for pile work
- RCC of pile
- Pier p1 pile concrete
- Piling work at A1 side

Scheduled progress as on 02-04-2022 - 85%

Achieved progress as on 02-04-2022 - 16%

Last week progress in 8.5%

Current week progress 10%

Current Bill Status : 2 nd bill submitted

Current Financial Progress : NIL

Images of works done at Site during last week (with time stamp)



**PROJECTS IN  
MALAPPURAM  
DISTRICT**

**Puzhankavu  
Regulator  
(KIIFB)**

# **KIIFB Project - Construction of Regulator at Puzhankavu across Kadalundi River**

**Name of Project Engineer: RAHEES.P**

Name of contractor : Infab Infrastructure Pvt Ltd  
Agreement date : 17-12-2019  
Agreed Amount : ₹ 9,79,65,435.62  
Agreed Amount With GST : Rs. 10,97,21,287.89  
Site Handover date : 17-12-2019  
Project duration : 18 months  
Scheduled Date of Completion :16/06/2021-(10/05/2022)  
Expected Date of completion :15/06/2022-(1/05/2022)

Scheduled progress as on 02-04-2022- 50 %

Achieved progress as on 02-04-2022 -90%(civil)

Last week progress -1%

Current week progress - 1%

Current Bill Status : Total Bill submitted ₹6.24 Crores

Current Financial Progress in :63.75%

Images of works done at Site during last week

**Status of Work in terms of components:**

- four piers completed upto Hammer head portion.
- Right Abutment completed up to hammer head level..
- Left abutment completed up to Ground level.
- Right side retaining wall completed.
- Left side retaining wall total U/S-87m (75m completed)
- L/S-D/S- 53m retaining wall completed.

**Works done in the last week**

- P1-above cut water level-fourth lift concreted.
- P2,P3,P4 above cut water level-Fourth lift concreted.
- L/B U/S Chainage 75-87m counterfort wall second lift concreted.
- weir b/w P1-P2, Cleaning and reinforcement work completed. but due to heavy rain concrete postponed to this week.



**RCB  
Moothikkayam  
(KIIFB)**

# **KIIFB - Construction of Regulator cum Bridge across thoothapuzha keezhmurikadavu moothikkayam in moorkanad panchayath**

**Name of Project Engineer: Sethumadhavan**

Name of contractor : M/s PGCC Pvt,Ltd  
Agreement date : 18/09/2020  
Agreed Amount : ₹57.56 Cr  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 26-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :26-03-2022  
Expected Date of completion :26/12/2022

**Scheduled progress as on 02-04-2022 - 100%**

**Achieved progress as on 02-04-2022 - 22%**

**Last week progress - 3%**

**Current week progress - 3%**

**Current Bill Status : Fourth bill submitted**

**Current Financial Progress : 15%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 41 out of 64 piles completed
- Open footing 6 out of 6 completed
- Right abutment completed
- Side protection-rightbank downstream - 250m length raft completed.right ba upstream 400m raft completed

**Works done in the last week**

- Pier cap for P9 and P10.
- Pile cap for P5
- Left Abutment piling in progress



# PROJECTS IN PALAKKAD DISTRICT



**ITI MALAMPUZHA  
(KASE)**

# **UPGRADATION OF GOVT. ITI MALAMPUZHA ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer:NITHISH. C**

Name of contractor : M/S. PERFECTENGINEERS  
Agreement date : 05/03/2020  
Agreed Amount : ₹11,61,93,745/-  
Agreed Amount With GST : Rs. 13,01,36,994.40/-  
Site Handover date : 06/03/2020  
Project duration : 18 months  
Scheduled Date of Completion. : 05/09/2021  
Expected Date of completion. : 02/06/22

Scheduled progress as on 02/04/2022- 100%

Achieved progress as on 02/04/2022 - 74.00%

Last week progress - 70%

Current week progress- 69.00%

Current Bill Status : no of bill submitted - 5, amount:- 19955538

Current Financial Progress : 28 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components**

- Smart classroom promethean and writing board fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

**Works done in the last week**

- Exterior plastering
- AAC block work at UGF
- Lintel concrete at UGF
- FF ceiling plastering
- FF Column concrete
- FF floor tile work
- FF Shuttering of slab
- FF lintel & sunshade concrete



VADAKARAPALLY  
REGULATOR  
(KIIFB)

Construction of Regulator across Chittur  
Puzha at Vadakarapally Palathulli in  
Peruvembu Grama Panchayt in Palakkad  
District

**Name of Project Engineer:NITHIN J B**

**Name of contractor** : Poonam grah nirman Pvt ltd  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹18.95 Cr  
**Agreed Amount With GST** : Rs. 21,23,18,001.2  
**Site Handover date** : 12-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 12-07-2022  
**Expected Date of completion** : 12-07-2022

**Status of Work in terms of components:**

- 8 number of pier foundations and right side abutment footing concrete completed.
- Abutment right wall concrete 4 lifts completed.
- Retaining wall U/S right 70m full completed.
- Downstream retaining wall three lifts accomplished.
- 72 lifts of piers and 4 hammer head completed.
- Fabrication works for shutter of 10 nos is completed and final shutter in progress.

**Works done in the last week**

- Mechanical fabrication work for shutter.
- Left side abutment excavation.
- Wall concrete on U/S RHS protection wall.
- Concreting on D/S RHS wall.
- Excavation on left side abutment portion.

**Scheduled progress as on 2/04/2022 - 76%**

**Achieved progress as on 2/04/2022 - 52%**

**Last week progress - 5%**

**Current week progress -1 %**

**Current Bill Status : Fourth and part bill passed.**

**Current Financial Progress : 28%**

**Images of works done at Site during last week**



**Moongilmada LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

**Name of contractor** : M/s poljo Vyapar kendra Pvt Ltd  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹33288750 Crores  
**Agreed Amount With GST** : Rs. 37283400/-  
**Site Handover date** : 26-02-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :28-02-2022  
**Expected Date of completion** :15-03-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

.Installation of Automation and testing

**Scheduled progress as on 03/04/2022 - 100%**

**Achieved progress as on 03/04/2022 - 95 %**

**Last week progress in : 90%**

**Current week progress : 5 %**

**Current Bill Status : Part Bill-3**

**Current Financial Progress :**

**Images of works done at Site during last week (with time stamp)**

# PROJECTS IN THRISSUR DISTRICT

**REGULATOR CUM  
BRIDGE ACROSS  
KURUMALI PUZHA  
IN THRISSUR  
DISTRICT.**

**CONSTRUCTION OF  
KANATHODU REGULATOR CUM  
BRIDGE ACROSS KURUMALI  
PUZHA AT KUNDUKADAVU IN  
PUDUKAD PANCHAYATH,  
THRISSUR DISTRICT.**

**Name of Project Engineer: RAHUL V R**



Name of contractor : PGCC  
Agreement date :05-01-2022  
Agreed Amount : 262383481.27  
Agreed Amount With GST : Rs.293869499.022  
Site Handover date : 13-01-2022  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2023  
Expected Date of completion : 13-07-2023

Scheduled progress as on 02-04-2022 10%

Achieved progress as on 02-04-2022 - 01%

Last week progress in 0 %

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- in accordance with the agreement dated 05-01-2022, the type of foundation adopted was pile foundation.
- as per the boreholes taken by the contractor, it is seen that hard rock is available at depth varying 5.75m (maximum depth ) to 3.2m from the bed level, hence the foundation for piers and abutments are revised to open foundation.

**Works done in the last week**

- Revised GFC drawings was issued on 02-04-2022
- Tiver boundary survey was completed on 18-02-2022
- Trial pits has been taken.
- Initial levels also been taken



**ITI CHALAKUDY  
KIIFB-KASE**

# **UP GRADATION OF GOVT ITI CHALAKUDY ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: RAHUL V R**

Name of contractor : Sidheek, M/S Sitco Associates  
Agreement date : 28-10-2020  
Agreed Amount : ₹ 7,47,51,405.13  
Agreed Amount With GST : ₹ 8,37,21,573.74  
Site Handover date : 06-11-2020  
Project duration : 12 months  
Scheduled Date of Completion : 05-11-2021  
Expected Date of Completion :

Scheduled progress as on 02/04/2022- 0 %

Achieved progress as on 02/04/2022 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

### Works done in the last week

- As per drawings building setbacks are not available at the site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign



# **PROJECTS IN ERNAKULAM DISTRICT**

**CHELLANAM  
COASTAL  
PROTECTION  
[KIIFB]**

**KIIFB PROJECT- REFORMATION OF DAMAGED  
SUNKEN SEA WALL AT CHELLANAM USING  
TETRAPODS AND RUBBLE IN BETWEEN CP  
STONE 976 AND 1052 FOR 10 KM STRETCHES  
ALONG CHELLANAM COAST IN ERNAKULAM  
DISTRICT - PHASE I FOR A LENGTH OF 7/350  
KM IN BETWEEN CP 986 AND CP 1026**

**Name of Project Engineer: SREELAKSHMI S**

Name of contractor : M/s Uralungal Labour Contract Co-operative

Agreement date : 30-12-2021

Agreed Amount : ₹ 256,89,67,441.29

Agreed Amount With GST : ₹ 287,72,43,534.25

Site Handover date : 03-01-2022

Project duration : 16 months

Scheduled Date of Completion : 02-05-2023

Expected Date of Completion : 02-05-2023

Scheduled progress as on 03/04/2022- 18.33%

Achieved progress as on 03/04/2022 - 4.80%

Last week progress - 1%

Current week progress - 0.3%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

### Status of Work :

- 5914nos of 2T tetrapods casted.
- 2390nos of 3.5T tetrapods casted.
- Available mould 2T = 141 nos
- Available mould 3.5T = 102 nos

### Total Boulders Supplied till 01.03.2022

- Core layer (10-50kg) = 19584.11 T
- Toe (200 to 400kg) = 2265.82 T
- Underlayer (150-200kg) = 3437.25 T
- Toe ( 250-350kg) = 5377.96 T
- Toe (350-700kg) = 5631.94 T
- Primary layer (500-700kg) = 1122.05 T

### Works done in the last week

- Placing and laying in position of 2T tetrapods at SR1,SR2 and 3.5T tetrapods at SR11,SR12.
- 428nos 2T and 218nos 3.5T are placed..
- Supplying and laying of boulders in progress at SR-1,2 Harbour, SR-11,12 Abad and SR-7 Bazar.



**RCB  
KONOTHUPUZHA  
(KIIFB)**

**Construction of Regulator with  
lock across Konothupuzha at  
Puthenkavu in Udayamperoor  
Panchayath in Ernakulam  
District**

**Name of Project Engineer: Remya P R**

**Name of contractor** : Marymatha construction  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹24.36 Cr  
**Agreed Amount With GST** : Rs. 272,843,729.92  
**Site Handover date** : 14-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 13-07-2022  
**Expected Date of completion** :

**Scheduled progress as on 02-04-2022 - 55%**

**Achieved progress as on 02-04-2022- 15%**

**Last week progress - 13.5%**

**Current week progress - 15%**

**Current Bill Status :cc 1st & part bill submitted**

**Current Financial Progress :0 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- REGULATOR –not started
- CONSTRUCTION OF LOCK PORTION –constructed ring bund completed,Piling started
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

**Works were done in the last week**

Piling works - 43nos completed(lock wall)





**ANTHAKARATHO  
DU CANAL  
(KIIFB)**

# **IMPROVEMENTS TO ANTHAKARATHODE IN THRIPPUNITHURA MUNICIPALITY**

**Name of Project Engineer: Princy Abraham**

Name of contractor : Southern Tech  
Agreement date : 29-09-2018  
Agreed Amount : ₹8.35 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 08-10-2018  
Project duration : 15 months  
Scheduled Date of Completion : 07-01-2021  
Expected Date of completion : 31-12-2021

Scheduled progress as on 02-04-2022 - 98.3%

Achieved progress as on 02-04-2022 - 96.5%

Last week progress - 96.25%

Current week progress 96.5%

Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Cleaning & desilting- completed
- Side protection work- 85%
- Road and walkway formation- 70%
- Fencing and Handrail work- 70%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%

**Works done in the last week**

- Tie beam concreting
- Road and walk way formation work in progress
- S S hand rail work in progress
- paver block work
- DR masonry work near skew bridge in progress



**ELECTRICAL  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY-PROVIDING STREET  
LIGHTS ALONG THE PATHWAYS OF  
ANTHAKARATHODE**

**Name of Project Engineer:Princy Abraham**

Name of contractor : Essjay Electro links  
Agreement date : 31-12-2020  
Agreed Amount : ₹50.27 lakhs  
Agreed Amount With GST : Rs. 5630313.00  
Site Handover date : 10-01-2021  
Project duration : 5 months  
Scheduled Date of Completion : 30-05-2021  
Expected Date of completion : 31-12-2021

**Status of Work in terms of components:**

- Excavation and supply Laying of cable-75%
- Placing of lamp post, LED & feeder -75%
- Excavation and concreting-75%

**Works done in the last week**

- Pole painting & plastering foundation (KONOTHUPUZ HA SIDE)
- Pole fixing, Light fixing
- The remaining works depends upon the civil work (pathway).

**Scheduled progress as on 02-04-2022- 84%**

**Achieved progress as on 02-04-2022- 82.1%**

**Last week progress - 82.1%**

**Current week progress 82.1%**

**Current Bill Status : Part Bill prepared**

**Current Financial Progress : 85%**

**Images of works done at Site during last week (with time stamp)**



**BEAUTIFICATION  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY–LANDSCAPING &  
ARBORICULTURE, CONSTRUCTION OF  
KIOSK AND TOILET AND OPERATION &  
MAINTENANCE FOR ONE YEAR**

**Name of Project Engineer: Princy Abraham**

**Name of contractor** : GRIDS,Digital Surveyors and  
Engineering Consultants  
**Agreement date** : 24-06-2021  
**Agreed Amount** : ₹76.62 lakhs  
**Agreed Amount With GST** : Rs. 8581690.00  
**Site Handover date** : 03-07-2021  
**Project duration** : 3 months  
**Scheduled Date of Completion** : 02-10-2021  
**Expected Date of completion** : 02-01-2022

**Status of Work in  
terms of components:**

- Landscaping & tress-0%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

**Works done in the last week**

Brick work and plastering works for plantar box ( CH 320-500)

The remaining works depends upon the civil work (pathway).

**Scheduled progress as on 02-04-2022- 40%**

**Achieved progress as on 02-04-2022- 6%**

**Last week progress - 5%**

**Current week progress - 6%**

**Current Bill Status : NIL**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN IDUKKI DISTRICT

**ITI  
KATTAPPANA  
(KASE)**

**UP GRADATION OF GOVT ITI  
KATTAPPANA ON PAR WITH  
INTERNATIONAL  
STANDARDS**

**Name of Project Engineer: ATHEESH P MOHAN**



**Name of contractor** : Anchanical constructions  
**Agreement date** : 16.10.2020  
**Agreed Amount** : Rs 4,76,87,560.83  
**Agreed Amount With GST** : Rs 5,34,10,068.1  
**Site Handover date** : 04-12-2019  
**Project duration** : 08 months  
**Scheduled Date of Completion** : 31-03-2022  
**Expected Date of completion** : 18-04-2022

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 100%
- Grade beam concrete- 100%
- Grade slab Concrete - 100%
- Roof beams and slab - 95%

Works done in the last week

- Brick works
- Headroom columns casting
- Electrical works for smart class room
- Dummy column casting
- Shutter stripping

Applied for time extension

**Scheduled progress as on 02.04.22- 80%**

**Achieved progress as on 02.04.22 - 52 %**

**Last week progress : 51%**

**Current week progress :52%**

**Current Bill Status : 3rd and part bill submitted**

**Current Financial Progress in %:40%**

**Images of works done at Site during last week**



**PAVANATHMA  
COLLEGE  
MURIKKASSERY  
(RUSA )**

**RUSA II PROJECT -  
CONSTRUCTION-PAVANATHMA  
COLLEGE MURIKKASSERI, IDUKKI.**

**Name of Project Engineer: DON BABY**

Name of contractor : Anchanical constructions  
Agreement date : 02.12.2019  
Agreed Amount : Rs.79,00,000  
Agreed Amount With GST : Rs.93,22,000  
Site Handover date : 02-06-2020  
Project duration : 09 months  
Scheduled Date of Completion : 31-08-2021  
Expected Date of completion : 31-08-2021

**Status of Work in terms of components:**

- Construction of head room for stairs - Completed
- Construction of stairs and ramp - Completed
- Fixing of door and window frame - Completed
- Flooring works-100% completed

**Works done in the last week**

- Painting works in progress
- Electrical works
- Septic tank pit earthwork

**Scheduled progress as on 02.04.22 - 100%**

**Achieved progress as on 02.04.22 - 96%**

**Last week progress : 95.5%**

**Current week progress in : 96%**

**Current Bill Status : 2 Bills submitted, Rs. 54,77,389.30**

**Current Financial Progress : 69%**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – I  
(TOURISM)**

**ADDITIONAL WORK I OF ECO LODGE  
CONSTRUCTION AT IDUKKI  
(CONSTRUCTION OF APPROACH  
ROAD,RETAINING WALL,DRAIN AND  
STREET LIGHTING).**

**Name of contractor** : M/S VJ Raju and Co.  
**Agreement date** : 11-08-2020  
**Agreed Amount** : Rs.69,50,003.24  
**Agreed Amount With GST** : Rs. 77,84,003.36  
**Site Handover date** : 21-08-2020  
**Project duration** : 04 months  
**Scheduled Date of Completion** : 31-08-2021  
**Expected Date of completion** : 31-08-2021

**Status of Work in terms of components:**

- Interlocking pathway 100%
- Gate installation 100%
- Providing street lights - 100%
- Pathway concrete - 100%
- Retaining wall - 100 %

**Works done in the last week**

- Work completed

**Scheduled progress - 100%**

**Achieved progress - Work Completed**

**Current progress : 100%**

**Current Bill Status : 1 Bill submitted, RS 36,27,077.98.**

**Current Financial Progress : 52%**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – II  
(TOURISM)**

**ADDITIONAL WORK II OF ECO LODGE  
CONSTRUCTION AT IDUKKI  
(CONSTRUCTION OF PUMP HOUSE,  
SECURITY CABIN, SUMP TANK AND  
FENCING).**

**Name of Project Engineer: DON BABY**

**Name of contractor** : M/S VJ Raju and Co.  
**Agreement date** : 26.02.2021  
**Agreed Amount** : Rs.45,85,722.41  
**Agreed Amount With GST** : Rs. 51,36,009.1  
**Site Handover date** : 08-03-2021  
**Project duration** : 04 months  
**Scheduled Date of Completion** : 07-10-2021  
**Expected Date of completion** : 07-10-2021

**Status of Work in terms of components:**

- Pump house - 100%
- Security cabin - 100%
- Fencing - 100%
- Sump tank - 100%
- Plumbing, Electrical and other works -100%

**Works done in the last week**

- All works completed

**Scheduled progress as on 12.02.22- 100%**

**Achieved progress as on 12.02.22 - 100%**

**Last week progress : 100%**

**Current week progress : 100%**

**Current Bill Status : Part bill submitted.**

**Current Financial Progress : NIL**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – III  
(TOURISM)**

**ADDITIONAL WORK III OF ECO LODGE  
CONSTRUCTION AT IDUKKI  
(CONSTRUCTION OF MODULAR  
KITCHEN,DRAINAGE,PARKING  
YARD,SIDE WALL,WOOD WORK  
POLISHING,ELECTRICAL WORKS &  
GENERATOR ROOM).**

**Name of Project Engineer:DON BABY**



**Name of contractor** : M/S VJ Raju and Co.  
**Agreement date** : 21.10.2021  
**Agreed Amount** : Rs.71,96,599.18  
**Agreed Amount With GST** : Rs. 80,60,191.08  
**Site Handover date** : 31-10-2021  
**Project duration** : 03 months  
**Scheduled Date of Completion** : 31-03-2022  
**Expected Date of completion** : 31-03-2022

**Status of Work in terms of components:**

- Modular kitchen-100%
- Wood work polishing - 100%
- Electrical works - 96%
- Generator room-62%
- Drainage-100%
- Parking yard-100%
- Handrail- 100%

**Works done in the last week**

- Generator works

**Scheduled progress as on 02.04.22- 100%**

**Achieved progress as on 02.04.22 - 91%**

**Last week progress : 90%**

**Current week progress : 91%**

**Current Bill Status : Part bill submitted**

**Current Financial Progress : NIL**

**Images of works done at Site during last week**



PEERMADE  
GUEST HOUSE  
RENOVATION  
(TOURISM)

UPGRADATION AND RENOVATION OF  
GOVT. GUEST HOUSE PEERMADE ,  
IDUKKI

**Name of Project Engineer: TEENU AUGUSTINE**

Name of contractor :SRI BIBY SCARIA  
Agreement date : 30-06-2020  
Agreed Amount : Rs.1,45,51,908.00  
Agreed Amount With GST : Rs. 1,71,71,251.44  
Site Handover date : 13-07-2020  
Project duration : 9 months  
Scheduled Date of Completion :13-04-2021  
Expected Date of completion : 30-04-2022

**Scheduled progress as on 02-04-2022- 80 %**

**Achieved progress as on 02-04-2022 - 46 %**

**Last week progress -46 %**

**Current week progress - 46%**

**Current Bill Status : 1st and part bill submitted RS-12,15,770 (with GST)**

**Current Financial Progress : 15%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Roofing works of guest house building is completed
- Roofing works of service building is completed
- Plastering of service building is completed
- Floor pcc works of service building and Tiling works completed
- structure of meeting hall completed

**Works done in the last week**

- Plastering works of water tank completed
- Ceiling works of annex building on progress



**PANCHALIMEDU  
(TOURISM)**

**PANCHALIMEDU TOURISM PROJECT  
PHASE – 2  
PERUVANTHANAM VILLAGE,  
PEERMEDU TALUK, IDUKKI DISTRICT**

**Name of Project Engineer: TEENU AUGUSTINE**

**Name of contractor** : EASYINFRA INC, TVM  
**Agreement date** : 22/12/2020  
**Agreed Amount** : ₹2,43,99,440.78  
**Agreed Amount With GST** : Rs. 2,73,27,373.67  
**Site Handover date** : 01-01-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 31-12-2021  
**Expected Date of completion** : 31-12-2021

**Scheduled progress as on 02-04-2022 - 50 %**

**Achieved progress as on 02-04-2022 - 17 %**

**Last week progress - 17 %**

**Current week progress - 17 %**

**Current Bill Status : 1st and part bill submitted Rs-16,68,292/- (with GST)**

**Current Financial Progress : 10 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 50% of retaining wall construction is completed
- Earth work excavation for check dam is completed and the reinforcement steel works are going on
- Earth work excavation for pathway is completed

**Works done in the last week**

- RR works for retaining wall on north side of check dam started
- RR works of panchalikulam on progress
- RE submitted at DTPC office Painavu, Idukki



PEERMADE  
(TOURISM)

**CONSTRUCTION OF PARKING YARD,  
COMPOUND FENCING, SERVICE  
BLOCK, AMBIENT LIGHTING AND  
MODULAR KITCHEN AT ECOLODGE  
PEERMADE**

**Name of Project Engineer: TEENU AUGUSTINE**

**Name of contractor** : Outlook communications pvt.ltd.  
**Agreement date** : 08-10-2021  
**Agreed Amount** : ₹80,27,681.98  
**Agreed Amount With GST** : Rs.9472664.74  
**Site Handover date** : 11-10-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :10-10-2022  
**Expected Date of completion** : 17-10-2022

**Scheduled progress as on 02-04-2022 - 46 %**

**Achieved progress as on 02-04-2022 - 46 %**

**Last week progress - 43 %**

**Current week progress - 46 %**

**Current Bill Status : no bill submitted**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Roof concreting of service building completed
- Roof concrete of security cabin completed
- Foundation and basement of generator room completed

**Works done in the last week**

- Demolishing brickwork of service block started
- Placing of modular kitchen items on progress
- Dshuttering of service building roof on completed
- Flooring of kitchen on completed
- Plastering work of security cabin completed



# PROJECTS IN KOTTAYAM DISTRICT



**ITI  
ETTUMANOOR  
(KASE)**

# **UP GRADATION OF GOVT ITI ETTUMANOOR ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: Anjaly C R**

**Name of contractor** : Swathy Construction  
**Agreement date** : 30-07-2020  
**Agreed Amount** : ₹ 6,95,25,557.81  
**Agreed Amount With GST** : ₹ 7,78,68,624.74  
**Site Handover date** : 10-08-2020  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 09-08-2021  
**Expected Date of Completion** : Within this Financial Year

**Scheduled progress as on 02-04-2022- 98 %**

**Achieved progress as on 02-04-2022 - 93 %**

**Last week progress - 92%**

**Current week progress - 1%**

**Current Bill Status : CC 6<sup>th</sup> and part is submitted (total : ₹ 93,45,102.72 (GST excluded))**

**Current Financial Progress : 54%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Main building civil works (72%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (20%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (35%)
- External lighting (0%)
- Fire protection works (20%)
- Furniture for existing smart class room  
Converted to smart class rooms (0%)

**Works were done in the last week - Main building civil works**

- Road works completed.
- Furniture aligning works completed.
- Front gate ACP works completed.



**SIHM PALA  
(TOURISM)**

**SETTING UP OF STATE INSTITUTE  
OF HOTEL MANAGEMENT  
STUDIES AT PALA, KOTTAYAM  
DISTRICT, CONSTRUCTION OF  
ACADEMIC BLOCK**

**Name of Project Engineer: ATHEESH P MOHAN**

Name of contractor : SITCO Associates  
Agreement date : 01-03-2016  
Agreed Amount : ₹13.48 Cr  
Site Handover date : 10-03-2016  
Project duration : 18 months  
Scheduled Date of Completion : 31/10/2017  
Expected Date of completion : 31/12/2021

Scheduled progress as on 02-04-2022 - 90%

Achieved progress as on 02-04-2022 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

**Works were done inEx the last week**

- No works have been done. Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.



**CHEEPUNKAL  
(TOURISM)**

**KI IDC KUMARAKOM  
CHEEPUNKAL DESTINATION  
DEVELOPMENT PROJECT AT  
AYMANAM PANCHAYAT IN  
KOTTAYAM DISTRICT**

**Name of Project Engineer: Anjaly C R**

Name of contractor : Sri Joseph R V  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1,19,66,517.41  
Agreed Amount With GST : ₹ 1,34,02,499.49  
Site Handover date : 05-05-2021  
Project duration : 12 months  
Scheduled Date of Completion : 04-05-2022  
Expected Date of Completion : 04-05-2022

**Status of Work in terms of components:**

- House Boat Jetty (60%)
- Improvement of Approach Road (0%)
- Solar Lighting (0%)

Due to raised level of water level in river, because of heavy rain delayed work (13th October to 26th October)

**Works were done in the last week**

- Boat jetty slab tile works completed.
- Road GSB works completed.
- Handrail works completed.
- Road and Yard Interlock works completed.

**Scheduled progress as on 02-04-2022- 99%**

**Achieved progress as on 02-04- 2022- 97%**


**Last week progress - 95%**

**Current week progress - 2%**

**Current Bill Status : CC 1<sup>st</sup> and part bill submitted.**

**Current Financial Progress : 40%**

**Images of works done at Site during last week (with time stamp)**

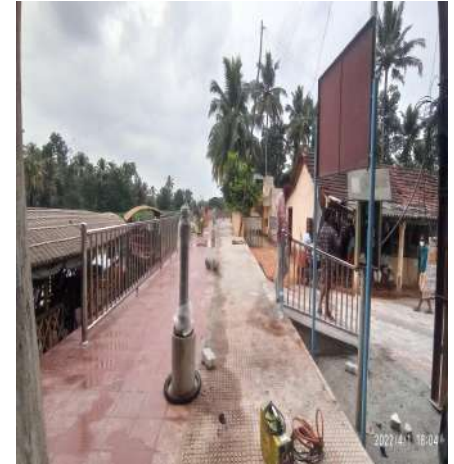

# PROJECTS IN ALAPPUZHA DISTRICT

**ITI  
CHENGANNUR  
(KASE)**

**UP-GRADATION OF GOVT ITI  
CHENGANNUR ON PAR WITH  
INTERNATIONAL  
STANDARDS - PHASE 1- REV 3**

**Name of Project Engineer: LEKSHMY GOPAN**



Name of contractor : Creators Construction  
Agreement date : 15/10/2020  
Agreed Amount : Rs 18 Cr  
Agreed Amount With GST : Rs20,64,45672/-  
Site Handover date : 30/10/2021  
Project duration :18 months  
Scheduled Date of Completion : 28/04/2023  
Expected Date of completion :30/04/2023

Scheduled progress as on 4/4/2022 : 20%

Achieved progress as on 4/4/2022 : 9%

Last week progress in : 7%

Current week progress in: 2%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Main building civil works (9%)
- Existing class room converted to smart classrooms (0%)
- Sump tank , substation works (0%)
- Road and ancillary works(0%)
- Land development (5%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

**Works done in the last week :**

- . Reinforcement works progressing.
- . Footing concrete works progressing.



**ALAPPUZHA  
CANALS  
PHASE.01  
(KIIFB)**

# **MODERNIZING WATER TRANSPORT IN ALAPPUZHA CANALS-PHASE 01**

**Name of Project Engineer: Shehas A Shukkur**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 15-02-2019  
Agreed Amount : ₹48.35 Cr  
Agreed Amount With GST : Rs. 54,15,71,596.79  
Site Handover date : 19-02-2019  
Project duration : 12 months  
Scheduled Date of Completion : 18-02-2020  
Expected Date of completion : 30-11-2021

Scheduled progress as on 04-04-2022 - 84%

Achieved progress as on 04-04-2022 - 84%

Last week progress in 82%

Current week progress- 2%

Current Bill Status : Rs.44,24,29,256.21 upto 5th bill

Current Financial Progress : 81.7%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- All agreed works has been completed
- The repair of sunken road(near Pagoda resorts) is under progress.
- The construction of roads is being carried out using GSB and paver blocks as directed by The Hon. MLA, Ambalappuzha.

**Works done in the last week**

- Repair works for Pile and slab retaining wall
- PCC for drain
- Raft slab concreting for drain



**PUNNAMADA  
(TOURISM WORK )**

# **Punnamada- Starting Point Pathway and Boat Landing at Alappuzha District.**

**Name of Project Engineer: Shehas A Shukkur**

**Name of contractor** : TBAS Construction, Aluva  
**Agreement date** : 26-02-2021  
**Agreed Amount** : ₹ 1.11 Cr  
**Agreed Amount With GST** : Rs. 1,23,77,355.31  
**Site Handover date** : 05-05-2021  
**Project duration** : 6 months  
**Scheduled Date of Completion** : 04-11-2021  
**Expected Date of completion** : 04-11-2021

**Status of Work in terms of components:**

- Pathway  
Solar Lighting

**Works done in the last week**

- Laying GSB
- Laying paver blocks
- Landscaping works
- Erection of solar LightLights
- Truss work for waiting sheds

**Scheduled progress as on 04/04/2022- 90%**

**Achieved progress as on 04/04/2022 - 90%**


**Last week progress - 80%**

**Current week progress - 10%**

**Current Bill Status : NIL**

**Current Financial Progress in %: 40%**

**Images of works done at Site during last week (with time stamp)**

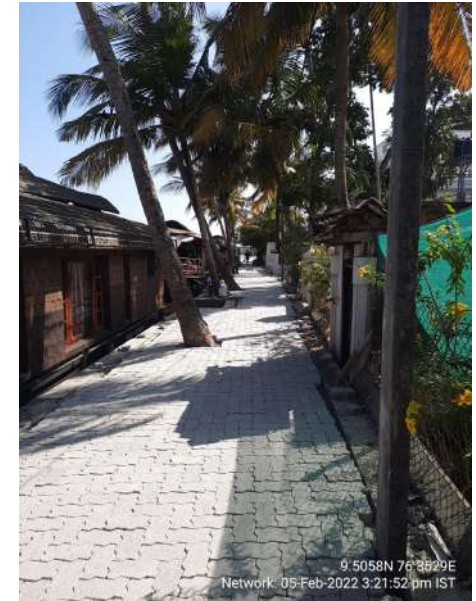

**CHUNGAM  
(TOURISM WORK )**

**CHUNGAM(CHAKREPURAKKAL)-  
KAYALCHIRA PATHWAY  
DEVELOPMENT AND BOAT  
LANDING BY THE SIDE OF  
PUNNAMADA RIVER, At  
ALAPPUZHA DISTRICT**

**Name of Project Engineer: Shehas A Shukkur**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 2.99 Cr  
Agreed Amount With GST : Rs. 3,34,07,087.37  
Site Handover date : 05-05-2021  
Project duration : 9 months  
Scheduled Date of Completion : 04-02-2022  
Expected Date of completion : 04-02-2022

Scheduled progress as on 04/04/2022 - 80%

Achieved progress as on 04/04/2022 - 68%

Last week progress - 64%

Current week progress - 4%

Current Bill Status : CC 1st and part bill: Rs.76,22,869

Current Financial Progress in %: 25.49

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

**Works done in the last week**

- Backfilling of earth and Construction of Rubble masonry Retaining wall for Pathway and Boat landing
- Backfilling behind Pile and slab retaining wall
- 



9.4974N 76.3557E  
Network time is not synchronized

**GROYNES AT  
AMBALAPUZHA  
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP  
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at  
Ambalapuzha South, North panchayath and  
Punnapra South Panchayath**

**Name of Project Engineer: SILPA R**



Name of contractor : Ramalingam Construction Company Pvt Ltd.  
Agreement date : 22-07-2020  
Agreed Amount : ₹ 51.3 Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion : 29-01-2022  
Expected Date of completion : 29-01-2022

Scheduled progress as on 02/04/2022 – 100 %

Achieved progress as on 02/04/2022 - 87.5%

Last week progress -1%

Current week progress -2.2%

Current Bill Status : 6 th bill submitted for an Amount of Rs. 8,13,05,596.70  
Total bill amount - Rs. 40,21,71,046.66

Current Financial Progress : 77%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- 20m groynes – 5 nos- 2 in progress
- 30M GROYNES -7nos- 2 in progress, 2 completed.
- 40M GROYNES – 9 nos - 6 in progress, 1 completed.
- 50M GROYNES – 9 nos -7 in progress, 2 completed.
- Sea wall length-305 m – not started
- 166369.788MT boulders reached out of 178922 MT (93%)
- 2T TETRAPODS –22612nos. casted out of 23902 nos. (94%)
- 5T TETRAPODS – 2955 nos. casted out of 2956 nos.(99.9 %)
- Earthwork Excavation – 23131.66 m3 completed out of 45955.7 M3 (43%)

**Works done in the last week**

- 2T tetrapod casted -150nos
- 5T tetrapod casted -0nos
- Supplying and Laying of Boulders -1482.87MT
- laying of boulders for,,G19,G12 ,G13is in progress
- Laying of tetrapods in G11,G21 ,G7,G20completed.



**GROYNES AT  
ARATTUPUZHA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
21NOS GROYNES AT  
ARATTUPUZHA IN BET.CH.56.6  
TO 57.8 KM AT ARATTUPUZHA**

**Name of Project Engineer: M A FASEELA NASAR**

**Name of contractor** : Ramalingam construction Company Pvt. Ltd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹ 26. 23Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :29-01-2022  
**Expected Date of completion** :29-05-2022

**Status of Work in terms of components:**

- 20M GROYNES - 6 NOS-Not started
- 25M GROYNES - 15 NOS- 1 cmplt, 2 ongoing
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 12666.15 (13.4 %) 94497 MT
- 2T TETRAPODS - 6085 ( 61.62 %) nos casted out of 9874 NOS
- 5T TETRAPODS - 491 (20.5 %) nos casted out of 2385 NOS
- GEOMAT - 64739 M2 ( not done )
- EARTHWORK EXCAVATION - 3290 M3(not done)

**Works done in the last week**

- 2T tetrapod casted - 205 nos.
- 5T tetrapod casted - 82 nos
- Supplying and Laying of Boulders- 435.64 T
- G16 started
- 165 5T tetraod layed
- 479 2T tetrapod layed

**Scheduled progress as on 03/04/2022 - 100 %**

**Achieved progress as on 03/04/2022- 26.27 %**


**Last week progress - 1 %**

**Current week progress - 1 %**

**Current Bill Status: 2 part bill submitted for an amount of Rs 5,12,95,406.88/**

**Current Financial Progress in % : 19.5 %**

**Images of works done at Site during last week (with time stamp)**

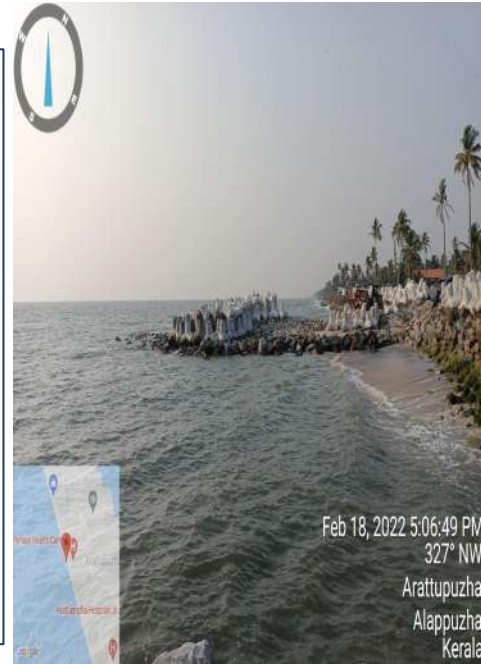

**GROYNE SITE  
AT  
PATHIYANKARA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
13NOS GROUYNE AT  
PATHIYANKARA IN BET.CH.60.1  
TO 61.6KM AT  
THRIKKUNNAPUZHA.**

**Name of Project Engineer: SILPA R**

**Name of contractor** : Ramalingam construction Company Pvt. Lmtd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹20.08Cr **Agreed Amount With GST** :  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Status of Work in terms of components:**

1. 20M GROYNES - 2 NOS-One is completed
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- 3completed and 2nos is in progress
4. 61876.225MT boulders reached out of 74546 MT(83%)
5. 2T TETRAPODS -8930casted out of 8930NOS(100%)
6. 5T TETRAPODS - 1099nos casted out of 1199NOS(91.65%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

**Works done in the last week**

- Tetrapod casting is in progress
- The total no.of tetrapods casted 2T-101& 5T-48nos
  - laying of boulders for G4,G7,G9,G11 are in progress
- Groynes G1,G2 ,G3 & G5;G6 are completed
- Supplying and laying of boulders-43.850T

**Scheduled progress as on 02/04/2022 - 100 %**

**Achieved progress as on 02/04/2022 -84.06%**

**Last week progress in -1.45%**

**Current week progress in 1.51%**

**Current Bill Status** :6 th part bill submitted for an Amt of Rs. 30230310.22  
Total bill amount - Rs. 158054952.07

**Current Financial Progress in :78%**

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT.  
VATTACHAL  
(KIIFB)**

**KIIFB  
PROJECT – CONSTRUCTION OF  
16 NOS GROUYNE AT  
VATTACHAL IN BET. CH.53.4 TO  
CH.55.2 KM(1.8KM)  
AT ARATTUPUZHA GP**

**Name of Project Engineer: M A FASEELA NASAR**

Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹28. 83Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :29-01-2022  
Expected Date of completion :29-05-2022

Scheduled progress as on 02/04/2022 - 100 %

Achieved progress as on 02/04/2022 - 66.9%

Last week progress - 3 %

Current week progress - 2 %

Current Status : 6 part bills submitted for an amt of Rs 13,45,94,938.19/-

Current Financial Progress in % : 46.65 %

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 ongoing
- 30M GROYNES - 10 NOS- 9 ongoing
- 40M T GROYNE - 4 Nos - not started
- TOTAL QUANTITY OF BOULDERS - 61794.48 MT ( 61 % ) reached out of 101487 MT
- 2T TETRAPODS - 8535( 95.49%) nos casted out of 8941 NOS
- 5T TETRAPODS - 2477 ( 72.17%) nos casted out of 3432 NOS
- GEOMAT - 4850 m2 ( 6 % ) layed out of 76299 M2
- EARTHWORK EXCAVATION - (8191.37 m3 out of 62380 M3)

### Works done in the last week

- 2T tetrapod casted - 370 nos.
- 5T tetrapod casted - 186 nos.
- Supplying and Laying of Boulders - 1040.57 T
- Groyne G10,G9,G7 completed
- 1161 5T tetrapods layed out of 3432
- 2027 2T layed



**GROYNES SITE AT  
KATTOOR  
(KIIFB)**

**Construction of 34 nos. Groyne  
at Kattoor from Ch.168.465KM  
TO CH 171.627KM (Old CH  
96.643KM TO CH 9.535 KM)**

**Name of Project Engineer: Lekshmi Priya .S**



**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 49.04 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 29-05-2022

**Scheduled progress as on 03-04-2022 – 87 % (as per EoT given)**

**Achieved progress as on 03-04-2022- 87.00%**

**Last week progress - 85.5%**

**Current week progress -1.51%**

**Current Bill Status** : 7<sup>th</sup> bill submitted for an Amount of Rs.2,82,93,879.56/- .Total bill amount - Rs. 41,21,82,538.03

**Current Financial Progress : 74.66% (with respect to RE amount)**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 20m groyne - 3 started out of 3
- 30m Groyne-5nos started out of 7
- 40m groyne - 17 nos started out of 24
- Total boulders quantity - 137534.868 MT boulders reached out of 191529.18 MT (72%)-as per RE
- 2T TETRAPODS – 21553 nos (99.95%) casted out of 21562 nos.
- 5T TETRAPODS – 3144(100%) nos. casted out of 3144 nos.
- Geomat - 13517m<sup>2</sup>
- Earthwork Excavation - 31767.090m<sup>3</sup> out of 42122 M<sup>3</sup>

**Works done in the last week**

- 2T tetrapod casted - 0nos.
- 5T tetrapod casted - 0nos.
- Supplying and Laying of Boulders -1332.16 MT
- laying of boulders for,G26,G5,G28,G19,G20 ,G17 are in progress.
- Laying of tetrapods at G4,G5,G18,G19,G20,G29 going on.



# PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE  
(KASE)**

**UPGRADATION OF GOVT. ITI  
CHANDANATHOPE ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of Project Engineer: Meenu es**

Name of contractor : Asian Constructions  
Agreement date : 16-12-2020  
Agreed Amount : ₹3.65 Cr  
Agreed Amount With GST : Rs. 4,09,28,822.77  
Site Handover date : 24-12-2020  
Project duration : 8 months  
Scheduled Date of Completion : 23/08/2021  
Expected Date of completion : 01/05/2022

### **Status of Work in terms of components:**

- Main building civil works –51%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works –3%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

### **Works done in the last week**

- . Main building AAC block work
- . Electrical works
- . Plastering works
- Tile work
- Primer work
- Work stopped due to non availability of part bill

**Scheduled progress as on 02/04/2022 - 100%**

**Achieved progress as on 02/04/2022 - 51%**

**Last week progress : 44%**

**Current week progress :5%**

**Current Bill Status :1st bill submitted to KASE, 2nd bill submitted to KIIDC office**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**



**Thenmala  
(Tourism Project)**

# **IMPROVEMENT AND DEVELOPING ECO-TOURISM AT THENMALA DAM IN KOLLAM DISTRICT**

**Name of Project Engineer:Meenu ES**

**Name of contractor** : Tomy Vallamattom  
Construction  
**Agreement date** : 29-10-2020  
**Agreed Amount** : ₹4.5 Cr  
**Agreed Amount With GST** : Rs. 4,49,90,000.00  
**Site Handover date** : 09-11-2020  
**Project duration** : 15 months  
**Scheduled Date of Completion** : 08-02-2022  
**Expected Date of completion** : 07-01-2022

**Scheduled progress as on 02/04/2022- 90%**

**Achieved progress as on 02/4/2022-51%**

**Last week progress -3%**

**Current week progress -5%**

**Current Bill Status : Nil**

**Current Financial Progress in %: Nil**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- SHOP (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)  
pavilion(50%)

**Works done in the last week**

1. Toilet, security room and cloak room-plinth beam work completed.column shuttering work under progress.brick work in progress
2. Shed to shop -roof slab concrete completed
3. Pavilion-step Work progress
4. Seating area clearance completed.



**ITI  
DHANUVECHAPU  
RAM  
(KASE)**

**UPGRADATION OF GOVT. ITI  
DHANUVECHAPURAM ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of Project Engineer: POOJITH J JOSEPH**

Name of contractor : Heather Construction  
Agreement date : 25-11-2019  
Agreed Amount : ₹11.18 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 04-12-2019  
Project duration : 20 months  
Scheduled Date of Completion : 03-04-2022  
Expected Date of completion : 03-04-2022

**Scheduled progress as on 02-04-2022- 80%(Scope of the work were increased as per the instructions from SPV)**

**Achieved progress as on 02-04-2022 - 77%**

**Last week progress - 78%**

**Current week progress - 78.50%**

**Current Bill Status** :12th bill were passed, Amount up to 12th bill:74357280.73/- (limited amount) ,14th bill submitted amount:6454677.55/-

**Current Financial Progress :74.77%**

### **Status of Work in terms of components:**

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering completed
- GF primer work 98% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 90% completed
- FF Block Work 98% completed
- FF Ceiling work 100% completed
- FF plastering 95% completed
- Dummy column RCC completed
- FF Elec- concealed work completed
- Parapet plastering completed
- GF Tile work 98%
- FF primer work 85% completed

### **Works done in the last week**

- Exterior 2nd coat painting work.
- External plumbing works
- Earth filling for road formation work.
- ELV works.

