

# KIIDC WEEKLY PROGRESS REPORT



KIIDC



# PROJECTS IN KANNUR DISTRICT

**ITI KANNUR  
(KASE )**

# **UPGRADATION OF GOVT. ITI KANNUR ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: Joel J Varghese**

Name of contractor : Shameer M A  
Agreement date : 26-08-2020  
Agreed Amount :Rs.3,40,93,937.97  
Agreed Amount With GST : Rs.3,64,82,353.00  
Site Handover date : 04-09-2020  
Project duration : 8 months  
Scheduled Date of Completion : 03-05-2021  
Expected Date of completion : 17-05-2022

Scheduled progress as on 14-05-2022 50%

Achieved progress as on 14-05-2022 30%

Last week progress in 25%

Current week progress - 30%

Current Bill Status : 2nd Bill on progress

Current Financial Progress :25%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

Footing works 100 % completed  
Stub columns, Grade beam concreting 100% completed  
Ground floor columns concreting 100% completed  
Block Work 85%  
Internal Plastering 30%  
Parapet Wall 75%

**Work done in last week**

Internal wall plastering  
Parappet wall  
Floor PCC  
Fixing of Window Grill  
Finnwall Blockwork  
Roofing Sheet



**REGULATOR  
ANCHARAKANDY  
RIVER AT  
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF  
REGULATOR WITH LOCK ACROSS  
ANCHARAKANDY RIVER AT  
PARAPRAM IN PINARAYI  
PANCHAYATH, KANNUR DISTRICT**

**Name of Project Engineer : Akhil P A**

Name of contractor : PGCC  
Agreement date :06-11-2020  
Agreed Amount : ₹44.49 Cr  
Agreed Amount With GST : Rs. 498,385,551.00  
Site Handover date : 16-11-2020  
Project duration : 18 months  
Scheduled Date of Completion : 15-05-2022  
Expected Date of completion : 15-05-2022

Scheduled progress as on 14-05-2022 99%

Achieved progress as on 14-05-2022 - 61%

Last week progress in 1 %

Current week progress - 0.5%

Current Bill Status :Sixth Part Bill submitted

Current Financial Progress : 48%

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- eWing Wall (Left Bank U/S & D/S Retaining wall upto Apron portion): Completed.
- Pier P1 & P2: Pier Head Concreting completed.
- Abutment A1: 10th lift concreting (+8.40m).
- Foot slab: Left bank upto P2 completed.
- Stair case: Left Bank completed.

### Works done in the last week

- Main Regulator pile are reached 100%
- Sheet pile driving work completed
- P3 lock wall line wall concrete completed
- Loose Apron work started
- Lock wall Concrete progressing at P4 line.



**RCB KUPPAM RIVER  
IN  
KOOVERY-KATTAM  
PALLY (KIIFB)**

**CONSTRUCTION OF REGULATOR  
CUM BRIDGE ACROSS KUPPAM  
RIVER IN KOOVERY-KATTAMPALLY  
IN CHAPPARAPADAVU PANCHAYAT ,  
THALIPARAMBA TALUK, KANNUR  
DISTRICT**

**Name of Project Engineer: Akhil P A**

**Name of contractor** : Infab Infrastructures Ltd  
**Agreement date** : 15-10-2019  
**Agreed Amount** : ₹ 18,57,64,823.98  
**Agreed Amount With GST** : 22,03,74,512.96 (as per RE)  
**Site Handover date** : 07-11-2019  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 07-05-2021  
**Expected Date of completion** : NA

**Status of Work in terms of components:**

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

**Works done in the last week**

- Nil

**Scheduled progress as on 14-05-2022 100%**

**Achieved progress as on 14-05-2022 - 0%**

**Last week progress in 0%**

**Current week progress - 0%**

**Current Bill Status :NA**

**Current Financial Progress :0%**

**Images of works done at Site during last week (with time stamp)**





## THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2

Phase 1- 14 projects- As received - 40.95 crores

Phase 2- 14 projects-AS received - 37.212 crores (Total AS received for 28 Projects – 78.162)

	Phase 1	Phase 2
<ul style="list-style-type: none"> <li>MoU signed – 18 projects</li> </ul>	Pindali kalari, Andalurkav Temple, Illikunnu church, Kottiyoor siva temple, Makreri temple, Lokanarkav temple, Thrissillery temple, Thirunelli temple, Thiruvangad Ramaswamy temple, Jagannath temple	Kadirur suryanarayana temple, Chirakkakavu temple, Mridangasaileswary temple, Oorpazhichikaav temple, Puralimala temple, Peralassery temple, Valliyoorkav temple, Thacholi manikoth
<ul style="list-style-type: none"> <li>Agreement executed - 10 projects</li> </ul>	Pindali kalari, Andalurkav Temple, Kottiyoor siva temple- Streetscape, Kottiyoor siva temple-Tourist amenities, Lokanarkav temple, Makreri Subramanyaswmi temple, Illikunnu church, Jagannath temple	Puralimala temple, Pazhassiraja smrithimandapam
<ul style="list-style-type: none"> <li>Works started – 9 (GFC drawing prepared by KIIDC)</li> </ul>	Andalurkav temple, Illikunnu church, Pindali kalari, Kottiyoor temple-Streetscape, Kottiyoor siva temple-Tourist amenities, Jagannath temple, Lokanarkav temple, Makreri Subramanyaswami temple	Puralimala temple
<ul style="list-style-type: none"> <li>Selection notice issued - 8 projects</li> </ul>	Thiruvangad Ramaswamy temple, Thirunelli Temple, Thrissillery Temple	Sree Thacholi Manikoth Temple, Vadakara Tazhe angadi, Peralassery Temple, Chirakkakav temple, Thalakkal Chandu Museum - Panamaram

**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

**THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2**

	Phase 1	Phase 2
<ul style="list-style-type: none"> <li>• Tender to be finalized - 2 Projects</li> </ul>	<p>Municipal Stadium (THP Office), Kakkulangara Mosque (Letter submitted to Tourism for tender excess approval)</p>	
<ul style="list-style-type: none"> <li>• To be retendered - 2 projects (After revising the TS in DSR 2018)</li> </ul>	<p>Odathil Mosque and Paris Hotel Street</p>	<p>Kadirur Surya Narayana Temple</p>
<ul style="list-style-type: none"> <li>• TS to be issued - 4 projects</li> </ul>		<p>Sree Mridanga Saileswari Temple, Thodeekalam Siva Temple, Sree Oorpazhachi Kavu Temple, Valliyoorkavu temple</p>
<ul style="list-style-type: none"> <li>• To be dropped - 2 projects (NOC not received)</li> </ul>		<p>Pazhassi Kovilakam (Mattannur), Arakkal Kettu (Total amount – 10.5Cr)</p>

**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT - THALASSERY  
HERITAGE PROJECT - PHASE 1  
-Pazhassi Circuit - Pindali Kalari  
House(Pathway,Conservation of  
Kalarithara,Pond restoration ,Seating,  
Landscaping ,Electrification)at  
Iritty,Kannur**

**Name of Project Engineer:Joel J Varghese**

Name of contractor : M/s Classic Builders  
Agreement date : 17-02-2021  
Agreed Amount : ₹ 0.6238 Cr  
Agreed Amount With GST : Rs. 6987127.71  
Site Handover date :  
Project duration : 12 months  
Scheduled Date of Completion : 27-02-2022  
Expected Date of completion :

Scheduled progress as on 14-05-2022 : 50%

Achieved progress as 14-05-2022 - 25%

Last week progress - 50%

Current week progress -30%

Current Bill Status : Ready for Part 1 bill

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

Gallery Work 100 % completed

Kalarithara 50%

Kalasamandaapam 25%

Pond 5%

**Works done last Week:**

Kalasamandapam

Pond Works

Kalarithara



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 - Cultural Circuit -Andalur Kavvu**

**Name of Project Engineer: Akhil P A**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.5189 Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 1.701 Cr  
Project duration : 12 months  
Scheduled Date of Completion : 26-02-2022  
Expected Date of completion :

**Status of Work in terms of components:**

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

**Work done in last week**

- Sadrahalli stone pavement progressing
- KIIFB Resident Engineer inspection was done

**Scheduled progress as on 14-05-2022 : 100%**

**Achieved progress as 14-05-2022 - 17 %**

**Last week progress - 0%**

**Current week progress -0%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -illikunnu**

**Name of Project Engineer: Akhil P A**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26/02/2021  
Agreed Amount : ₹ 8300000  
Agreed Amount With GST : Rs  
Site Handover date :  
Project duration : 12 months  
Scheduled Date of Completion : 26/02/2022  
Expected Date of completion :

**Status of Work in terms of components of cemetery :**

- Land scaping of cemetery area
- Lighting
- Conservation of ceiling,wood work, joinery

**Work done in last week**

- Compound laterite work in progressing
- Sadarahalli pavement started.
- KIIFB Resident Engineer inspection has done.

**Scheduled progress as on 14-05-2022 : 100%**

**Achieved progress as 14-05-2022 - 30%**


**Last week progress - 1%**

**Current week progress -1%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**

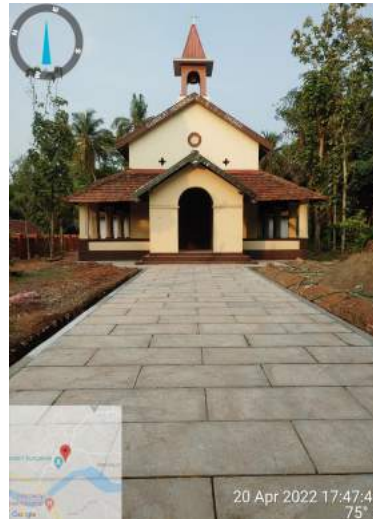



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -Jaganath Temple**

**Name of Project Engineer: Akhil P A**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26/02/2021  
Agreed Amount : ₹ 1,48,17,938.56  
Agreed Amount With GST : 1.56cr

Site Handover date : 08/03/2021  
Project duration : 12 months  
Scheduled Date of Completion : 08/03/2022  
Expected Date of completion :

**Status of Work in terms of components :**

- Pathway
- Rivival of pond
- Compound wall
- Landscaping

**Work done in last week**  
**Compound laterite work in progressing**

- GSB work progressing for pathway
- Sadrahalli stone laying progressing

**Scheduled progress as on 14-05-2022 : 100%**

**Achieved progress as 14-05-2022 - 27%**

**Last week progress - 0%**

**Current week progress -1%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT –THALASSERY HERITAGE  
PROJECT-PHASE 1-pazhassi circuit –kottiyoor shiva  
temple(streetscape,landscaping,agrashala,carpark  
ing,stage and electrical work at kottiyoor shiva  
temple in irrity,Kannur district)**

**Name of Project Engineer:Basil George**

Name of contractor : M/s Rubicon construction  
Agreement date : 05/10/2021  
Agreed Amount : ₹ 1.21 cr  
Agreed Amount With GST : RS 1,36,06,740.60  
Site Handover date : 14/10/2021  
Project duration : 12 months  
Scheduled Date of Completion : 13-10-2022  
Expected Date of completion : 13/10/2022

**Status of Work in terms of components:**

- Streetscape
- Landscaping
- Agrashala
- Car parking
- Stage
- electrification

**Work done in last week**

Ootupura-foundation work in progress  
Laying narasapuram stone-streetscape work  
Pedestal work for lamp post.  
Pantry building laterate masonry.  
Lamp post fixing

**Scheduled progress as on 14-05.2022 : 60%**

**Achieved progress as 14-05-2022 - 50%**


**Last week progress - 30%**

**Current week progress -30%**

**Current Bill Status : 1st bill submitted**

**Current Financial Progress : 17%**

**Images of works done at Site during last week (with time stamp)**

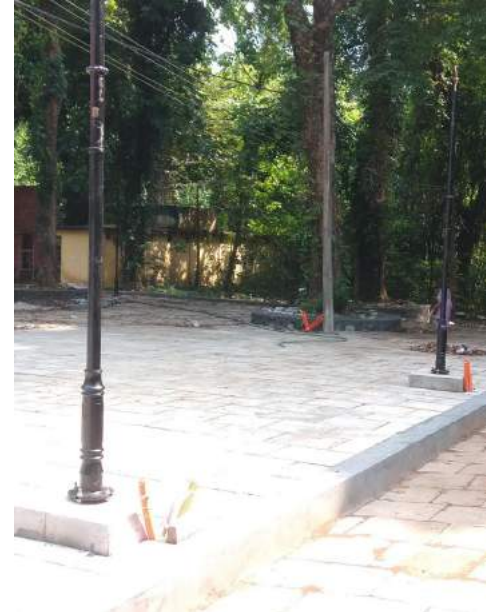

# COMPREHENSIVE DEVELOPMENT OF MUZHAPPILANGAD AND DHARMADOM BEACH IN KANNUR DISTRICT

**IN PRINCIPLE SANCTION : 233.71 Cr**

**FUNDING AGENCY : KIIFB**

**The whole project is divided into 4 Character areas**

**AS Amount for Character Area 1 : 79.51 Cr**

**CA 1 - AS DATE : 17/03/2022**

**CA 1- TS DATE : 22/03/2022**

## **CHARACTER AREA 1**

- ❖ CRZ clearance obtained
- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai and revised architectural drawing prepared by consultant architect received on 01.12.2021
- ❖ KIIFB approved Character area 1 for an amount 79.51 Cr on 17.03.2022
- ❖ Work tendered and tender opened on 23.04.2022
- ❖ 5 bidders quoted for the work. Since the work is above 5 crore, Pre-qualification is necessary
- ❖ Tender will be finalized after PQ

## **CHARACTER AREA 2**

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

## **CHARACTER AREA 3**

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

## **CHARACTER AREA 4**

- ❖ DPR and detailed project components are under preparation with Consultant architect CBRE

# PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS  
POONUR  
PUZHA-POOLAKAD  
AVU (KIIFB)**

**KIIFB PROJECT CONSTRUCTION  
OF RCB ACROSS POONUR PUZHA  
NEAR KWA PUMPING HOUSE AT  
POOLAKADAVU IN KURUVATTOOR  
PANCHAYATH**

**Name of Project Engineer: Athul Ashar**

Name of contractor : ULCCS Ltd.  
Agreement date : 18-08-2021  
Agreed Amount : ₹22,68,45,702.29  
Agreed Amount With GST : Rs.  
Site Handover date : 27-08-2021  
Project duration : 18 months  
Scheduled Date of Completion : 26-02-2023  
Expected Date of completion : 26-02-2023

**Status of Work in terms of components:**

- 43 no of pile foundation is completed out of 48
- Piling work for P1,P2 & P3 are complete
- Piling work for A1 & A2 are ongoing
- 

**Works done in the last week**

- Land acquisition proposal is submitted.
- Piling work for A2

**Scheduled progress as on 14-05-2022 - 25%**

**Achieved progress as on 14-05-2022- 12%**

**Last week progress- 2 %**

**Current week progress - 1 %**

**Current Bill Status : nil**

**Current Financial Progress : nil**

**Images of works done at Site during last week (with time stamp)**





**ITI KOYILANDY  
(KASE)**

**UPGRADATION OF GOVT. ITI  
KOYILANDY ON PAR WITH  
INTERNATIONAL STANDARDS**

**Name of Project Engineer: Basil George**

Name of contractor : ULCCS Ltd.  
Agreement date : 14-08-2020  
Agreed Amount : ₹4.22 Cr  
Agreed Amount With GST : Rs. 4,22,86,606  
Site Handover date : 14-08-2020  
Project duration : 12 months  
Scheduled Date of Completion :13-08-2021  
Expected Date of completion :13-11-2021

**Status of Work in terms of components:**

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

**Works done in the last week**

- Work delayed

**Scheduled progress as on 14-05-2022- 100%**

**Achieved progress as on 14-05-2022 - 85%**

**Last week progress- 0%**

**Current week progress - 0%**

**Current Bill Status : CC 3rd and part submitted**

**Current Financial Progress : 34.3%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT –THALASSERY HERITAGE  
PROJECT-PHASE 1-pazhassi circuit –  
Lokanarkavu Temple (Conservation of  
Thantrimadom, Folklore, Oottupura,Chiras,  
Plumbing and Electrification at  
Lokanarkavu Temple in Vadakara,  
Kozhikode District)**

**Name of Project Engineer:Basil George**

Name of contractor : Saaj Constructions  
Agreement date : 17-06-2021  
Agreed Amount : ₹ 3,78,74,574.27/-  
Agreed Amount With GST : Rs.  
Site Handover date : 27-06-2021  
Project duration : 12 months  
Scheduled Date of Completion :  
Expected Date of completion :

Scheduled progress as on 14-05-2022- 90%

Achieved progress as on 14-05-2022 - 1%

Last week progress- 1%

Current week progress - 1%

Current Bill Status :

Current Financial Progress :

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- thanthrimadam up to plinth belt were completed.
- big chira side protection work in progress.
- compound wall work

**Works done in the last week**

- big chira DR masonry works.
- compound wall excavation works



**RCB  
PERINCHERIKADAVU  
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM  
BRIDGE AT U/S OF  
PERINCHERIKADAVU IN KUTTIADY  
RIVER (GULIKAPUZHA) AT KOZHIKODE  
DISTRICT**

**Name of Project Engineer: Basil George**

**Name of contractor** : TBAS – EKK Consortium  
**Agreement date** : 07-09-2020  
**Agreed Amount** : ₹ 61,13,34,133.18/-  
**Agreed Amount With GST** : ₹ 68,46,94,229/-  
**Site Handover date** : 17-09-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 16-03-2022  
**Expected Date of completion** : 01-03-2024

**Status of Work in terms of components:**

- RCB – 10%
- Bank Protection works – 17%
- Material collection works are going on.( Coconut posts supplying)

**Works done in the last week**

- Pile chipping-abutment
- Earth work excavation for pile cap
- Pile cap for retaining wall and wall concrete



**Scheduled progress as on 14-05-2022 - 85%**

**Achieved progress as on 14-05-2022 - 22%**

**Last week progress in 8.5%**

**Current week progress 10%**

**Current Bill Status : 2 nd bill submitted**

**Current Financial Progress : 17%**

**Images of works done at Site during last week (with time stamp)**



**PROJECTS IN  
MALAPPURAM  
DISTRICT**

**Puzhankavu  
Regulator  
(KIIFB)**

# **KIIFB Project - Construction of Regulator at Puzhankavu across Kadalundi River**

**Name of Project Engineer: RAHEES.P**



**Name of contractor** : Infab Infrastructure Pvt Ltd  
**Agreement date** : 17-12-2019  
**Agreed Amount** : ₹ 9,79,65,435.62  
**Agreed Amount With GST** : Rs. 10,97,21,287.89  
**Site Handover date** : 17-12-2019  
**Project duration** : 18 months  
**Scheduled Date of Completion** :16/06/2021-(10/05/2022)  
**Expected Date of completion** :15/06/2022-(1/05/2022)

**Scheduled progress as on 15-05-2022-95%**

**Achieved progress as on 15-05-2022 -94%**

**Last week progress -0%**

**Current week progress - 0%**

**Current Bill Status : Total Bill submitted ₹7.10 Crores (9th part bill)**

**Current Financial Progress in :72.53%**

**Images of works done at Site during last week**

**Status of Work in terms of components:**

- four piers completed including Hammer head portion.
- Right & Left side Abutments completed up to hammer head level..
- Right side retaining wall u/s 110/110m & d/s 50/50m completed.
- Left side retaining wall total U/S-87/110 L/S-D/S- 53/53m retaining wall completed.

**Works done in the last week**

- Guard room column concreted.
- secondary concrete of piers on core portion progressing.
- mechanical shutters shifted to site from yard.
- Heavy rain occurred at site.



**RCB  
Moothikkayam  
(KIIFB)**

# **KIIFB - Construction of Regulator cum Bridge across thoothapuzha keezhmurikadavu moothikkayam in moorkanad panchayath**

**Name of Project Engineer: RAHEES.P**

Name of contractor : M/s PGCC Pvt,Ltd  
Agreement date : 18/09/2020  
Agreed Amount : ₹57.56 Cr  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 26-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :26-03-2022  
Expected Date of completion :26/12/2022

**Scheduled progress as on 15-05-2022 - 100%**

**Achieved progress as on 15-05-2022 - 32%**

**Last week progress - 2%**

**Current week progress -1%**

**Current Bill Status : Fourth bill submitted**

**Current Financial Progress : 24.84%**


**Images of works done at Site during last week (with time stamp)**

### **STATUS OF WORK IN TERMS OF COMPONENTS**

- 64 OUT OF 64 piles completed
- girder beam 28/28 concreted.
- Open footing 6 out of 6 completed
- side protection  
1)D/S-R/S- 216/260 M raft completed.  
2)U/S-R/S- 251/600m raft completed. 206 m partially completed

#### Works done in the last week

- Pile casting completed
- Pier cap -7 nos concreted
- girder beam casting completed.
- retaining wall 24m completed.
- pile load test-platform making on going.

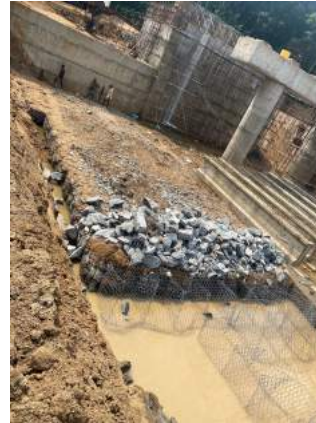

# PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA  
(KASE)**

# **UPGRADATION OF GOVT. ITI MALAMPUZHA ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: NITHISH. C**

Name of contractor : M/S. PERFECTENGINEERS  
Agreement date : 05/03/2020  
Agreed Amount : ₹11,61,93,745/-  
Agreed Amount With GST : Rs. 13,01,36,994.40/-  
Site Handover date : 06/03/2020  
Project duration : 18 months  
Scheduled Date of Completion. : 05/09/2021  
Expected Date of completion. : 02/06/22

Scheduled progress as on 14/05/2022- 100%

Achieved progress as on 14/05/2022 - 75.00%

Last week progress - 70%

Current week progress- 69.00%

Current Bill Status : no of bill submitted - 5, amount:- 36640193

Current Financial Progress : 28 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components**

- Smart classroom promethean and writing board fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

**Works done in the last week**

- AAC block work at FF
- Plumbing work at FF
- FF ceiling plastering
- FF roof slab projection concreting
- FF floor tile work
- Reinforcement work of Lift wall
- Drainage wall concrete



VADAKARAPALLY  
REGULATOR  
(KIIFB)

Construction of Regulator across Chittur  
Puzha at Vadakarapally Palathulli in  
Peruvembu Grama Panchayt in Palakkad  
District

**Name of Project Engineer:NITHIN J B**

**Name of contractor** : Poonam grah nirman Pvt ltd  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹18.95 Cr  
**Agreed Amount With GST** : Rs. 21,23,18,001.2  
**Site Handover date** : 12-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 12-07-2022  
**Expected Date of completion** : 12-07-2022

**Status of Work in terms of components:**

- 9 number of pier foundations and right side abutment footing concrete completed.
- 8 Sill beams erected.
- Hoisting bridge fabrication in progress.
- Downstream retaining wall 20m fully accomplished.
- 123 lifts of piers out of 168 completed.
- Fabrication works for shutter of 11 nos is completed.
- 8 weir concrete completed.

**Works done in the last week**

- Mechanical fabrication work for shutter.
- Left side abutment excavation.
- Wall concrete on U/S RHS protection wall.
- Concreting on D/S RHS wall.
- Excavation on left side abutment portion.

**Scheduled progress as on 14/05/2022 - 82%**

**Achieved progress as on 14/05/2022 - 62%**

**Last week progress - 2%**

**Current week progress -1 %**

**Current Bill Status : Fifth and part bill submitted**

**Current Financial Progress : 28%**

**Images of works done at Site during last week**





**Moongilmada LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd  
Agreement date : 26-02-2021  
Agreed Amount : ₹33288750 Crores  
Agreed Amount With GST : Rs. 37283400/-  
Site Handover date : 26-02-2021  
Project duration : 12 months  
Scheduled Date of Completion :28-02-2022  
Expected Date of completion :15-03-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

.Conducting Trial Run

**Scheduled progress as on 15/05/2022 - 100%**

**Achieved progress as on 15/05/2022 - 99 %**

**Last week progress in : 99%**

**Current week progress : %**

**Current Bill Status : Part Bill-3**

**Current Financial Progress : 90%**

**Images of works done at Site during last week (with time stamp)**



**Moongilmada LIS  
(Civil)  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

**Name of contractor** : M/s Vallamattam constructions  
**Agreement date** : 18-09-2020  
**Agreed Amount** : ₹15422222 Crores  
**Agreed Amount With GST** : Rs. 18198221.96/-  
**Site Handover date** : 03-06-2021  
**Project duration** : 6 months  
**Scheduled Date of Completion** :03-12-2021  
**Expected Date of completion** :31-05-2022

**Status of Work in terms of components:**

- Pump House
- Conversion of abonded RBC to water storage.
- Electrical Works

**Works done in the last week**

.Electrical works ongoing

**Scheduled progress as on 15/05/2022 - 100%**

**Achieved progress as on 15/05/2022 - 87 %**

**Last week progress in : 87%**

**Current week progress : 0%**

**Current Bill Status : Part Bill-2**

**Current Financial Progress : 65%**

**Images of works done at Site during last week (with time stamp)**

**Valiyeri LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Valiyeri LIS in  
eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd  
Agreement date : 24-06-2021  
Agreed Amount : ₹31004000 Rupees  
Agreed Amount With GST : Rs. 36581180/-  
Site Handover date : 25-06-2021  
Project duration : 12 months  
Scheduled Date of Completion :25-06-2022  
Expected Date of completion :31-05-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

.Automation Works

**Scheduled progress as on 15/05/2022 - 87%**

**Achieved progress as on 15/05/2022 - 86 %**

**Last week progress in : 85%**

**Current week progress : 1%**

**Current Bill Status : Part Bill-2**

**Current Financial Progress : 68%**

**Images of works done at Site during last week (with time stamp)**



**Navithankulam LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at  
Navithankulam LIS in  
eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd  
Agreement date : 24-06-2021  
Agreed Amount : ₹16327047.54 Rupees  
Agreed Amount With GST : Rs. 19265916.09/-  
Site Handover date : 25-06-2021  
Project duration : 12 months  
Scheduled Date of Completion :25-06-2022  
Expected Date of completion :31-06-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

.Main line Works

**Scheduled progress as on 15/05/2022 - 87%**

**Achieved progress as on 15/05/2022 - 56 %**

**Last week progress in : 55%**

**Current week progress : 1%**

**Current Bill Status : Nil**

**Current Financial Progress :**

**Images of works done at Site during last week (with time stamp)**





**Kunnamkatupathy  
LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at  
Kunnamkatupathy LIS in  
eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

Name of contractor : M/s Mahendra Pvt Ltd  
Agreement date : 18-11-2021  
Agreed Amount : ₹36068276 Rupees  
Agreed Amount With GST : Rs. 42560565.68/-  
Site Handover date : 27-11-2021  
Project duration : 6 months  
Scheduled Date of Completion :29-05-2022  
Expected Date of completion :31-06-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

.Submain and Main line Works

**Scheduled progress as on 15/05/2022 - 87%**

**Achieved progress as on 15/05/2022 - 56 %**

**Last week progress in : 54%**

**Current week progress : 2%**

**Current Bill Status : Partbill-2**

**Current Financial Progress : 42%**

**Images of works done at Site during last week (with time stamp)**



**MOOLATHARA  
RIGHT BANK CANAL  
PHASE 1 FROM  
KORAYAR TO  
VARATTAYAR  
(KIIFB)**

**KIIFB-Extension of Moolathara  
right bank canal phase 1 from  
korayar to varattayar**

**Name of Project Engineer: NITHISH.C**

Name of contractor : M/s Prathmesh & K.K.Constructions  
Agreement date : 23-12-2021  
Estimate P.A.C : Rs.158,50,00,000/-  
CONTRACT P.A.C : Rs. 174,34,95000/-  
Site Handover date : 31-12-2021  
Project duration : 30 months  
Scheduled Date of Completion :  
Expected Date of completion :

**Status of Work in terms of components:**

- Site clearance

**Works done in the last week**

.Design works

**Scheduled progress as on 14/05/2022 - Nil**

**Achieved progress as on 14/05/2022 - Nil**

**Last week progress in : Nil**

**Current week progress : Nil**

**Current Bill Status : Nil**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN THRISSUR DISTRICT

**REGULATOR CUM  
BRIDGE ACROSS  
KURUMALI PUZHA  
IN THRISSUR  
DISTRICT.**

**CONSTRUCTION OF  
KANATHODU REGULATOR CUM  
BRIDGE ACROSS KURUMALI  
PUZHA AT KUNDUKADAVU IN  
PUDUKAD PANCHAYATH,  
THRISSUR DISTRICT.**

**Name of Project Engineer: RAHUL V R**

Name of contractor : PGCC  
Agreement date : 05-01-2022  
Agreed Amount : 262383481.27  
Agreed Amount With GST : Rs.293869499.022  
Site Handover date : 13-01-2022  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2023  
Expected Date of completion : 13-07-2023

**Scheduled progress as on 14-05-2022 12%**

**Achiever progress as on 14-05-2022 - 3.5%**

**Last week progress- 3.5%**

**Current week progress - 0%**

**Current Bill Status : NIL**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- in accordance with the agreement dated 05-01-2022, the type of foundation adopted was pile foundation.
- as per the boreholes taken by the contractor, it is seen that hard rock is available at depth varying 5.75m (maximum depth ) to 3.2m from the bed level, hence the foundation for piers and abutments are revised to open foundation.

**Works done in the last week**

- Revised GFC drawings was issued on 02-04-2022
- Tiver boundary survey was completed on 18-02-2022
- Trial pits has been taken.
- Initial levels also been taken
- Work was inaugurated on 16/04/2022
- **Heavy Rain causes rise in water level so, no work at site**



**ITI CHALAKUDY  
KIIFB-KASE**

# **UP GRADATION OF GOVT ITI CHALAKUDY ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: RAHUL V R**



Name of contractor : Sidheek, M/S Sitco Associates  
Agreement date : 28-10-2020  
Agreed Amount : ₹ 7,47,51,405.13  
Agreed Amount With GST : ₹ 8,37,21,573.74  
Site Handover date : 06-11-2020  
Project duration : 12 months  
Scheduled Date of Completion : 05-11-2021  
Expected Date of Completion :

Scheduled progress as on 14/05/2022- 0 %

Achieved progress as on 14/05/2022 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%


Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

### Works done in the last week

- As per drawings building setbacks are not available at the site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign

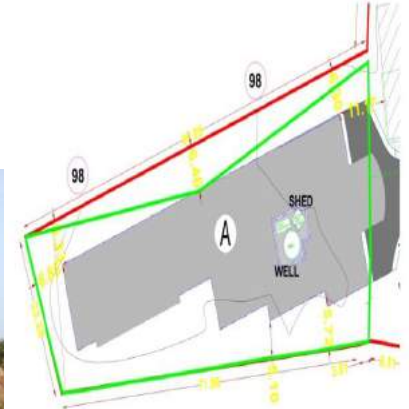

# **PROJECTS IN ERNAKULAM DISTRICT**

**CHELLANAM  
COASTAL  
PROTECTION  
[KIIFB]**

**KIIFB PROJECT- REFORMATION OF DAMAGED  
SUNKEN SEA WALL AT CHELLANAM USING  
TETRAPODS AND RUBBLE IN BETWEEN CP  
STONE 976 AND 1052 FOR 10 KM STRETCHES  
ALONG CHELLANAM COAST IN ERNAKULAM  
DISTRICT - PHASE I FOR A LENGTH OF 7/350  
KM IN BETWEEN CP 986 AND CP 1026**

**Name of Project Engineer: SREELAKSHMI S**

Name of contractor : M/s Uralungal Labour Contract Co-operative

Agreement date : 30-12-2021

Agreed Amount : ₹ 256,89,67,441.29

Agreed Amount With GST : ₹ 287,72,43,534.25

Site Handover date : 03-01-2022

Project duration : 16 months

Scheduled Date of Completion : 02-05-2023

Expected Date of Completion : 02-05-2023

Scheduled progress as on 15/05/2022- 27.5%

Achieved progress as on 08/05/2022 - 16.73%

Last week progress - 1.70%

Current week progress- 2.73%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

### Status of Work :

- 12206nos of 2T tetrapods cast.
- 8233nos of 3.5T tetrapods cast.
- Available mould 2T = 144 nos
- Available mould 3.5T = 153 nos

### Total Boulders Supplied till 12.05.2022

- Core layer (10-50kg) = 44702.168 T
- Toe (200 to 400kg) = 29312.101 T
- Underlayer (150-200kg) = 14503.701 T
- Toe ( 250-350kg) = 45351.07 T
- Toe (350-700kg) = 25367.30 T
- Primary layer(500-800kg)=18679.231T

### Works done in the last week

- 3981nos 2T and 3574nos 3.5T tetrapods are placed.
- Supplying and laying of boulders in progress at SR-1,2,3 Harbour, SR-10,11,12,13 Abad and SR-7,8 Bazar.
- RMC Plant Commissioned on 11-05-2022



**RCB  
KONOTHUPUZHA  
(KIIFB)**

**Construction of Regulator with  
lock across Konothupuzha at  
Puthenkavu in Udayamperoor  
Panchayath in Ernakulam  
District**

**Name of Project Engineer: Remya P R**

Name of contractor : Marymatha construction  
Agreement date : 04-01-2021  
Agreed Amount : ₹24.36 Cr  
Agreed Amount With GST : Rs. 272,843,729.92  
Site Handover date : 14-01-2021  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2022  
Expected Date of completion : 26-04-2023

Scheduled progress as on 14-05-2022 - 55%

Achieved progress as on 14-05-2022- 22%

Last week progress - 21.5.5%

Current week progress - 0.5%

Current Bill Status :cc 1st & part bill submitted

Current Financial Progress :6.5 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- REGULATOR –Pier 1 piling started.
- CONSTRUCTION OF LOCK PORTION –constructed ring bund completed,Pile boring completed
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

**Works were done in the last week**

Piling works -  
Lock portin- 56 piles,  
Pier 1 & Pier 2- 8  
8 piles completed  
Left abutment- 1  
no.s



**ANTHAKARATHO  
DU CANAL  
(KIIFB)**

# **IMPROVEMENTS TO ANTHAKARATHODE IN THRIPPUNITHURA MUNICIPALITY**

**Name of Project Engineer: Princy Abraham**

Name of contractor : Southern Tech  
Agreement date : 29-09-2018  
Agreed Amount : ₹8.35 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 08-10-2018  
Project duration : 15 months  
Scheduled Date of Completion : 07-01-2021  
Expected Date of completion : 31-12-2021

**Status of Work in terms of components:**

- Cleaning & desilting- completed
- Side protection work- 85%
- Road and walkway formation- 70%
- Fencing and Handrail work- 70%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%

**Works done in the last week**

- Tie beam concreting work in progress
- Road and walk way formation work in progress
- S S hand rail work in progress
- paver block work
- DR masonry work in progress

**Scheduled progress as on 14-05-2022 - 98.5%**

**Achieved progress as on 14-05-2022 - 96.85%**

**Last week progress - 96.75%**

**Current week progress 96.85%**

**Current Bill Status : 3 bills submitted of amount ,Rs.5,53,62,463.00**

**Current Financial Progress : 65%**

**Images of works done at Site during last week (with time stamp)**





**ELECTRICAL  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY-PROVIDING STREET  
LIGHTS ALONG THE PATHWAYS OF  
ANTHAKARATHODE**

**Name of Project Engineer:Princy Abraham**

Name of contractor : Essjay Electro links  
Agreement date : 31-12-2020  
Agreed Amount : ₹50.27 lakhs  
Agreed Amount With GST : Rs. 5630313.00  
Site Handover date : 10-01-2021  
Project duration : 5 months  
Scheduled Date of Completion : 30-05-2021  
Expected Date of completion : 31-12-2021

**Status of Work in terms of components:**

- Excavation and supply Laying of cable-75%
- Placing of lamp post, LED & feeder -75%
- Excavation and concreting-75%

**Works done in the last week**

- Pole painting & plastering foundation (KONOTHUPUZ HA SIDE)
- Pole fixing, Light fixing
- The remaining works depends upon the civil work (pathway).

Scheduled progress as on 14-05-2022- 84%

Achieved progress as on 14-05-2022- 82.1%

Last week progress - 82.1%

Current week progress 82.1%

Current Bill Status : Part Bill prepared

Current Financial Progress : 85%

Images of works done at Site during last week (with time stamp)



**BEAUTIFICATION  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY–LANDSCAPING &  
ARBORICULTURE, CONSTRUCTION OF  
KIOSK AND TOILET AND OPERATION &  
MAINTENANCE FOR ONE YEAR**

**Name of Project Engineer: Princy Abraham**

**Name of contractor** : GRIDS,Digital Surveyors and  
Engineering Consultants  
**Agreement date** : 24-06-2021  
**Agreed Amount** : ₹76.62 lakhs  
**Agreed Amount With GST** : Rs. 8581690.00  
**Site Handover date** : 03-07-2021  
**Project duration** : 3 months  
**Scheduled Date of Completion** : 02-10-2021  
**Expected Date of completion** : 02-01-2022

**Status of Work in terms of components:**

- Landscaping & tress-0%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

**Works done in the last week**

Brick work and plastering works for plantar box ( CH 320-500)

The remaining works depends upon the civil work (pathway).

**Scheduled progress as on 14-05-2022- 40%**

**Achieved progress as on 14-05-2022- 6%**

**Last week progress - 5%**

**Current week progress - 6%**

**Current Bill Status : NIL**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN IDUKKI DISTRICT

**ITI  
KATTAPPANA  
(KASE)**

**UP GRADATION OF GOVT ITI  
KATTAPPANA ON PAR WITH  
INTERNATIONAL  
STANDARDS**

**Name of Project Engineer: DON BABY**

**Name of contractor** : Anchanical constructions  
**Agreement date** : 16.10.2020  
**Agreed Amount** : Rs 4,76,87,560.83  
**Agreed Amount With GST** : Rs 5,34,10,068.1  
**Site Handover date** : 04-12-2019  
**Project duration** : 08 months  
**Scheduled Date of Completion** : 31-05-2022  
**Expected Date of completion** : 31- 05-2022

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 100%
- Grade beam concrete- 100%
- Grade slab Concrete - 100%
- Roof beams and slab - 100%

Works done in the last week

- Brick works
- Electrical works
- Plastering works

**Scheduled progress as on 15.05.22- 80%**

**Achieved progress as on 15.05.22 - 55%**

**Last week progress : 54%**

**Current week progress :55%**

**Current Bill Status : 4th and part bill submitted**

**Current Financial Progress in %:48 %**

**Images of works done at Site during last week**



**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – III  
(TOURISM)**

**ADDITIONAL WORK III OF ECO LODGE  
CONSTRUCTION AT IDUKKI  
(CONSTRUCTION OF MODULAR  
KITCHEN,DRAINAGE,PARKING  
YARD,SIDE WALL,WOOD WORK  
POLISHING,ELECTRICAL WORKS &  
GENERATOR ROOM).**

**Name of Project Engineer:DON BABY**



**Name of contractor** : M/S VJ Raju and Co.  
**Agreement date** : 21.10.2021  
**Agreed Amount** : Rs.71,96,599.18  
**Agreed Amount With GST** : Rs. 80,60,191.08  
**Site Handover date** : 31-10-2021  
**Project duration** : 03 months  
**Scheduled Date of Completion** : 31-03-2022  
**Expected Date of completion** : 14-05-2022

**Status of Work in terms of components:**

- Modular kitchen-100%
- Wood work polishing - 100%
- Electrical works - 96%
- Generator room-92%
- Drainage-100%
- Parking yard-100%
- Handrail- 100%

**Works done in the last week**

- Generator works
- Solar lamp post earthwork & base concrete

**Scheduled progress as on 15.05.22- 100%**

**Achieved progress as on 15.05.22 - 92.5%**

**Last week progress : 92.5%**

**Current week progress : 93%**

**Current Bill Status : Part bill submitted**

**Current Financial Progress : NIL**

**Images of works done at Site during last week**



PEERMADE  
GUEST HOUSE  
RENOVATION  
(TOURISM)

UPGRADATION AND RENOVATION OF  
GOVT. GUEST HOUSE PEERMADE ,  
IDUKKI

**Name of Project Engineer: TEENU AUGUSTINE**

Name of contractor :SRI BIBY SCARIA  
Agreement date : 30-06-2020  
Agreed Amount : Rs.1,45,51,908.00  
Agreed Amount With GST : Rs. 1,71,71,251.44  
Site Handover date : 13-07-2020  
Project duration : 9 months  
Scheduled Date of Completion :13-04-2021  
Expected Date of completion : 31-10-2022

Scheduled progress as on 14-05-2022- 80 %

Achieved progress as on 14-05-2022 - 51 %

Last week progress -49 %

Current week progress - 51%

Current Bill Status : 1st and part bill submitted RS-12,15,770 (with GST)

Current Financial Progress : 15%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Guest house renovation - 15%
- Service block renovation - 85%
- Water tank - 85%
- Parking shed - 0%
- Conference hall - 70%

**Works done in the last week**

- Carpentry and painting works of annex building on progress
- Plastering works of water tank completed
- Ceiling works of annex building on progress



**PANCHALIMEDU  
(TOURISM)**

**PANCHALIMEDU TOURISM PROJECT  
PHASE – 2  
PERUVANTHANAM VILLAGE,  
PEERMEDU TALUK, IDUKKI DISTRICT**

**Name of Project Engineer: TEENU AUGUSTINE**

Name of contractor : EASYINFRA INC, TVM  
Agreement date : 22/12/2020  
Agreed Amount : ₹2,43,99,440.78  
Agreed Amount With GST : Rs. 2,73,27,373.67  
Site Handover date : 01-01-2021  
Project duration : 12 months  
Scheduled Date of Completion : 31-12-2021  
Expected Date of completion : 31-12-2021

Scheduled progress as on 14-05-2022 - 50 %

Achieved progress as on 14-05-2022 - 17 %

Last week progress - 17 %

Current week progress - 17 %

Current Bill Status : 1st and part bill submitted Rs-16,68,292/- (with GST)

Current Financial Progress : 10 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Renovation of panchalikulam - 50%
- Construction of pathway - 50%
- Proposed check dam - 20%
- Proposed lighting system - 0%
- Sitting benches - 0%
- Landscaping - 0%
- Rope cycling - 0%

**Works done in the last week**

- Work stopped due to heavy rain
- Dewatering of check dam foundation progressing
- Earthwork excavation of check dam started
- RR works for retaining wall on east side of check dam started
- RR works of panchalikulam on progress



PEERMADE  
(TOURISM)

**CONSTRUCTION OF PARKING YARD,  
COMPOUND FENCING, SERVICE  
BLOCK, AMBIENT LIGHTING AND  
MODULAR KITCHEN AT ECOLODGE  
PEERMADE**

**Name of Project Engineer: TEENU AUGUSTINE**

**Name of contractor** : Outlook communications pvt.ltd.  
**Agreement date** : 08-10-2021  
**Agreed Amount** : ₹80,27,681.98  
**Agreed Amount With GST** : Rs.9472664.74  
**Site Handover date** : 11-10-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :10-10-2022  
**Expected Date of completion** : 10-10-2022

**Status of Work in terms of components:**

- Fencing - 0%
- Service block - 80%
- Security cabin - 85%
- Diesel generator - 70%
- Modular kitchen - 90%
- Generator room - 50%
- Electrical works -0%
- Civil work for lamp post - 0%

**Works done in the last week**

- Plastering works of service block progressing
- Demolishing brickwork of service block completed
- Placing of modular kitchen items on progress
- Dethuttering of service building roof on completed
- Flooring of kitchen on completed
- Plastering work of security cabin completed

**Scheduled progress as on 14-05-2022 - 46 %**

**Achieved progress as on 14-05-2022 - 46 %**

**Last week progress - 43 %**

**Current week progress - 46 %**

**Current Bill Status : 1st and part bill submitted**

**Current Financial Progress : 28 %**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN KOTTAYAM DISTRICT



**ITI  
ETTUMANOOR  
(KASE)**

# **UP GRADATION OF GOVT ITI ETTUMANOOR ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: Anjaly C R**

**Name of contractor** : Swathy Construction  
**Agreement date** : 30-07-2020  
**Agreed Amount** : ₹ 6,95,25,557.81  
**Agreed Amount With GST** : ₹ 7,78,68,624.74  
**Site Handover date** : 10-08-2020  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 09-08-2021  
**Expected Date of Completion** : Within this Financial Year

**Scheduled progress as on 14-05-2022- 98 %**

**Achieved progress as on 14-05-2022 - 86 % ( As per revised Estimate)**

**Last week progress - 86%**

**Current week progress - 0%**

**Current Bill Status : CC 8<sup>th</sup> and part is under preparation**

**Current Financial Progress : 72%**

**Status of Work in terms of components:**

- Main building civil works (72%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (20%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (35%)
- External lighting (0%)
- Fire protection works (20%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

**Works were done in the last week - Main building civil works**

- Road works completed.
- Furniture aligning works completed.
- Front gate ACP works completed.
- ELV works completed

**Images of works done at Site during last week (with time stamp)**



**SIHM PALA  
(TOURISM)**

**SETTING UP OF STATE INSTITUTE  
OF HOTEL MANAGEMENT  
STUDIES AT PALA, KOTTAYAM  
DISTRICT, CONSTRUCTION OF  
ACADEMIC BLOCK**

**Name of Project Engineer: DON BABY**

Name of contractor : SITCO Associates  
Agreement date : 01-03-2016  
Agreed Amount : ₹13.48 Cr  
Site Handover date : 10-03-2016  
Project duration : 18 months  
Scheduled Date of Completion : 31/10/2017  
Expected Date of completion : 31/12/2021

Scheduled progress as on 15-05-2022 - 90%

Achieved progress as on 15-05-2022 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

**Works were done inEx the last week**

- No works have been done. Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.



# PROJECTS IN ALAPPUZHA DISTRICT

**ITI  
CHENGANNUR  
(KASE)**

**UP-GRADATION OF GOVT ITI  
CHENGANNUR ON PAR WITH  
INTERNATIONAL  
STANDARDS - PHASE 1- REV 3**

**Name of Project Engineer: LEKSHMY GOPAN**

**Name of contractor** : Creators Construction  
**Agreement date** : 15/10/2020  
**Agreed Amount** : Rs 18 Cr  
**Agreed Amount With GST** : Rs20,64,45672/-  
**Site Handover date** : 31/10/2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29/04/2023  
**Expected Date of completion** : 30/04/2023

**Scheduled progress as on 14/5/2022 : 30%**

**Achieved progress as on 14/5/2022 : 22%**

**Last week progress in : 1%**

**Current week progress in: 1%**

**Current Bill Status** : 1st part bill submitted to KIIDC

**Current Financial Progress in %: Nil**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Main building civil works (9%)
- Existing class room converted to smart classrooms (0%)
- Sump tank , substation works (0%)
- Road and ancillary works(0%)
- Land development (5%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

**Works done in the last week :**

- . Reinforcement works
- . Backfilling works for main building and hostel building
- . Plinth beam concrete



**ALAPPUZHA  
CANALS  
PHASE.01  
(KIIFB)**

# **MODERNIZING WATER TRANSPORT IN ALAPPUZHA CANALS-PHASE 01**

**Name of Project Engineer: Stephy Sebastian**



Name of contractor : TBAS Construction, Aluva  
Agreement date : 15-02-2019  
Agreed Amount : ₹48.35 Cr  
Agreed Amount With GST : Rs. 54,15,71,596.79  
Site Handover date : 19-02-2019  
Project duration : 12 months  
Scheduled Date of Completion : 18-02-2020  
Expected Date of completion : 30-08-2022

**Status of Work in terms of components:**

- All agreed works has been completed
- The repair of sunken road(near Pagoda resorts) is under progress.
- Construction of damaged road using interlock paver tiles in progress

**Works done in the last week**

- Dismantling of damaged retaining wall
- Driving down of coconut piles
- construction of retaining wall using gabion.
- Laying of GSB for road in progress.

Scheduled progress as on 14-05-2022 - 99%

Achieved progress as on 14-05-2022 - 98%

Last week progress in 97%

Current week progress- 1%

Current Bill Status : Rs.47,65,31,121 upto 6th bill

Current Financial Progress :88%

Images of works done at Site during last week (with time stamp)



**PUNNAMADA  
(TOURISM WORK )**

# **Punnamada- Starting Point Pathway and Boat Landing at Alappuzha District.**

**Name of Project Engineer: Stephy Sebastian**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.11 Cr  
Agreed Amount With GST : Rs. 1,23,77,355.31  
Site Handover date : 05-05-2021  
Project duration : 6 months  
Scheduled Date of Completion : 04-11-2021  
Expected Date of completion : 30-08-2022

Scheduled progress as on 14/05/2022- 98%

Achieved progress as on 14/05/2022 - 90%

Last week progress - 80%

Current week progress - 10%

Current Bill Status : 46,71,545/-

Current Financial Progress in %: 40%


Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Pathway
- Solar Lighting

**Works done in the last week**

- Laying GSB
- Laying paver blocks
- Landscaping works
- Erection of solar LightLights
- Truss work for waiting sheds

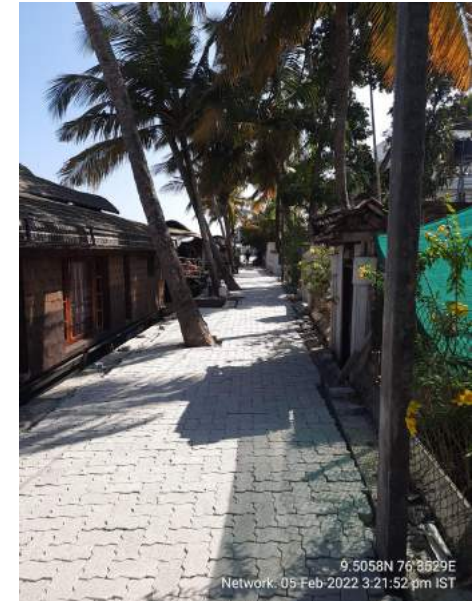

**CHUNGAM  
(TOURISM WORK )**

**CHUNGAM(CHAKREPURAKKAL)-  
KAYALCHIRA PATHWAY  
DEVELOPMENT AND BOAT  
LANDING BY THE SIDE OF  
PUNNAMADA RIVER, At  
ALAPPUZHA DISTRICT**

**Name of Project Engineer: Stephy Sebastian**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 2.99 Cr  
Agreed Amount With GST : Rs. 3,34,07,087.37  
Site Handover date : 05-05-2021  
Project duration : 9 months  
Scheduled Date of Completion : 04-02-2022  
Expected Date of completion : 30-08-2022

Scheduled progress as on 14/05/2022 - 100%

Achieved progress as on 14/05/2022 - 70%

Last week progress - 64%

Current week progress - 6%

Current Bill Status : CC 1st and part bill: Rs.86,99,563

Current Financial Progress in %: 26%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

**Works done in the last week**

- Backfilling of earth and Construction of Rubble masonry Retaining wall for Pathway and Boat landing
- Backfilling behind Pile and slab retaining wall
- Anchor belt and beam concrete in progress
- Filling of pavement



**GROYNES AT  
AMBALAPUZHA  
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP  
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at  
Ambalapuzha South, North panchayath and  
Punnapra South Panchayath**

**Name of Project Engineer: SILPA R**

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 51.3 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 15-06-2022

**Status of Work in terms of components:**

- 20m groynes – 5 nos- 2completed
- 30M GROYNES -7nos- 2 in progress, 3completed.
- 40M GROYNES – 9 nos -5completed.
- 50M GROYNES – 9 nos -6completed.
- Sea wall length-305 m – not started
- 168350.274 MT boulders reached out of 178922 MT (94.09%)
- 2T TETRAPODS –23151nos. casted out of 23902 nos. (96.86%)
- 5T TETRAPODS – 2955 nos. casted out of 2956 nos.(99.9 %)
- Earthwork Excavation – 23131.66 m3 completed out of 45955.7 M3 (43%)

**Works done in the last week**

- 2T tetrapod casted -0nos
- 5T tetrapod casted -0nos
- Supplying and Laying of Boulders -75.200MT
- laying of boulders for,G14 in progress
- Laying of tetrapods in G19, G13completed.

**Scheduled progress as on 14/05/2022 – 92 %**

**Achieved progress as on 14/05/2022 - 90.1%**

**Last week progress - 0 %**

**Current week progress -0.1%**

**Current Bill Status** : 7 th bill submitted for an Amt of Rs.48492386.46  
Total bill amount - Rs. 450663433.14

**Current Financial Progress : 87%**

**Images of works done at Site during last week (with time stamp)**



**GROYNES AT  
ARATTUPUZHA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
21NOS GROYNES AT  
ARATTUPUZHA IN BET.CH.56.6  
TO 57.8 KM AT ARATTUPUZHA**

**Name of Project Engineer: M A FASEELA NASAR**



**Name of contractor** : Ramalingam construction Company Pvt. Ltd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹ 26. 23Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :29-01-2022  
**Expected Date of completion** :29-05-2022

**Scheduled progress as on 15/05/2022 - 92 %**

**Achieved progress as on 15/05/2022- 40 %**

**Last week progress - 3 %**

**Current week progress - 3 %**

**Current Bill Status: 4 part bill submitted for an amount of Rs 6,89,37,410.80/**

**Current Financial Progress in % : 26.28%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- 20M GROYNES - 6 NOS-Not started
- 25M GROYNES - 15 NOS- 2 cmplt, 2 ongoing
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 18234.02 (20%) ) 94497 MT
- 2T TETRAPODS - 8446 ( 85.5% ) nos casted out of 9874 NOS
- 5T TETRAPODS - 990 (41.5% ) nos casted out of 2385 NOS
- GEOMAT - 64739 M2 ( not done )
- EARTHWORK EXCAVATION - 3290 M3(not done)

**Works done in the last week**

- 2T tetrapod casted - 307 nos.
- 5T tetrapod casted - 93 nos
- Supplying and Laying of Boulders - 645.78 T (G12)
- 333 5T tetrapod layed
- 986 2T tetrapod layed



**GROYNE SITE  
AT  
PATHIYANKARA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
13NOS GROUYNE AT  
PATHIYANKARA IN BET.CH.60.1  
TO 61.6KM AT  
THRIKKUNNAPUZHA.**

**Name of Project Engineer: SILPA R**

**Name of contractor** : Ramalingam construction Company Pvt. Lmtd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹20.08Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022  
**Expected Date of completion** : 15-06-2022

**Status of Work in terms of components:**

- 1 20M GROYNES - 2 NOS-One is completed
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- 3completed and 2nos is in progress
- 4.61876.225MT boulders reached out of 74546 MT(83%)
5. 2T TETRAPODS -8930casted out of 8930NOS(100%)
6. 5T TETRAPODS - 1190nos casted out of 1199NOS(99%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

**Works done in the last week**

- Tetrapod casting is in progress
- The total no.of tetrapods casted 2T-0& 5T-0nos
- laying of boulders for G7,G9,G11 are in progress
- Groynes G1,G2 ,G3 & G5;G6 are completed
- Supplying and laying of boulders-0T

**Scheduled progress as on 14/05/2022 - 92%**

**Achieved progress as on 14/05/2022 -86%**

**Last week progress in -0%**

**Current week progress in 0%**

**Current Bill Status** :7th part bill submitted for an Amt of Rs. 12811052.37  
Total bill amount - Rs. 170854619.44

**Current Financial Progress in :85%**

**Images of works done at Site during last week (with time stamp)**



**GROYNE SITE  
AT.  
VATTACHAL  
(KIIFB)**

**KIIFB  
PROJECT – CONSTRUCTION OF  
16 NOS GROUYNE AT  
VATTACHAL IN BET. CH.53.4 TO  
CH.55.2 KM(1.8KM)  
AT ARATTUPUZHA GP**

**Name of Project Engineer: M A FASEELA NASAR**

Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹28. 83Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :29-01-2022  
Expected Date of completion :29-05-2022

Scheduled progress as on 15/05/2022 - 92 %

Achieved progress as on 15/05/2022 - 80 %

Last week progress - 4 %

Current week progress - 3 %

Current Status : 7 part bills submitted for an amt of Rs 19,22,31,192.52/-

Current Financial Progress in % : 66.66 %

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 cmpltd
- 30M GROYNES - 10 NOS- 6 cmpltd, 3 ongoing
- 40M T GROYNE - 4 Nos -1 ongoing
- TOTAL QUANTITY OF BOULDERS - 73330.364 MT (72 % ) reached out of 101487 MT
- 2T TETRAPODS - 8941( 100 %) nos casted out of 8941 NOS
- 5T TETRAPODS - 3432 (100 %) nos casted out of 3432 NOS
- GEOMAT - 4850 m2 (6 %) layed out of 76299 M2
- EARTHWORK EXCAVATION - (8191.37 m3 out of 62380 M3)

### Works done in the last week

- 2T tetrapod casted - 80 nos.
- 5T tetrapod casted - 163 nos.
- Supplying and Laying of Boulders - 600 T
- Groyne G10,G9, G7,G8,G6,G3,G2, G16 completed.
- 1695 5T tetrapods layed
- 4243 2T layed.



**GROYNES SITE AT  
KATTOOR  
(KIIFB)**

**Construction of 34 nos. Groyne  
at Kattoor from Ch.168.465KM  
TO CH 171.627KM (Old CH  
96.643KM TO CH 9.535 KM)**

**Name of Project Engineer:SILPA R**

**Name of contractor** : Ramalingam Construction  
Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 49.04 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 15-06-2022 as per EoT  
**Expected Date of completion** : 15-06-2022

**Status of Work in terms of components:**

- 20m groynes - 3 started out of 3
- 30m Groynes-5nos started out of 7
- 40m groynes - 19 nos started out of 24
- Total boulders quantity - 150594.38MT boulders reached out of 174010 MT (86.54%)
- 2T TETRAPODS – 21553 nos (99.95%) casted out of 21562 nos.
- 5T TETRAPODS – 3144(100%) nos. casted out of 3144 nos.
- Geomat - 14015.5m2
- Earthwork Excavation - 31767.090m3 out of 42122 M3

**Works done in the last week**

- 2T tetrapod casted - 0nos.
- 5T tetrapod casted - 0nos.
- Supplying and Laying of Boulders-3187.25 MT
- laying of boulders for,G22,G21,G25,G15,G12,G27are in progress.
- Laying of tetrapods at G6,G18,G19,G20 finished

**Scheduled progress as on 14-05-2022 –92 % (as per EoT given)**

**Achieved progress as on 14-05-2022- 89.500%**

**Last week progress - 1%**

**Current week progress -1.5%**

**Current Bill Status :7<sup>th</sup> bill submitted for an Amount of Rs.2,82,93,879.56/- .Total bill amount - Rs. 41,21,82,538.03**

**Current Financial Progress : 84%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN KOLLAM DISTRICT



**ITI CHANDANATHOPE  
(KASE)**

**UPGRADATION OF GOVT. ITI  
CHANDANATHOPE ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of Project Engineer: MEENU ES**

Name of contractor : Asian Constructions  
Agreement date : 16-12-2020  
Agreed Amount : ₹3.65 Cr  
Agreed Amount With GST : Rs. 4,09,28,822.77  
Site Handover date : 24-12-2020  
Project duration : 8 months  
Scheduled Date of Completion :23/08/2021  
Expected Date of completion : 31/07/2022

**Status of Work in terms of components:**

- Main building civil works –51%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works –3%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

**Works done in the last week**

. Main building AAC block work  
. Electrical works  
. Plastering works  
Tile work completed  
Primer work  
Fin wall work in Progressing..

**Scheduled progress as on 14/05/2022 - 100%**

**Achieved progress as on 14/05/2022 - 58%**

**Last week progress : 44%**

**Current week progress :5%**

**Current Bill Status :1st bill submitted to KASE, 2nd bill submitted to KASE**

**Current Financial Progress in %: NIL**

**Images of works done at Site during last week (with time stamp)**



**Thenmala  
(Tourism Project)**

# **IMPROVEMENT AND DEVELOPING ECO-TOURISM AT THENMALA DAM IN KOLLAM DISTRICT**

**Name of Project Engineer:Meenu ES**

Name of contractor : Tomy Vallamattom  
Construction  
Agreement date : 29-10-2020  
Agreed Amount : ₹4.5 Cr  
Agreed Amount With GST : Rs. 4,49,90,000.00  
Site Handover date : 09-11-2020  
Project duration : 15 months  
Scheduled Date of Completion : 08-02-2022  
Expected Date of completion : 31/05/2022

Scheduled progress as on 14/05/2022- 100%

Achieved progress as on 14/05/2022-59%

Last week progress -3%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- SHOP (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)  
pavilion(50%)

**Works done in the last week**

1. Toilet, security room and cloak room-plinth beam work completed.column shuttering work under progress.brick work in progress
2. Shed to shop -roof slab concrete completed
3. Pavilion-step Work progress
4. Seating area clearance completed.



**ITI  
DHANUVACHAPU  
RAM  
(KASE)**

**UPGRADATION OF GOVT. ITI  
DHANUVACHAPURAM ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of Project Engineer: ATHEESH P MOHAN**

Name of contractor : Heather Construction  
Agreement date : 25-11-2019  
Agreed Amount : ₹11.18 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 04-12-2019  
Project duration : 20 months  
Scheduled Date of Completion : 03-04-2022  
Expected Date of completion : 03-04-2022

**Scheduled progress as on 13-05-2022- 80%(Scope of the work were increased as per the instructions from SPV)**

**Achieved progress as on 13-05-2022 - 89%**

**Last week progress - 84%**

**Current week progress - 5%**

**Current Bill Status :**12th bill were passed, Amount up to 12th bill:74357280.73/- (limited amount) ,14th bill submitted amount:6454677.55/-

**Current Financial Progress :74.77%**

**Status of Work in terms of components:**

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering completed
- GF primer work 98% Completed
- GF Electrical (Concealed)work completed
- GF plumbing work 90% completed
- FF Block Work 98% completed
- FF Ceiling work 100% completed
- FF plastering 95% completed
- Dummy column RCC completed
- FF Elec- concealed work completed
- Parapet plastering completed
- GF Tile work 98%
- FF primer work 85% completed

**Works done in the last week**

- GSB laying
- Retaining wall rubble works, Rcc belt concrete
- Security cabin brick work,
- Front gate brick works,
- Roof top plastering
- Ponting works, putty and painting works,
- Hvac works at seminar halls, electrical works.



## LIST OF TOURISM DEPARTMENT COMPLETED PROJECTS

(PHYSICAL PROGRESS 100%)

Sl. No.	Name of Project	Financial Progress	Remarks
1	Karappuzha Phase III - Construction of Viewing Tower, Bamboo Pavilion and Bridge (Wayanad)	100.00%	-
2	Karappuzha Phase III - Construction of Pathway, Fishing Dock, Pond, Gazebo, Parking yard and Landscaping (Wayanad)	100.00%	-
3	Development of Peruvannamuzhi Dam Tourism Project in Kozhikode District	65.22%	4 <sup>th</sup> and final bill amounting to ₹1,07,88,549.00 submitted to Department of Tourism for release of payment on 20.04.2022.
4	Additional Work I of Eco Lodge Construction at Idukki	100.00%	-
5	Additional Work II of Eco Lodge, Idukki	0.00%	First and part bill amounting to ₹36,81,648.00 submitted to Department of Tourism on 14.03.2022. (Contract PAC: ₹45,85,722.41). Revised Estimate preparation under progress.
6	Providing Temporary Rest Room cum Store (Container Type) for Life Guards at Alappuzha Beach	0.00%	First and final bill amounting to ₹11,96,272.00 submitted to Department of Tourism on 23.03.2022.
