


KIIDC WEEKLY PROGRESS REPORT



KIIDC

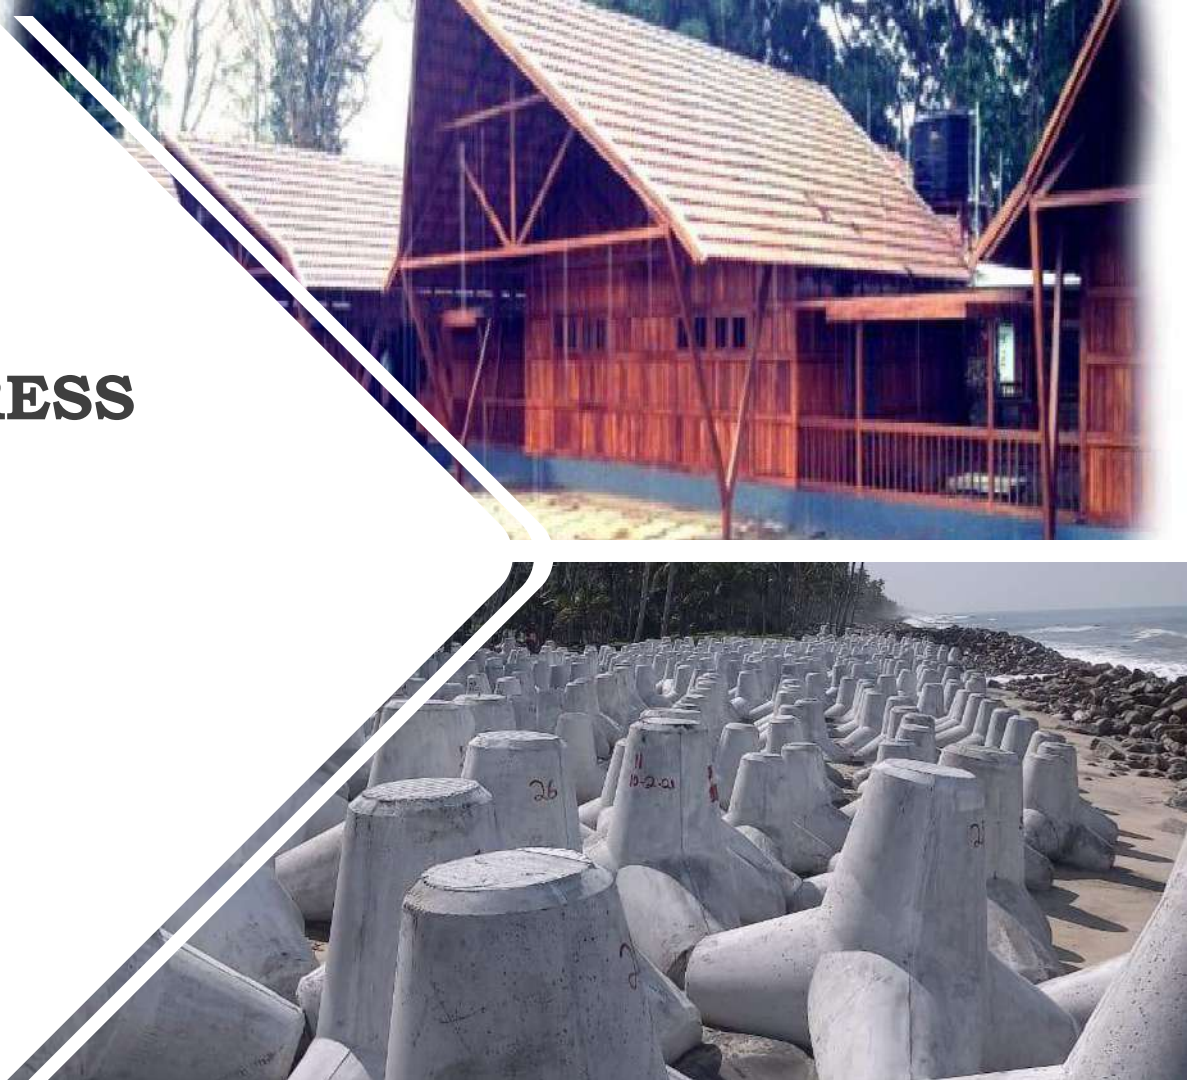

PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

UPGRADATION OF GOVT. ITI KANNUR ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: Joel J Varghese

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount :Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion : 17-05-2022

Scheduled progress as on 28-05-2022 51%

Achieved progress as on 28-05-2022 31%

Last week progress in 30%

Current week progress - 30%

Current Bill Status : 2nd Bill on progress

Current Financial Progress :30%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

Footing works 100 % completed

Stub columns, Grade beam concreting 100% completed

Ground floor columns concreting 100% completed

Block Work 85%

Internal Plastering 30%

Parapet Wall 75%

Work done in last week

Internal wall plastering

Parappet wall

Floor PCC

Fixing of Window Grill

Finnwall Blockwork

Roofing Sheet



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF
REGULATOR WITH LOCK ACROSS
ANCHARAKANDY RIVER AT
PARAPRAM IN PINARAYI
PANCHAYATH, KANNUR DISTRICT**

Name of Project Engineer : Akhil P A

Name of contractor : PGCC
Agreement date :06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion : 15-05-2022
Expected Date of completion : 15-05-2022

Scheduled progress as on 28-05-2022 100%

Achieved progress as on 28-05-2022 - 62%

Last week progress in 1 %

Current week progress - 0.5%

Current Bill Status :Sixth Part Bill submitted

Current Financial Progress : 48%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- eWing Wall (Left Bank U/S & D/S Retaining wall upto Apron portion): Completed.
- Pier P1 & P2: Pier Head Concreting completed.
- Abutment A1: 10th lift concreting (+8.40m).
- Foot slab: Left bank upto P2 completed.
- Stair case: Left Bank completed.

Works done in the last week

- Main Regulator pile are reached 100%
- Sheet pile driving work completed
- P3 lock wall line wall concrete completed
- Loose Apron work started
- Lock wall Concrete progressing at P4 line.



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY (KIIFB)**

**CONSTRUCTION OF REGULATOR
CUM BRIDGE ACROSS KUPPAM
RIVER IN KOOVERY-KATTAMPALLY
IN CHAPPARAPADAVU PANCHAYAT ,
THALIPARAMBA TALUK, KANNUR
DISTRICT**

Name of Project Engineer: Akhil P A

Name of contractor : Infab Infrastructures Ltd
Agreement date : 15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Status of Work in terms of components:

- Work gets halted for the last one year because of the case filed by previous contractor to the honorable high court.
- Survey work for finalising land acquisition area has finished.
- Side protection and approach road measurements finalised.

Works done in the last week

- Nil

Scheduled progress as on 28-05-2022 100%

Achieved progress as on 28-05-2022 - 0%

Last week progress in 0%

Current week progress - 0%

Current Bill Status :NA

Current Financial Progress :0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2

Phase 1- 14 projects- As received - 40.95 crores		
Phase 2- 14 projects-AS received - 37.212 crores (Total AS received for 28 Projects – 78.162)		
	Phase 1	Phase 2
• MoU signed – 18 projects	Pindali kalari, Andalurkav Temple, Illikunnu church, Kottiyoor siva temple, Makreri temple, Lokanarkav temple, Thrissillery temple, Thirunelli temple, Thiruvangad Ramaswamy temple, Jagannath temple	Kadirur suryanarayana temple, Chirakkakavu temple, Mridangasaileswary temple, Oorpazhichikaav temple, Puralimala temple, Peralassery temple, Valliyoorkav temple, Thacholi manikoth
• Agreement executed - 10 projects	Pindali kalari, Andalurkav Temple, Kottiyoor siva temple- Streetscape, Kottiyoor siva temple-Tourist amenities, Lokanarkav temple, Makreri Subramanyaswmi temple, Illikunnu church, Jagannath temple	Puralimala temple, Pazhassiraja smrithimandapam
• Works started – 9 (GFC drawing prepared by KIIFB)	Andalurkav temple, Illikunnu church, Pindali kalari, Kottiyoor temple- Streetscape, Kottiyoor siva temple- Tourist amenities, Jagannath temple, Lokanarkav temple, Makreri Subramanyaswami temple	Puralimala temple
• Selection notice issued - 8 projects	Thiruvangad Ramaswamy temple, Thirunelli Temple, Thrissillery Temple	Sree Thacholi Manikoth Temple, Vadakara Tazhe angadi, Peralassery Temple, Chirakkakav temple, Thalakkal Chandu Museum - Panamaram

**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2

	Phase 1	Phase 2
<ul style="list-style-type: none"> • Tender to be finalized - 2 Projects 	Municipal Stadium (THP Office), Kakkulangara Mosque (Letter submitted to Tourism for tender excess approval)	
<ul style="list-style-type: none"> • To be retendered - 2 projects (After revising the TS in DSR 2018) 	Odathil Mosque and Paris Hotel Street	Kadirur Surya Narayana Temple
<ul style="list-style-type: none"> • TS to be issued - 4 projects 		Sree Mridanga Saileswari Temple, Thodeekalam Siva Temple, Sree Oorpazhachi Kavu Temple, Valliyoorkavu temple
<ul style="list-style-type: none"> • To be dropped - 2 projects (NOC not received) 		Pazhassi Kovilakam (Mattannur), Arakkal Kettu (Total amount – 10.5Cr)

**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT - PHASE 1
-Pazhassi Circuit - Pindali Kalari
House(Pathway,Conservation of
Kalarithara,Pond restoration ,Seating,
Landscaping ,Electrification)at
Iritty,Kannur**

Name of Project Engineer:Joel J Varghese

Name of contractor : M/s Classic Builders
Agreement date : 17-02-2021
Agreed Amount : ₹ 0.6238 Cr
Agreed Amount With GST : Rs. 6987127.71
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-02-2022
Expected Date of completion :

Scheduled progress as on 28-05-2022 : 50%

Achieved progress as 28-05-2022 - 25%

Last week progress - 50%

Current week progress -30%

Current Bill Status : Ready for Part 1 bill

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

Gallery Work 100 % completed

Kalarithara 50%

Kalasamandaapam 25%

Pond 5%

Works done last Week:

Kalasamandapam

Pond Works

Kalarithara



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 - Cultural Circuit -Andalur Kavvu

Name of Project Engineer: Akhil P A

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.5189 Cr
Agreed Amount With GST : Rs.
Site Handover date : 1.701 Cr
Project duration : 12 months
Scheduled Date of Completion : 26-02-2022
Expected Date of completion :

Status of Work in terms of components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

Work done in last week

- Sadrahalli stone pavement progressing
- KIIFB Resident Engineer inspection was done

Scheduled progress as on 28-05-2022 : 100%

Achieved progress as 28-05-2022 - 17 %

Last week progress - 0%

Current week progress -0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -illikunnu

Name of Project Engineer: Akhil P A

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26/02/2021
Agreed Amount : ₹ 8300000
Agreed Amount With GST : Rs
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 26/02/2022
Expected Date of completion :

Status of Work in terms of components of cemetery :

- Land scaping of cemetery area
- Lighting
- Conservation of ceiling,wood work, joinery

Work done in last week

- Compound laterite work in progressing
- Sadarahalli pavement started.
- KIIFB Resident Engineer inspection has done.



Scheduled progress as on 28-05-2022 : 100%

Achieved progress as 28-05-2022 - 30%

Last week progress - 1%

Current week progress -1%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -Jaganath Temple

Name of Project Engineer: Akhil P A

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26/02/2021
Agreed Amount : ₹ 1,48,17,938.56
Agreed Amount With GST : 1.56cr

Site Handover date : 08/03/2021
Project duration : 12 months
Scheduled Date of Completion : 08/03/2022
Expected Date of completion :

Status of Work in terms of components :

- Pathway
- Rivival of pond
- Compound wall
- Landscaping

Work done in last week
Compound laterite work in progressing

- GSB work progressing for pathway
- Sadrahalli stone laying progressing

Scheduled progress as on 28-05-2022 : 100%

Achieved progress as 28-05-2022 - 27%

Last week progress - 0%

Current week progress -1%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY HERITAGE
PROJECT-PHASE 1-pazhassi circuit –kottiyoor shiva
temple(streetscape,landscaping,agrashala,carpark
ing,stage and electrical work at kottiyoor shiva
temple in irrity,Kannur district)**

Name of Project Engineer:Basil George

Name of contractor : M/s Rubicon construction
Agreement date : 05/10/2021
Agreed Amount : ₹ 1.21 cr
Agreed Amount With GST : RS 1,36,06,740.60
Site Handover date : 14/10/2021
Project duration : 12 months
Scheduled Date of Completion : 13-10-2022
Expected Date of completion : 13/10/2022

Status of Work in terms of components:

- Streetscape
- Landscaping
- Agrashala
- Car parking
- Stage
- electrification

Work done in last week

Ootupura-foundation work in progress
Laying narasapuram stone-streetscape work

Work delayed due to temple festival

Scheduled progress as on 28-05.2022 : 60%

Achieved progress as 28-05-2022 - 50%

Last week progress - 0%

Current week progress -0%

Current Bill Status : 1st bill submitted

Current Financial Progress : 17%

Images of works done at Site during last week (with time stamp)



COMPREHENSIVE DEVELOPMENT OF MUZHAPPILANGAD AND DHARMADOM BEACH IN KANNUR DISTRICT

IN PRINCIPLE SANCTION : 233.71 Cr

FUNDING AGENCY : KIIFB

The whole project is divided into 4 Character areas

AS Amount for Character Area 1 : 79.51 Cr

CA 1 - AS DATE : 17/03/2022

CA 1- TS DATE : 22/03/2022

CHARACTER AREA 1

- ❖ CRZ clearance obtained
- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai and revised architectural drawing prepared by consultant architect received on 01.12.2021
- ❖ KIIFB approved Character area 1 for an amount 79.51 Cr on 17.03.2022
- ❖ Work tendered and tender opened on 23.04.2022
- ❖ 5 bidders quoted for the work. 4 were PQ qualified. Opened Financial bid on 31-05-2022. M/s ULCCS is the L1 bidder.

CHARACTER AREA 2

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

CHARACTER AREA 3

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

CHARACTER AREA 4

- ❖ DPR and detailed project components are under preparation with Consultant architect CBRE

PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS
POONUR
PUZHA-POOLAKAD
AVU (KIIFB)**

**KIIFB PROJECT CONSTRUCTION
OF RCB ACROSS POONUR PUZHA
NEAR KWA PUMPING HOUSE AT
POOLAKADAVU IN KURUVATTOOR
PANCHAYATH**

Name of Project Engineer: Athul Ashar

Name of contractor : ULCCS Ltd.
Agreement date : 18-08-2021
Agreed Amount : ₹22,68,45,702.29
Agreed Amount With GST : Rs.
Site Handover date : 27-08-2021
Project duration : 18 months
Scheduled Date of Completion : 26-02-2023
Expected Date of completion : 26-02-2023

Status of Work in terms of components:

- 43 no of pile foundation is completed out of 48
- Piling work for P1,P2 & P3 are complete
- Piling work for A1 & A2 are ongoing
-

Works done in the last week

- Land acquisition proposal is submitted.
- Piling work for A2
-

Scheduled progress as on 28-05-2022 - 25%

Achieved progress as on 28-05-2022- 15%

Last week progress- 2 %

Current week progress - 1 %

Current Bill Status : nil

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)



**ITI KOYILANDY
(KASE)**

**UPGRADATION OF GOVT. ITI
KOYILANDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of Project Engineer: Basil George

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion :13-08-2021
Expected Date of completion :13-11-2021

Status of Work in terms of components:

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

Works done in the last week

- Work delayed

Scheduled progress as on 28-05-2022- 100%

Achieved progress as on 28-05-2022 - 85%

Last week progress- 0%

Current week progress - 0%

Current Bill Status : CC 3rd and part submitted

Current Financial Progress : 34.3%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY HERITAGE
PROJECT-PHASE 1-pazhassi circuit –
Lokanarkavu Temple (Conservation of
Thantrimadom, Folklore, Oottupura,Chiras,
Plumbing and Electrification at
Lokanarkavu Temple in Vadakara,
Kozhikode District)**

Name of Project Engineer:Basil George

Name of contractor : Saaj Constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3,78,74,574.27/-
Agreed Amount With GST : Rs.
Site Handover date : 27-06-2021
Project duration : 12 months
Scheduled Date of Completion :
Expected Date of completion :

Status of Work in terms of components:

- thanthrimadam up to plinth belt were completed.
- big chira side protection work in progress.
- compound wall work

Workshops done in the last week

- big chira DR masonry works.
- compound wall excavation works
- Thanthrimadam- laterate masonry works up to lintel level

Scheduled progress as on 28-05-2022- 90%

Achieved progress as on 28-05-2022 - 4%

Last week progress- 1%

Current week progress - 1%

Current Bill Status :

Current Financial Progress :

Images of works done at Site during last week (with time stamp)



**RCB
PERINCHERIKADAVU
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM
BRIDGE AT U/S OF
PERINCHERIKADAVU IN KUTTIADY
RIVER (GULIKAPUZHA) AT KOZHIKODE
DISTRICT**

Name of Project Engineer: Basil George

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 61,13,34,133.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022
Expected Date of completion :01-03-2024

Scheduled progress as on 28-05-2022 - 85%

Achieved progress as on 28-05-2022 - 22%

Last week progress in 8.5%

Current week progress 10%

Current Bill Status : 2 nd bill submitted

Current Financial Progress : 17%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- RCB – 10%
- Bank Protection works – 17%
- Material collection works are going on.(Coconut posts supplying)

Works done in the last week

- Pile chipping-abutment
- Earth work excavation for pile cap
- Pile cap for retaining wall and wall concrete



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

KIIFB Project - Construction of Regulator at Puzhankavu across Kadalundi River

Name of Project Engineer: RAHEES.P

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 10,97,21,287.89
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion :16/06/2021-(10/05/2022)
Expected Date of completion :15/06/2022-(1/05/2022)

Scheduled progress as on 28-05-2022-95%

Achieved progress as on 28-05-2022 -94%

Last week progress -0%

Current week progress - 0%

Current Bill Status : Total Bill submitted ₹7.10 Crores (9th part bill)

Current Financial Progress in :72.53%

Images of works done at Site during last week

Status of Work in terms of components:

- four piers completed including Hammer head portion.
- Right & Left side Abutments completed up to hammer head level..
- Right side retaining wall u/s 110/110m & d/s 50/50m completed.
- Left side retaining wall total U/S-87/110 L/S-D/S- 53/53m retaining wall completed.

Works done in the last week

- Guard room masonry work ongoing
- Continuing Heavy raining at site.
- Electrical drawings not finalised yet.



**RCB
Moothikkayam
(KIIFB)**

KIIFB - Construction of Regulator cum Bridge across thoothapuzha keezhmurikadavu moothikkayam in moorkanad panchayath

Name of Project Engineer: RAHEES.P

Name of contractor : M/s PGCC Pvt,Ltd
Agreement date : 18/09/2020
Agreed Amount : ₹57.56 Cr
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 26-09-2020
Project duration : 18 months
Scheduled Date of Completion :26-03-2022
Expected Date of completion :26/12/2022

Scheduled progress as on 28-05-2022 - 100%

Achieved progress as on 28-05-2022 - 34%

Last week progress -1%

Current week progress -1%

Current Bill Status : Fourth bill submitted

Current Financial Progress : 24.84%

Images of works done at Site during last week (with time stamp)

**STATUS OF WORK IN
TERMS OF COMPONENTS**

- 64 OUT OF 64 piles completed
- girder beam 28/28 concreted and erected.
- Open footing 6 out of 6 completed
- side protection
1)D/S-R/S- 216/260 M raft completed.
2)U/S-R/S- 251/600m raft completed. 206 m partially completed

Works done in the last week

- Heavy rain occurred at site
- pile load test-platform making on going.
- Diaphragm casting work ongoing.
-



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA
(KASE)**

UPGRADATION OF GOVT. ITI MALAMPUZHA ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: NITHISH. C

Name of contractor : M/S. PERFECTENGINEERS
Agreement date : 05/03/2020
Agreed Amount : ₹11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date : 06/03/2020
Project duration : 18 months
Scheduled Date of Completion. : 05/09/2021
Expected Date of completion. : 02/06/22

Scheduled progress as on 28/05/2022- 100%

Achieved progress as on 28/05/2022 - 76.00%

Last week progress - 75%

Current week progress- 70.00%

Current Bill Status : no of bill submitted - 5, amount:- 36640193

Current Financial Progress : 28 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components

- Smart classroom promethean and writing board fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

Works done in the last week

- AAC block work at FF
- Plumbing work at FF
- FF ceiling plastering
- FF roof slab projection concreting
- FF floor tile work
- Reinforcement work of Lift wall
- Drainage wall concrete



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of Project Engineer:NITHIN J B

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-07-2022

Status of Work in terms of components:

- 10 number of pier foundations and both right and left side abutment footing concrete completed.
- 8 Sill beams erected.
- Hoisting bridge fabrication in progress.
- U/S LHS raft completed for ch: 7 to 30m.
- 123 lifts of piers out of 168 completed.
- Painting works for shutters in progress.
- 8 weir concrete completed.

Works done in the last week

- Painting works for shutters.
- Left side retaining wall raft concrete.
- Wall concrete on U/S LHS retaining wall.
- Concreting on D/S LHS wall.
- Excavation on left side protection wall area.

Scheduled progress as on 28/05/2022 - 83%

Achieved progress as on 28/05/2022 - 69%

Last week progress - 64%

Current week progress -5 %

Current Bill Status : Fifth and part bill passed.

Current Financial Progress :

Images of works done at Site during last week



**Moongilmada LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s poljo Vyapar kendra Pvt Ltd
Agreement date : 26-02-2021
Agreed Amount : ₹33288750 Crores
Agreed Amount With GST : Rs. 37283400/-
Site Handover date : 26-02-2021
Project duration : 12 months
Scheduled Date of Completion :28-02-2022
Expected Date of completion :15-03-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

.Conducting Trial Run

Scheduled progress as on 28/05/2022 - 100%

Achieved progress as on 28/05/2022 - 100 %

Last week progress in : 100%

Current week progress : %

Current Bill Status : Part Bill-3

Current Financial Progress : 90%

Images of works done at Site during last week (with time stamp)



**Moongilmada LIS
(Civil)
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Vallamattam constructions
Agreement date : 18-09-2020
Agreed Amount : ₹15422222 Crores
Agreed Amount With GST : Rs. 18198221.96/-
Site Handover date : 03-06-2021
Project duration : 6 months
Scheduled Date of Completion :03-12-2021
Expected Date of completion :31-05-2022

Status of Work in terms of components:

- Pump House
- Conversion of abonded RBC to water storage.
- Electrical Works

Works done in the last week

.Electrical works ongoing

Scheduled progress as on 28/05/2022 - 100%

Achieved progress as on 28/05/2022 - 87 %

Last week progress in : 87%

Current week progress : 0%

Current Bill Status : Part Bill-2

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)



**Valiyeri LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Valiyeri LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd
Agreement date : 24-06-2021
Agreed Amount : ₹31004000 Rupees
Agreed Amount With GST : Rs. 36581180/-
Site Handover date : 25-06-2021
Project duration : 12 months
Scheduled Date of Completion :25-06-2022
Expected Date of completion :31-05-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

.Automation Works stoped due to rain

Scheduled progress as on 30/05/2022 - 91%

Achieved progress as on 30/05/2022 - 87 %

Last week progress in : 87%

Current week progress : 1%

Current Bill Status : Part Bill-2

Current Financial Progress : 68%

Images of works done at Site during last week (with time stamp)



**Navithankulam LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at
Navithankulam LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd
Agreement date : 24-06-2021
Agreed Amount : ₹16327047.54 Rupees
Agreed Amount With GST : Rs. 19265916.09/-
Site Handover date : 25-06-2021
Project duration : 12 months
Scheduled Date of Completion :25-06-2022
Expected Date of completion :31-06-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

.Main line Works
work stopped due to rain

Scheduled progress as on 28/05/2022 - 91%

Achieved progress as on 28/05/2022 - 59 %

Last week progress in : 56%

Current week progress : 3%

Current Bill Status : Nil

Current Financial Progress :

Images of works done at Site during last week (with time stamp)



**Kunnamkatupathy
LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at
Kunnamkatupathy LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Mahendra Pvt Ltd
Agreement date : 18-11-2021
Agreed Amount : ₹36068276 Rupees
Agreed Amount With GST : Rs. 42560565.68/-
Site Handover date : 27-11-2021
Project duration : 6 months
Scheduled Date of Completion :29-05-2022
Expected Date of completion :31-06-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

work stopped due to rain

Scheduled progress as on 28/05/2022 - 93%

Achieved progress as on 28/05/2022 - 57 %

Last week progress in : 57%

Current week progress : 0%

Current Bill Status : Partbill-2

Current Financial Progress : 42%

Images of works done at Site during last week (with time stamp)



**MOOLATHARA
RIGHT BANK CANAL
PHASE 1 FROM
KORAYAR TO
VARATTAYAR
(KIIFB)**

**KIIFB-Extension of Moolathara
right bank canal phase 1 from
korayar to varattayar**

Name of Project Engineer: NITHISH.C

Name of contractor	: M/s Prathmesh & K.K.Constructions
Agreement date	: 23-12-2021
Estimate P.A.C	: Rs.158,50,00,000/-
CONTRACT P.A.C	: Rs. 174,34,95000/-
Site Handover date	: 31-12-2021
Project duration	: 30 months
Scheduled Date of Completion	:
Expected Date of completion	:

Status of Work in terms of components:

- Site clearance

Works done in the last week

.Design works

Scheduled progress as on 28/05/2022 - Nil

Achieved progress as on 28/05/2022 - Nil

Last week progress in : Nil

Current week progress : Nil

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN THRISSUR DISTRICT

**REGULATOR CUM
BRIDGE ACROSS
KURUMALI PUZHA
IN THRISSUR
DISTRICT.**

**CONSTRUCTION OF
KANATHODU REGULATOR CUM
BRIDGE ACROSS KURUMALI
PUZHA AT KUNDUKADAVU IN
PUDUKAD PANCHAYATH,
THRISSUR DISTRICT.**

Name of Project Engineer: RAHUL V R

Name of contractor : PGCC
Agreement date : 05-01-2022
Agreed Amount : 262383481.27
Agreed Amount With GST : Rs.293869499.022
Site Handover date : 13-01-2022
Project duration : 18 months
Scheduled Date of Completion : 13-07-2023
Expected Date of completion : 13-07-2023

Scheduled progress as on 28-05-2022 13.5%

Achiever progress as on 28-05-2022 - 3.5%

Last week progress- 3.5%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- in accordance with the agreement dated 05-01-2022, the type of foundation adopted was pile foundation.
- as per the boreholes taken by the contractor, it is seen that hard rock is available at depth varying 5.75m (maximum depth) to 3.2m from the bed level, hence the foundation for piers and abutments are revised to open foundation.

Works done in the last week

- Revised GFC drawings was issued on 02-04-2022
- Tiver boundary survey was completed on 18-02-2022
- Trial pits has been taken.
- Initial levels also been taken
- Work was inaugurated on 16/04/2022
- 18m ring bund achieved
- **Heavy Rain causes rise in water level so, no work at site**



**ITI CHALAKUDY
KIIFB-KASE**

UP GRADATION OF GOVT ITI CHALAKUDY ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: RAHUL V R

Name of contractor : Sidheek, M/S Sitco Associates
Agreement date : 28-10-2020
Agreed Amount : ₹ 7,47,51,405.13
Agreed Amount With GST : ₹ 8,37,21,573.74
Site Handover date : 06-11-2020
Project duration : 12 months
Scheduled Date of Completion : 05-11-2021
Expected Date of Completion :

Scheduled progress as on 28/05/2022- 0 %

Achieved progress as on 28/05/2022 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the last week

- As per drawings building setbacks are not available at the site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign



PROJECTS IN ERNAKULAM DISTRICT

**CHELLANAM
COASTAL
PROTECTION
[KIIFB]**

**KIIFB PROJECT- REFORMATION OF DAMAGED
SUNKEN SEA WALL AT CHELLANAM USING
TETRAPODS AND RUBBLE IN BETWEEN CP
STONE 976 AND 1052 FOR 10 KM STRETCHES
ALONG CHELLANAM COAST IN ERNAKULAM
DISTRICT - PHASE I FOR A LENGTH OF 7/350
KM IN BETWEEN CP 986 AND CP 1026**

Name of Project Engineer: SREELAKSHMI S

Name of contractor : M/s Uralungal Labour Contract Co-operative

Agreement date : 30-12-2021

Agreed Amount : ₹ 256,89,67,441.29

Agreed Amount With GST : ₹ 287,72,43,534.25

Site Handover date : 03-01-2022

Project duration : 16 months

Scheduled Date of Completion : 02-05-2023

Expected Date of Completion : 02-05-2023

Scheduled progress as on 29/05/2022- 30.17%

Achieved progress as on 29/05/2022 - 22.26%

Last week progress - 2.62%

Current week progress- 2.91%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work :


- 15116nos of 2T tetrapods cast.
- 11456nos of 3.5T tetrapods cast.
- Available mould 2T = 146 nos
- Available mould 3.5T = 163 nos

Total Boulders Supplied till 27.05.2022

- Core layer (10-50kg) = 70454.009 T
- Toe (200 to 400kg) = 33961.067 T
- Underlayer (150-200kg) = 17686.959 T
- Toe (250-350kg) = 53912.504 T
- Toe (350-700kg) = 39418.427 T
- Primary layer(500-800kg)=23756.951T

Works done in the last week

- 4746nos 2T and 4639nos 3.5T tetrapods are placed.
- Supplying and laying of boulders in progress at SR-1,2,3 Harbour, SR-10,11,12,13,14 Abad and SR-7,8 Bazar.

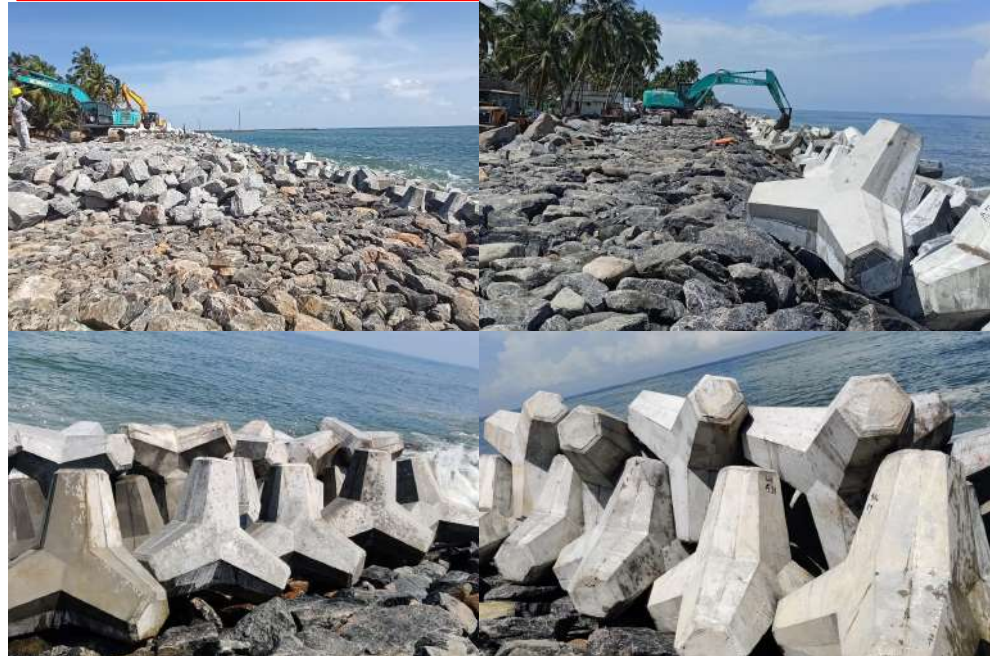

**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

Name of Project Engineer: Remya P R

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion : 26-04-2023

Scheduled progress as on 28-05-2022 - 55%

Achieved progress as on 28-05-2022- 23.5%

Last week progress - 22.5%

Current week progress - 1%

Current Bill Status :cc 2nd & part bill submitted

Current Financial Progress :20 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- REGULATOR –Pier 1 piling started.
- CONSTRUCTION OF LOCK PORTION –constructed ring bund completed,Pile boring completed
- RIVER BANK PROTECTION –not started
- CONSTRUCTION OF WATCHMAN ROOM-not started
- ELECTRICAL WORKS-not started
- MECHANICAL WORKS-not started

Works done in the last week

Piling works -
Lock portin- 56 piles,
Pier 1 & Pier 2- 8 8
piles completed
Left abutment- 4 no.s
***Ring bund
demolished due to
heavy rain & flood. It
affects the work
progress**



**ANTHAKARATHO
DU CANAL
(KIIFB)**

IMPROVEMENTS TO ANTHAKARATHODE IN THRIPPUNITHURA MUNICIPALITY

Name of Project Engineer: Princy Abraham

Name of contractor : Southern Tech
Agreement date : 29-09-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 08-10-2018
Project duration : 15 months
Scheduled Date of Completion : 07-01-2021
Expected Date of completion : 31-12-2021

Status of Work in terms of components:

- Cleaning & desilting- completed
- Side protection work- 85%
- Road and walkway formation- 70%
- Fencing and Handrail work- 70%
- Boat jetty -98%(tile work remaining)
- Skew bridge -98%(tile work remaining)
- Foot bridge-95%

Works done in the last week

- Tie beam concreting work in progress
- Road and walk way formation work in progress
- S S hand rail work in progress
- paver block work
- DR masonry work in progress

Scheduled progress as on 29-05-2022 - 98.5%

Achieved progress as on 29-05-2022 - 96%

Last week progress - 96%

Current week progress 96%

Current Bill Status : 4th bill submitted

Current Financial Progress : 65%

Images of works done at Site during last week (with time stamp)



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY-PROVIDING STREET
LIGHTS ALONG THE PATHWAYS OF
ANTHAKARATHODE**

Name of Project Engineer:Princy Abraham

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 10-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 31-12-2021

Status of Work in terms of components:

- Excavation and supply Laying of cable-75%
- Placing of lamp post, LED & feeder -75%
- Excavation and concreting-75%

Works done in the last week

- Pole painting & plastering foundation (KONOTHUPUZ HA SIDE)
- Pole fixing, Light fixing
- The remaining works depends upon the civil work (pathway).

Scheduled progress as on 29-05-2022- 84%

Achieved progress as on 29-05-2022- 82.1%

Last week progress - 82.1%

Current week progress 82.10%

Current Bill Status : Part Bill prepared

Current Financial Progress : 82%

Images of works done at Site during last week (with time stamp)



**BEAUTIFICATION
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY–LANDSCAPING &
ARBORICULTURE, CONSTRUCTION OF
KIOSK AND TOILET AND OPERATION &
MAINTENANCE FOR ONE YEAR**

Name of Project Engineer: Princy Abraham

Name of contractor : GRIDS,Digital Surveyors and
Engineering Consultants
Agreement date : 24-06-2021
Agreed Amount : ₹76.62 lakhs
Agreed Amount With GST : Rs. 8581690.00
Site Handover date : 03-07-2021
Project duration : 3 months
Scheduled Date of Completion : 02-10-2021
Expected Date of completion : 02-01-2022

**Status of Work in
terms of components:**

- Landscaping & tress-0%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

Works done in the last week

Brick work and plastering works for plantar box (CH 320-500)

The remaining works depends upon the civil work (pathway).

Scheduled progress as on 29-05-2022- 40%

Achieved progress as on 29-05-2022- 6%

Last week progress - 5%

Current week progress - 6%

Current Bill Status : NIL

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

**UP GRADATION OF GOVT ITI
KATTAPPANA ON PAR WITH
INTERNATIONAL
STANDARDS**

Name of Project Engineer: DON BABY

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 31-05-2022
Expected Date of completion : 31- 05-2022

Status of Work in terms of components:

- Work slowed down due to rain.
- Reinforcement works of grade beam - 100%
- Grade beam concrete- 100%
- Grade slab Concrete - 100%
- Roof beams and slab - 100%

Works done in the last week

- Brick works
- Electrical works
- Plastering works



Scheduled progress as on 28.05.22- 80%

Achieved progress as on 28.05.22 - 56.5%

Last week progress : 56%

Current week progress :56.5%

Current Bill Status : 4th and part bill submitted

Current Financial Progress in %:48 %

Images of works done at Site during last week

**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – III
(TOURISM)**

**ADDITIONAL WORK III OF ECO LODGE
CONSTRUCTION AT IDUKKI
(CONSTRUCTION OF MODULAR
KITCHEN,DRAINAGE,PARKING
YARD,SIDE WALL,WOOD WORK
POLISHING,ELECTRICAL WORKS &
GENERATOR ROOM).**

Name of Project Engineer:DON BABY

Name of contractor : M/S VJ Raju and Co.
Agreement date : 21.10.2021
Agreed Amount : Rs.71,96,599.18
Agreed Amount With GST : Rs. 80,60,191.08
Site Handover date : 31-10-2021
Project duration : 03 months
Scheduled Date of Completion : 31-03-2022
Expected Date of completion : 14-05-2022

Status of Work in terms of components:

- Modular kitchen-100%
- Wood work polishing - 100%
- Electrical works - 96%
- Generator room-92%
- Drainage-100%
- Parking yard-100%
- Handrail- 100%

Works done in the last week

- Generator works
- Solar lamp post earthwork & base concrete

Scheduled progress as on 28.05.22- 100%

Achieved progress as on 28.05.22 - 94%

Last week progress : 93%

Current week progress : 94%

Current Bill Status : Part bill submitted

Current Financial Progress : NIL

Images of works done at Site during last week



PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVT. GUEST HOUSE PEERMADE ,
IDUKKI**

Name of Project Engineer: TEENU AUGUSTINE

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 31-10-2022

Scheduled progress as on 28-05-2022- 80 %

Achieved progress as on 28-05-2022 - 51 %

Last week progress -49 %

Current week progress - 51%

Current Bill Status : 2nd and part bill submitted

Current Financial Progress : 35%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Guest house renovation - 15%
- Service block renovation - 85%
- Water tank - 85%
- Parking shed - 0%
- Conference hall - 70%

Works done in the last week

- Carpentry and painting works of annex building on progress
- Plastering works of water tank completed
- Ceiling works of annex building on progress



**PANCHALIMEDU
(TOURISM)**

**PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAM VILLAGE,
PEERMEDU TALUK, IDUKKI DISTRICT**

Name of Project Engineer: TEENU AUGUSTINE

Name of contractor : EASYINFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : 31-12-2021

Status of Work in terms of components:

- Renovation of panchalikulam - 50%
- Construction of pathway - 50%
- Proposed check dam - 20%
- Proposed lighting system - 0%
- Sitting benches - 0%
- Landscaping - 0%
- Rope cycling - 0%

Works done in the last week

- Work stopped due to heavy rain
- Dewatering of check dam foundation progressing
- Earthwork excavation of check dam started
- RR works for retaining wall on east side of check dam started
- RR works of panchalikulam on progress

Scheduled progress as on 28-05-2022 - 50 %

Achieved progress as on 28-05-2022 - 17 %

Last week progress - 17 %

Current week progress - 17 %

Current Bill Status : 1st and part bill submitted Rs-16,68,292/-(with GST)

Current Financial Progress : 10 %

Images of works done at Site during last week (with time stamp)



PEERMADE
(TOURISM)

**CONSTRUCTION OF PARKING YARD,
COMPOUND FENCING, SERVICE
BLOCK, AMBIENT LIGHTING AND
MODULAR KITCHEN AT ECOLODGE
PEERMADE**

Name of Project Engineer: TEENU AUGUSTINE

Name of contractor : Outlook communications pvt.ltd.
Agreement date : 08-10-2021
Agreed Amount : ₹80,27,681.98
Agreed Amount With GST : Rs.9472664.74
Site Handover date : 11-10-2021
Project duration : 12 months
Scheduled Date of Completion :10-10-2022
Expected Date of completion : 10-10-2022

Scheduled progress as on 28-05-2022 - 48 %

Achieved progress as on 28-05-2022 - 48 %

Last week progress - 46 %

Current week progress - 48 %

Current Bill Status : 1st and part bill submitted

Current Financial Progress : 28 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Fencing - 0%
- Service block - 85%
- Security cabin - 85%
- Diesel generator - 70%
- Modular kitchen - 90%
- Generator room - 50%
- Electrical works -0%
- Civil work for lamp post - 0%

Works done in the last week

- Plastering works of service block progressing
- Demolishing brickwork of service block completed
- Placing of modular kitchen items on progress
- Dethuttering of service building roof on completed
- Flooring of kitchen on completed
- Plastering work of security cabin completed



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

UP GRADATION OF GOVT ITI ETTUMANOOR ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: Anjaly C R

Name of contractor : Swathy Construction
Agreement date : 30-07-2020
Agreed Amount : ₹ 6,95,25,557.81
Agreed Amount With GST : ₹ 7,78,68,624.74
Site Handover date : 10-08-2020
Project duration : 12 months
Scheduled Date of Completion : 09-08-2021
Expected Date of Completion : Within this Financial Year

Scheduled progress as on 28-05-2022- 98 %

Achieved progress as on 28-05-2022 - 86 % (As per revised Estimate)

Last week progress - 86%

Current week progress - 0%

Current Bill Status : CC 8th and part is under preparation

Current Financial Progress : 72%

Status of Work in terms of components:

- Main building civil works (72%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (20%)
- Road and ancillary works, compound wall (0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (35%)
- External lighting (0%)
- Fire protection works (20%)
- Furniture for existing smart class room Converted to smart class rooms (0%)

Works were done in the last week - Main building civil works

- Road works completed.
- Furniture aligning works completed.
- Front gate ACP works completed.
- ELV works completed

Images of works done at Site during last week (with time stamp)



**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE INSTITUTE
OF HOTEL MANAGEMENT
STUDIES AT PALA, KOTTAYAM
DISTRICT, CONSTRUCTION OF
ACADEMIC BLOCK**

Name of Project Engineer: DON BABY

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Scheduled progress as on 28-05-2022 - 90%

Achieved progress as on 28-05-2022 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : RA Bill 12 Amount: Rs. 11,66,57,461.18

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works were done inEx the last week

- No works have been done. Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.



PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR WITH
INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

Name of Project Engineer: LEKSHMY GOPAN

Name of contractor : Creators Construction
Agreement date : 15/10/2020
Agreed Amount : Rs 18 Cr
Agreed Amount With GST : Rs20,64,45672/-
Site Handover date : 31/10/2021
Project duration : 18 months
Scheduled Date of Completion : 29/04/2023
Expected Date of completion : 30/04/2023

Scheduled progress as on 28/5/2022 : 34%

Achieved progress as on 28/5/2022 : 24%

Last week progress in : 1%

Current week progress in: 1%

Current Bill Status : 1st part bill submitted to KIIDC

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (9%)
- Existing class room converted to smart classrooms (0%)
- Sump tank , substation works (0%)
- Road and ancillary works(0%)
- Land development (5%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

Works done in the last week :

- . Reinforcement works
- . Backfilling works for main building and hostel building
- . Plinth beam concrete
- . Grade slab concrete



**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

MODERNIZING WATER TRANSPORT IN ALAPPUZHA CANALS-PHASE 01

Name of Project Engineer: Stephy Sebastian

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-08-2022

Status of Work in terms of components:

- All agreed works has been completed
- The repair of sunken road(near Pagoda resorts) is under progress.
- Construction of damaged road using interlock paver tiles in progress

Works done in the last week

- Dismantling of damaged retaining wall
- Driving down of coconut piles
- construction of retaining wall using gabion.
- Laying of GSB for road in progress.

Scheduled progress as on 28-05-2022 - 99%

Achieved progress as on 28-05-2022 - 98%

Last week progress in 97%

Current week progress- 1%

Current Bill Status : Rs.47,65,31,121 upto 6th bill

Current Financial Progress :88%

Images of works done at Site during last week (with time stamp)



**PUNNAMADA
(TOURISM WORK)**

Punnamada- Starting Point Pathway and Boat Landing at Alappuzha District.

Name of Project Engineer: Stephy Sebastian

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 04-11-2021
Expected Date of completion : 30-08-2022

Scheduled progress as on 28/05/2022- 98%

Achieved progress as on 28/05/2022 - 90%

Last week progress - 80%

Current week progress - 10%

Current Bill Status : 46,71,545/-

Current Financial Progress in %: 40%


Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Pathway
Solar Lighting

Works done in the last week

- Laying GSB
- Laying paver blocks
- Landscaping works
- Erection of solar LightLights
- Truss work for waiting sheds

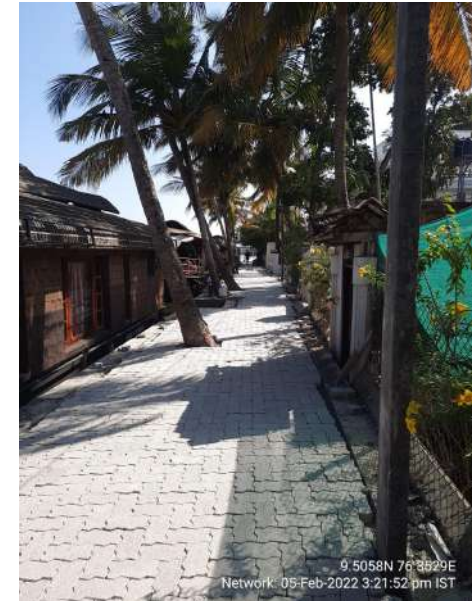

**CHUNGAM
(TOURISM WORK)**

**CHUNGAM(CHAKREPURAKKAL)-
KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of Project Engineer: Stephy Sebastian

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 30-08-2022

Scheduled progress as on 28/05/2022 - 100%

Achieved progress as on 28/05/2022 - 70%

Last week progress - 64%

Current week progress - 6%

Current Bill Status : CC 1st and part bill: Rs.86,99,563

Current Financial Progress in %: 26%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- Backfilling of earth and Construction of Rubble masonry Retaining wall for Pathway and Boat landing
- Backfilling behind Pile and slab retaining wall
- Anchor belt and beam concrete in progress
- Filling of pavement



**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of Project Engineer: SILPA R

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 15-06-2022

Status of Work in terms of components:

- 20m groynes – 5 nos- 2completed
- 30M GROYNES -7nos- 2 in progress, 3completed.
- 40M GROYNES – 9 nos -5completed.
- 50M GROYNES – 9 nos -6completed.
- Sea wall length-305 m – not started
- 168350.274 MT boulders reached out of 178922 MT (94.09%)
- 2T TETRAPODS –23151nos. casted out of 23902 nos. (96.86%)
- 5T TETRAPODS – 2955 nos. casted out of 2956 nos.(99.9 %)
- Earthwork Excavation – 23131.66 m3 completed out of 45955.7 M3 (43%)

Works done in the last week

- 2T tetrapod casted -0nos
- 5T tetrapod casted -0nos
- Supplying and Laying of Boulders -0MT
- laying of boulders for,G14 in progress
- Laying of tetrapods in G19, G13completed.

Scheduled progress as on 28/05/2022 – 92 %

Achieved progress as on 28/05/2022 - 90.1%

Last week progress - 0.1 %

Current week progress -0%

Current Bill Status : 7th bill submitted for an Amt of Rs.48492386.46
Total bill amount - Rs. 450663433.14

Current Financial Progress : 87%

Images of works done at Site during last week (with time stamp)



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of Project Engineer: M A FASEELA NASAR

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹ 26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Scheduled progress as on 28/05/2022 - 92 %

Achieved progress as on 28/05/2022- 40 %

Last week progress - 1 %

Current week progress - 3 %

Current Bill Status: 5 part bill submitted for an amount of Rs 10,23,28,679/-

Current Financial Progress in % : 39 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 6 NOS-Not started
- 25M GROYNES - 15 NOS- 2 cmplt, 2 ongoing
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 18234.02 (20%)) 94497 MT
- 2T TETRAPODS - 8670 (88 %) nos casted out of 9874 NOS
- 5T TETRAPODS - 1081 (45%) nos casted out of 2385 NOS
- GEOMAT - 64739 M2 (not done)
- EARTHWORK EXCAVATION - 3290 M3(not done)

Works done in the last week

- 2T tetrapod casted - 224 nos
- 5T tetrapod casted - 90 nos
- Supplying and Laying of Boulders - 645.78 T (G12)
- 333 5T tetrapod layed
- 986 2T tetrapod layed



**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of Project Engineer: SILPA R

Name of contractor : Ramalingam construction Company Pvt. Lmtd.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022
Expected Date of completion : 15-06-2022

Status of Work in terms of components:

- 1 20M GROYNES - 2 NOS-One is complted
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- 3completed and 2nos is in progress
- 4.61876.225MT boulders reached out of 74546 MT(83%)
5. 2T TETRAPODS -8930casted out of 8930NOS(100%)
6. 5T TETRAPODS - 1190nos casted out of 1199NOS(99%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

Works done in the last week

- Tetrapod casting is in progress
- The total no.of tetrapods casted 2T-0& 5T-0nos
- laying of boulders for G7,G9,G11 are in progress
- Groynes G1,G2 ,G3 & G5;G6 are completed
- Supplying and laying of boulders-0T

Scheduled progress as on 28/05/2022 - 92%

Achieved progress as on 28/05/2022 -86%

Last week progress in -0%

Current week progress in 0%

Current Bill Status :7th part bill submitted for an Amt of Rs. 12811052.37
Total bill amount - Rs. 170854619.44

Current Financial Progress in :85%

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

Name of Project Engineer: M A FASEELA NASAR

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :29-01-2022
Expected Date of completion :29-05-2022

Scheduled progress as on 28/05/2022 - 92 %

Achieved progress as on 28/05/2022 - 82 %

Last week progress - 2 %

Current week progress - 3 %

Current Status : 8 part bills submitted for an amt of Rs 23,13,12,922/-

Current Financial Progress in % : 80%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 cmpltd
- 30M GROYNES - 10 NOS- 6 cmpltd, 3 ongoing
- 40M T GROYNE - 4 Nos -1 ongoing
- TOTAL QUANTITY OF BOULDERS - 73968 MT (73%) reached out of 101487 MT
- 2T TETRAPODS - 8941(100 %) nos casted out of 8941 NOS
- 5T TETRAPODS - 3432 (100 %) nos casted out of 3432 NOS
- GEOMAT - 4850 m2 (6 %) layed out of 76299 M2
- EARTHWORK EXCAVATION - (8191.37 m3 out of 62380 M3)

Works done in the last week

- 2T tetrapod casted - 0 nos.
- 5T tetrapod casted - 0 nos.
- Supplying and Laying of Boulders - 600 T
- Groyne G10,G9, G7,G8,G6,G3,G2, G16 completed.
- 1695 5T tetrapods layed
- 4243 2T layed.



**GROYNES SITE AT
KATTOOR
(KIIFB)**

**Construction of 34 nos. Groyne
at Kattoor from Ch.168.465KM
TO CH 171.627KM (Old CH
96.643KM TO CH 9.535 KM)**

Name of Project Engineer: SILPA R

Name of contractor : Ramalingam Construction
Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 15-06-2022 as per EoT
Expected Date of completion : 15-06-2022

Status of Work in terms of components:

- 20m groynes - 3 started out of 3
- 30m Groynes-5nos started out of 7
- 40m groynes - 19 nos started out of 24
- Total boulders quantity - 162612.848MT boulders reached out of 174010 MT (93.45%)
- 2T TETRAPODS – 21553 nos (99.95%) casted out of 21562 nos.
- 5T TETRAPODS – 3144(100%) nos. casted out of 3144 nos.
- Geomat - 14015.5m2
- Earthwork Excavation - 31767.090m3 out of 42122 M3

Works done in the last week

- 2T tetrapod casted - 0nos.
- 5T tetrapod casted - 0nos.
- Supplying and Laying of Boulders-7710.39 MT
- laying of boulders for,G22,G21,G25,G15,G12,G27,g19are in progress.
- Laying of tetrapods at G26,G25 are progressing

Scheduled progress as on 28-05-2022 –92 % (as per EoT given)

Achieved progress as on 28-05-2022- 93.00%

Last week progress - 1.5%

Current week progress -2%

Current Bill Status : 7th bill submitted for an Amount of Rs.2,82,93,879.56/- .Total bill amount - Rs. 41,21,82,538.03

Current Financial Progress : 84%

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of Project Engineer: MEENU ES

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion :23/08/2021
Expected Date of completion : 31/07/2022

Status of Work in terms of components:

- Main building civil works –51%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works –3%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

. Main building AAC block work
. Electrical works
. Plastering works
Tile work completed
Primer work
Fin wall work in Progressing..

Scheduled progress as on 28/05/2022 - 100%

Achieved progress as on 28/05/2022 - 59%

Last week progress : 44%

Current week progress :5%

Current Bill Status :1st bill submitted to KASE, 2nd bill submitted to KASE,3rd bill submitted to KIIDC

Current Financial Progress in %: 56%

Images of works done at Site during last week (with time stamp)



**Thenmala
(Tourism Project)**

IMPROVEMENT AND DEVELOPING ECO-TOURISM AT THENMALA DAM IN KOLLAM DISTRICT

Name of Project Engineer:Meenu ES

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹4.5 Cr
Agreed Amount With GST : Rs. 4,49,90,000.00
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 31/05/2022

Scheduled progress as on 28/05/2022- 100%

Achieved progress as on 28/ 05/2022-59%

Last week progress -3%

Current week progress -5%

Current Bill Status : Nil

Current Financial Progress in %: Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- SHOP (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)
pavilion(50%)

Works done in the last week

1. Toilet, security room and cloak room-plinth beam work completed.column shuttering work under progress.brick work in progress
2. Shed to shop -roof slab concrete completed
3. Pavilion-step Work progress
4. Seating area clearance completed.



**ITI
DHANUVACHAPU
RAM
(KASE)**

**UPGRADATION OF GOVT. ITI
DHANUVACHAPURAM ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of Project Engineer: ATHEESH P MOHAN

Name of contractor : Heather Construction
Agreement date : 25-11-2019
Agreed Amount : ₹11.18 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration : 20 months
Scheduled Date of Completion : 30-05-2022
Expected Date of completion : 30-05-2022

Scheduled progress as on 28-05-2022- 88 % (Scope of the work were increased as per the instructions from SPV)

Achieved progress as on 28-05-2022 - 88%

Last week progress - 85%

Current week progress -3%

Current Bill Status :15th bill submitted amount:2,02,42,253.35/-

Current Financial Progress :79.42%

Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering completed
- GF primer work 98% Completed
- GF Electrical (Concealed) work completed
- GF plumbing work 90% completed
- FF Block Work 98% completed
- FF Ceiling work 100% completed
- FF plastering 95% completed
- Dummy column RCC completed
- FF Elec- concealed work completed
- Parapet plastering completed
- GF Tile work 98%
- FF primer work 85% completed

Works done in the last week

- Paving tiles works
- Retaining wall rubble works, Rcc belt concrete
- Porch roof top plastering
- Front gate works,
- Ponting works, putty and painting works,
- ceiling works
- Fixing of Jalram furniture
- Fixing of over head tank
- Fixing of writing board, prometean board etc



LIST OF TOURISM DEPARTMENT COMPLETED PROJECTS

(PHYSICAL PROGRESS 100%)

SL No.	Name of Project	Financial Progress	Remarks
1	Karappuzha Phase III - Construction of Viewing Tower, Bamboo Pavilion and Bridge (Wayanad)	100.00%	-
2	Karappuzha Phase III - Construction of Pathway, Fishing Dock, Pond, Gazebo, Parking yard and Landscaping (Wayanad)	100.00%	-
3	Development of Peruvannamuzhi Dam Tourism Project in Kozhikode District	65.22%	4 th and final bill amounting to ₹1,07,88,549.00 submitted to Department of Tourism for release of payment on 20.04.2022.
4	Additional Work I of Eco Lodge Construction at Idukki	100.00%	-
5	Additional Work II of Eco Lodge, Idukki	0.00%	First and part bill amounting to ₹36,81,648.00 submitted to Department of Tourism on 14.03.2022. (Contract PAC: ₹45,85,722.41). Revised Estimate preparation under progress.
6	Providing Temporary Rest Room cum Store (Container Type) for Life Guards at Alappuzha Beach	0.00%	First and final bill amounting to ₹11,96,272.00 submitted to Department of Tourism on 23.03.2022.
