


KIIDC WEEKLY PROGRESS REPORT



KIIDC

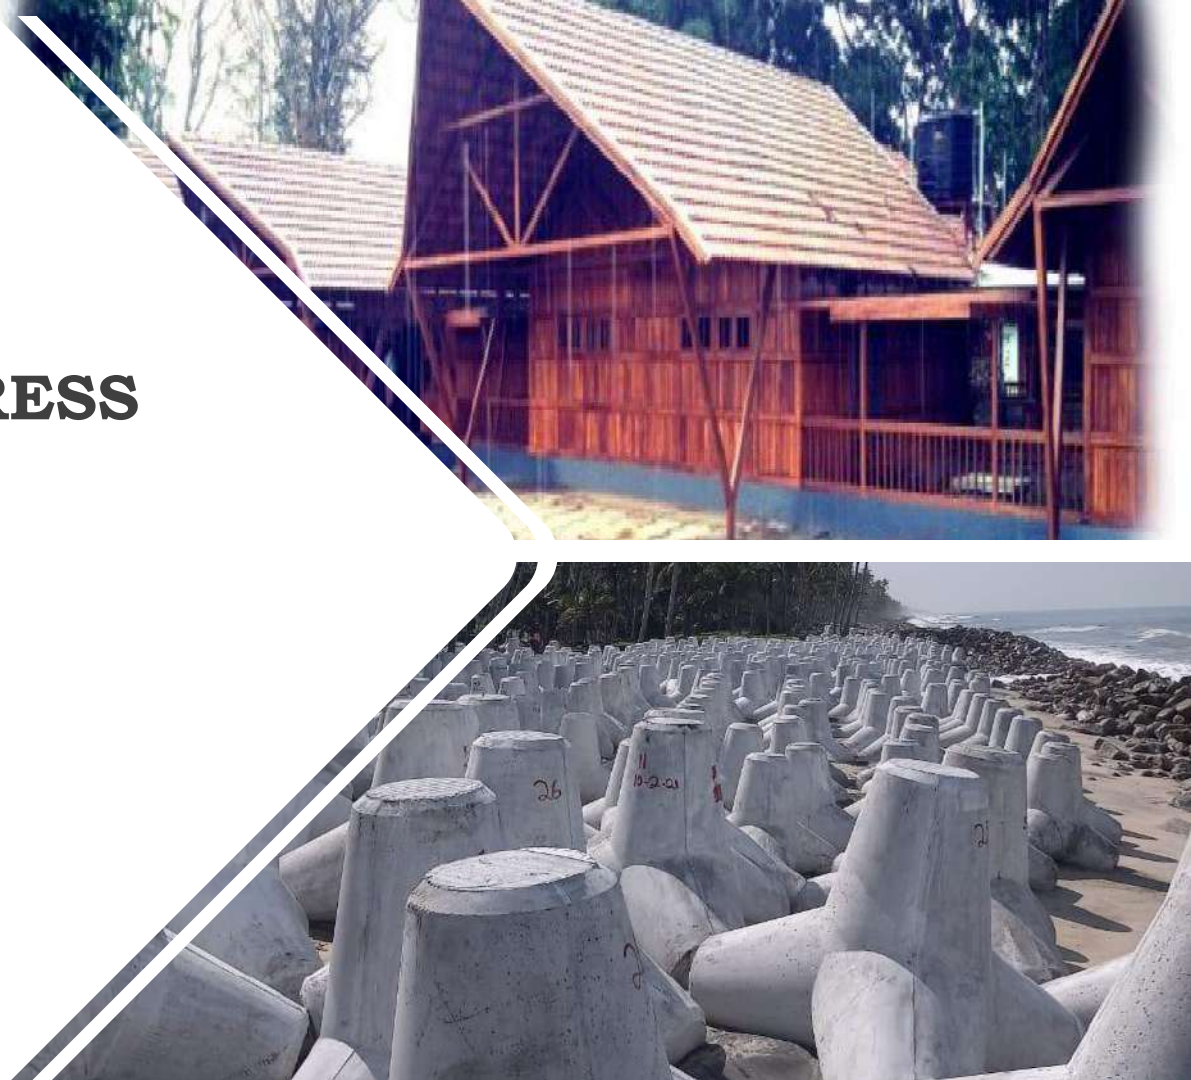

PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

UPGRADATION OF GOVT. ITI KANNUR ON PAR WITH INTERNATIONAL STANDARDS

**Name of Project Engineer : Joel J Varghese
Name of Project Coordinator : Visakh A.K**

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount :Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion : 17-05-2022

Scheduled progress as on 06-08-2022 53%

Achieved progress as on 06-08-2022 32%

Last week progress in 1%

Current week progress - 1%

Current Bill Status : 2nd Bill submitted

Current Financial Progress :31%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

Footing works 100 % completed
Stub columns, Grade beam
concreting 100% completed

Ground floor columns concreting
100% completed

Block Work 95%

Internal Plastering 90%

External Plastering 80%

Work done in last week

Excavation for gate work
Front gate security cabin
footing
mS pipe section setting



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF
REGULATOR WITH LOCK ACROSS
ANCHARAKANDY RIVER AT
PARAPRAM IN PINARAYI
PANCHAYATH, KANNUR DISTRICT**

Name of Project Engineer : Athul Ashar

Name of Project Coordinator : Visakh A K

Name of contractor : PGCC
Agreement date :06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion : 15-05-2022 (extended to 21-11-2022)
Expected Date of completion : 30-06-2023

Status of Work in terms of components:

- Regulator - 70%
- Foot Bridge -57%
- Lock Portion -95%
- Side Protection -75%
- Mechanical Works -10%
- Generator Cum Watchman Room -60%
- Electrical Works -

Works done in the last week

- Switchroom main slab concrete done
- P2 to P3 footbridge concrete completed
- Piling work for right side U/S retail wall
- Bund dismantled due to heavy rain

Scheduled progress as on 06-08-2022 100%

Achieved progress as on 06-08-2022 - 71%

progress upto last week = 69.5%

Current week progress - 1.5%

Current Bill Status :Eight Part Bill submitted

Current Financial Progress : 62%

Images of works done at Site during last week (with time stamp)



**REGULATOR
UMMENCHIRA RIVER
AT
CHEKKUPALAM(KIIFB)**

**KIIFB - CONSTRUCTION OF REGULATOR
CUM BRIDGE ACROSS UMMENCHIRA
RIVER AT CHEKKUPALAM IN PINARAYI
PANCHAYATH,KANNUR DISTRICT**

Name of Project Engineer : Joel J Varghese

Name of Project Coordinator : Visakh A K

Name of contractor : PGCC
Agreement date :04-05-2022
Agreed Amount : ₹34.47Cr
Agreed Amount With GST : Rs.
Site Handover date : 13-05-2022
Project duration : 18 months
Scheduled Date of Completion : 13-11-2023
Expected Date of completion : 13-11-2023

Scheduled progress as on 06-08-2022 - 0%

Achieved progress as on 06-08-2022 - 0%

Progress upto last week-0 %

Current week progress - 0%

Current Bill Status :

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Regulator -
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

Alignment drawing has been prepared
Letter sent Permission seeking from Social forestry
Letter sent Permission for shifting equipment to DTPC
Letter sent to KWA regarding the NoC



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY (KIIFB)**

**CONSTRUCTION OF REGULATOR
CUM BRIDGE ACROSS KUPPAM
RIVER IN KOOVERY-KATTAMPALLY
IN CHAPPARAPADAVU PANCHAYAT ,
THALIPARAMBA TALUK, KANNUR
DISTRICT**

Name of Project Engineer: Athul Ashar

Name of contractor : Infab Infrastructures Ltd
Agreement date : 15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Status of Work

- The contractor has filed a Writ Petition No 1217/2021 in the Hon'ble High Court of Kerala to stay all coercive steps like termination pursuant to the demand for extension of Bank Guarantee as seen in Ext.P17,till the disposal of this Writ petition.Court directed the 6th respondant(vigilance) to submit report on the matter.Vigilance made an enquiry regarding the matter and they will submit the report to the honourable court.Final decision will be taken according to the verdict from the court.

Scheduled progress as on 06-08-2022 100%

Achieved progress as on 06-08-2022 - 0%

Progress up to last week-0 %

Current week progress - 0%

Current Bill Status :NA

Current Financial Progress :0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2

Phase 1- 14 projects- As received - 40.95 crores		
Phase 2- 14 projects-AS received - 37.212 crores (Total AS received for 28 Projects – 78.162)		
	Phase 1	Phase 2
• MoU signed – 18 projects	Pindali kalari, Andalurkav Temple, Illikunnu church, Kottiyoor siva temple, Makreri temple, Lokanarkav temple, Thrissillery temple, Thirunelli temple, Thiruvangad Ramaswamy temple, Jagannath temple	Kadirur suryanarayana temple, Chirakkakavu temple, Mridangasaileswary temple, Oorpazhichikaav temple, Puralimala temple, Peralassery temple, Valliyoorkav temple, Thacholi manikoth
• Agreement executed - 10 projects	Pindali kalari, Andalurkav Temple, Kottiyoor siva temple- Streetscape, Kottiyoor siva temple-Tourist amenities, Lokanarkav temple, Makreri Subramanyaswmi temple, Illikunnu church, Jagannath temple	Puralimala temple, Pazhassiraja smrithimandapam
• Works started – 9 (GFC drawing prepared by KIIFB)	Andalurkav temple, Illikunnu church, Pindali kalari, Kottiyoor temple- Streetscape, Kottiyoor siva temple- Tourist amenities, Jagannath temple, Lokanarkav temple, Makreri Subramanyaswami temple	Puralimala temple
• Selection notice issued - 8 projects	Thiruvangad Ramaswamy temple, Thirunelli Temple, Thrissillery Temple	Sree Thacholi Manikoth Temple, Vadakara Tazhe angadi, Peralassery Temple, Chirakkakav temple, Thalakkal Chandu Museum - Panamaram

**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2

	Phase 1	Phase 2
<ul style="list-style-type: none"> • Tender to be finalized - 2 Projects 	<p>Municipal Stadium (THP Office), Kakkulangara Mosque (Letter submitted to Tourism for tender excess approval)</p>	
<ul style="list-style-type: none"> • To be retendered - 2 projects (After revising the TS in DSR 2018) 	<p>Odathil Mosque and Paris Hotel Street</p>	<p>Kadirur Surya Narayana Temple</p>
<ul style="list-style-type: none"> • TS to be issued - 4 projects 		<p>Sree Mridanga Saileswari Temple, Thodeekalam Siva Temple, Sree Oorpazhachi Kavu Temple, Valliyoorkavu temple</p>
<ul style="list-style-type: none"> • To be dropped - 2 projects (NOC not received) 		<p>Pazhassi Kovilakam (Mattannur), Arakkal Kettu (Total amount – 10.5Cr)</p>

**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT - PHASE 1
-Pazhassi Circuit - Pindali Kalari
House(Pathway,Conservation of
Kalarithara,Pond restoration ,Seating,
Landscaping ,Electrification)at
Iritty,Kannur**

Name of Project Engineer:Joel J Varghese

Name of Project Coordinator : Visakh A.K

Name of contractor : M/s Classic Builders
Agreement date : 17-02-2021
Agreed Amount : ₹ 0.6238 Cr
Agreed Amount With GST : Rs. 6987127.71
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-02-2022
Expected Date of completion :

Scheduled progress as on 06-08-2022 : 51%

Achieved progress as on 06-08-2022 - 37%

Progress upto last week - 1%

Current week progress -1%

Current Bill Status : Ready for Part 1 bill

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

Gallery Work 100 % completed
Kalarithara 50%
Kalasamandaapam 25%
Pond 25%

Works done last Week

Heavy rainfall no work done

Unavailability of brick



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 - Cultural Circuit -Andalur Kavvu

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Visakh A.K

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.5189 Cr
Agreed Amount With GST : Rs.
Site Handover date : 1.701 Cr
Project duration : 12 months
Scheduled Date of Completion : 26-02-2022
Expected Date of completion :

Status of Work in terms of components:

- Pathway
- Chuttambalam
- Roofing
- Lighting
- Street Development
- Electrification

Work done in last week

- work stopped due to heavy rain



Scheduled progress as on 06-08-2022 : 100%

Achieved progress as 06-08-2022 - 17 %

Progress upto last week - 0%

Current week progress -0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -illikunnu

**Name of Project Engineer: Athul Ashar
Name of Project Coordinator : Visakh A.K**

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26/02/2021
Agreed Amount : ₹ 8300000
Agreed Amount With GST : Rs
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 26/02/2022
Expected Date of completion :

Status of Work in terms of components of cemetery :

- Land scaping of cemetery area
- Lighting
- Conservation of ceiling, wood work, joinery

Work done in last week

- Polishing work

Scheduled progress as on 06-08-2022 : 100%

Achieved progress as on 06-08-2022 - 35%

Progress upto last week - 34%

Current week progress -1%

Current Bill Status : 1st bill submitted

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -Jaganath Temple

**Name of Project Engineer: Athul Ashar
Name of Project Coordinator : Visakh A.K**

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26/02/2021
Agreed Amount : ₹ 1,48,17,938.56
Agreed Amount With GST : 1.56cr

Site Handover date : 08/03/2021
Project duration : 12 months
Scheduled Date of Completion : 08/03/2022
Expected Date of completion :

Status of Work in terms of components :

- Pathway
- Rival of pond
- Compound wall
- Landscaping

Work done in last week

- Work stopped due to heavy rain

Scheduled progress as on 06-08-2022 : 100%

Achieved progress as 06-08-2022 - 27%

Progress upto last week- 0%

Current week progress -1%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT-Makreri
Subramanyaswami Temple (Cultural
Circuit)**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Visakh A.K

Name of contractor : M/S Saaj Constructions
Agreement date : 17/06/2021
Agreed Amount : ₹ 1,83,50,573.45/-
Agreed Amount With GST : 2,05,52,642.26/-
Site Handover date : 27.06.2021
Project duration : 12months
Scheduled Date of Completion : 27/06/2022
Expected Date of completion :

Status of Work in terms of components :

- Ootupura
- Toilet block
- Landscaping
- Water supply and Sanitary Arrangements
- street scape of Paving of Chuttambalam
- Stone paving
- Conservation of pond
- Electrification

Work done in last week

- Ootupura laterite masonry started
- Plinth belt concrete for toilet completed
- Reinforcement for toilet plinth progressing.

Scheduled progress as on 06-08-2022 : 100 %

Achieved progress as 06-08-2022 - 12%

Last week progress - 11%

Current week progress -1%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY HERITAGE
PROJECT-PHASE 1-pazhassi circuit –kottiyoor shiva
temple(streetscape,landscaping,agrashala,carpark
ing,stage and electrical work at kottiyoor shiva
temple in irrity,Kannur district)**

Name of Project Engineer :Basil George

Name of Project Coordinator : Visakh A.K

Name of contractor : M/s Rubicon construction
Agreement date : 05/10/2021
Agreed Amount : ₹ 1.21 cr
Agreed Amount With GST : RS 1,36,06,740.60
Site Handover date : 14/10/2021
Project duration : 12 months
Scheduled Date of Completion : 13-10-2022
Expected Date of completion : 13/10/2022

Status of Work in terms of components:

- Streetscape
- Landscaping
- Agrashala
- Car parking
- Stage
- electrification

Work done in last week

Work has delayed due to heavy rain.

Scheduled progress as on 06/08/2022 : 80%

Achieved progress as 06-08-2022 - 50%

Last week progress - 0%

Current week progress -0%

Current Bill Status : 1st bill submitted

Current Financial Progress : 17%

Images of works done at Site during last week (with time stamp)



COMPREHENSIVE DEVELOPMENT OF MUZHAPPILANGAD AND DHARMADOM BEACH IN KANNUR DISTRICT

IN PRINCIPLE SANCTION : 233.71 Cr

FUNDING AGENCY : KIIFB

The whole project is divided into 4 Character areas

AS Amount for Character Area 1 : 79.51 Cr

CA 1 - AS DATE : 17/03/2022

CA 1- TS DATE : 22/03/2022

CHARACTER AREA 1

- ❖ CRZ clearance obtained
- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai and revised architectural drawing prepared by consultant architect received on 01.12.2021
- ❖ KIIFB approved Character area 1 for an amount 79.51 Cr on 17.03.2022
- ❖ Work tendered and tender opened on 23.04.2022
- ❖ Selection notice issued to ULCCS. Agreement to be executed

CHARACTER AREA 2

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

CHARACTER AREA 3

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

CHARACTER AREA 4

- ❖ DPR and detailed project components are under preparation with Consultant architect CBRE

PROJECTS IN WAYANAD DISTRICT

**Community micro
irrigation at
Athichal
Mundankolly
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Athichal
Mundankolly in Ambalavayal
Panchayath Wayanad district -
CMI Part**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Visakh Ak

Name of contractor : M/S Mahindra EPC Irrigation limited
Agreement date : 13-04-2022
Agreed Amount : 2.14 Crores
Agreed Amount With GST :
Site Handover date : 22-04-2022
Project duration : 6 months
Scheduled Date of Completion :21-10-2022
Expected Date of completion :21-10-2022

Status of Work in terms of components:

- Main line
- Submain line
- Automation

Works done in the last week

- Survey completed
- Alignment marking is restarted

Scheduled progress as on 06/08/2022 - 40 %

Achieved progress as on 06/08/2022 - 10 %

Last week progress in : 8%

Current week progress : 2%

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

**Community micro
irrigation at
Athichal
Mundankolly
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Athichal
Mundankolly in Ambalavayal
Panchayath Wayanad district -
Civil**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Visakh Ak

Name of contractor : Shri Saji mathew
Agreement date : 04-04-2022
Agreed Amount : 25.05 Lakhs
Agreed Amount With GST :
Site Handover date : 13-04-2022
Project duration : 4 months
Scheduled Date of Completion :12-08-2022
Expected Date of completion :12-08-2022

Status of Work in terms of components:

- Irrigation room
- Sump tank
- Electrical Works

Works done in the last week

Work not yet started

Scheduled progress as on 06/08/2022 - 50 %

Achieved progress as on 06/08/2022 - 0 %

Last week progress in : 0%

Current week progress : 0%

Current Bill Status :

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB Project - KIIFB Project- Thalassery Heritage Project - Phase 2 - Pazhassi Circuit -Valliyoorkavu temple - Streetscape (Stone steps to temple, Lamp Post, Electrification) at Mananthavady in Wayanad District – Conducting test on given samples of cement, Aggregate, Laterite and Sadarhalli granite stone

Name of Project Engineer :Athul ashar

Name of Project Coordinator : Visakh A.K

Name of contractor : Shri. Ameer Ali N
Agreement date : 30 -04-2022
Agreed Amount : 3673949.76
Agreed Amount With GST :
Site Handover date : 12/05/2021
Project duration : 6 months
Scheduled Date of Completion : 11-11-2022
Expected Date of completion :11-11-2022

Status of Work in terms of components:

- Stone steps to temple
- Lamp post
- electrification

Work done in last week

Work has delayed due to heavy rain.

Scheduled progress as on 06/08/2022 : 60%

Achieved progress as 06-08-2022 - 50%

Last week progress - 50%

Current week progress -0%

Current Bill Status : nil

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS
POONUR
PUZHA-POOLAKAD
AVU (KIIFB)**

**KIIFB PROJECT CONSTRUCTION
OF RCB ACROSS POONUR PUZHA
NEAR KWA PUMPING HOUSE AT
POOLAKADAVU IN KURUVATTOOR
PANCHAYATH**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Bibin Giri

Name of contractor : ULCCS Ltd.
Agreement date : 18-08-2021
Agreed Amount : ₹22,68,45,702.29
Agreed Amount With GST : Rs.
Site Handover date : 27-08-2021
Project duration : 18 months
Scheduled Date of Completion : 26-02-2023
Expected Date of completion : 26-02-2023

Status of Work in terms of components:

- Regulator -17%
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

- Bar bending for Pile cap and Pile
- Major works are suspended due to high flood

Scheduled progress as on 06-08-2022 - 29%

Achieved progress as on 06-08-2022- 17%

Progress upto last week- 16 %

Current week progress - 1 %

Current Bill Status : CC First and part under preparation

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)



**ITI KOYILANDY
(KASE)**

**UPGRADATION OF GOVT. ITI
KOYILANDY ON PAR WITH
INTERNATIONAL STANDARDS**

Name of Project Engineer : Basil George

**Name of Project Coordinator : Sethumadhavan K.P
(Additional charge)**

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion :13-08-2021
Expected Date of completion :13-11-2021

Status of Work in terms of components:

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

Works done in the last week

- Work delayed due to not getting approval for RE from KASE

Scheduled progress as on 06-08-2022- 100%

Achieved progress as on 06-08-2022 - 85%

Last week progress- 0%

Current week progress - 0%

Current Bill Status : CC 3rd and part submitted

Current Financial Progress : 34.3%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY HERITAGE
PROJECT-PHASE 1-pazhassi circuit –
Lokanarkavu Temple (Conservation of
Thantrimadom, Folklore, Oottupura,Chiras,
Plumbing and Electrification at
Lokanarkavu Temple in Vadakara,
Kozhikode District)**

Name of Project Engineer: Basil George

Name of Project Coordinator : Visakh Ak

Name of contractor : Saaj Constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3,78,74,574.27/-
Agreed Amount With GST : Rs.
Site Handover date : 26-06-2021
Project duration : 12 months
Scheduled Date of Completion :25/06/2022
Expected Date of completion :31/03/2023

Status of Work in terms of components:

- thanthrimadam up to plinth belt were completed.
- big chira side protection work in progress.
- compound wall work

Workshops done in the last week

Compound wall-
pointing
Pavement works-gsb
laying



Scheduled progress as on 06-08-2022- 90%

Achieved progress as on 06-08-2022 - 8%

Last week progress- 0%

Current week progress - 0%

Current Bill Status :

Current Financial Progress :

Images of works done at Site during last week (with time stamp)



**RCB
PERINCHERIKADAVU
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM
BRIDGE AT U/S OF
PERINCHERIKADAVU IN KUTTIADY
RIVER (GULIKAPUZHA) AT KOZHIKODE
DISTRICT**

Name of Project Engineer : Basil George

**Name of Project Coordinator : Sethumadhavan K.P
(Additional charge)**

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 61,13,34,133.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022 (Extended to 15-04-2023)
Expected Date of completion :01-03-2024

Scheduled progress as on 06-08-2022 - 85%

Achieved progress as on 06-08-2022 - 24%

Progress upto last week--24%

Current week progress 0%

Current Bill Status : 2 nd bill submitted

Current Financial Progress : 17%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Regulator -14%
- Lock Portion -
- Side Protection -35%
- Deck Slab -
- Approach Road -
- Mechanical Works-
- Generator Cum Watchman Room-
- Electrical Works -

Works done in last week

Work delayed due to heavy rain.
RE submitted to KIIFB for Scrutiny



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

KIIFB Project - Construction of Regulator at Puzhankavu across Kadalundi River

Name of Project Engineer : RAHEES.P

Name of Project Coordinator : Pushparaj

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 10,97,21,287.89
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion : 16/06/2021-(Extended to 21-11-2022)
Expected Date of completion : 21-11-2022

Scheduled progress as on 07-08-2022-95%

Achieved progress as on 07-08-2022 -95.5%

Progress upto last week -95%

Current week progress - 0.50%

Current Bill Status : Total Bill submitted ₹7.10 Crores (9th part bill)

Current Financial Progress in :72.53%

Images of works done at Site during last week

Status of Work in terms of components:

- Regulator -100%
- Side Protection -95%
- Mechanical Works -90%
- Generator Cum Watchman Room -50%
- Electrical Works -

Works done in the last week.

- Continuing Heavy raining at site.
- RE submitted..
- Guard room shutter beam concreted and truss work started.



**RCB
Moothikkayam
(KIIFB)**

KIIFB - Construction of Regulator cum Bridge across thoothapuzha keezhmurikadavu moothikkayam in moorkanad panchayath

Name of Project Engineer: Sethu Madhavan

Name of Project Coordinator : Lakhan Murari

Name of contractor : M/s PGCC Pvt,Ltd
Agreement date : 18/09/2020
Agreed Amount : ₹57.56 Cr
Agreed Amount With GST : Rs. 64.46 crore
Site Handover date : 26-09-2020
Project duration : 18 months
Scheduled Date of Completion :26-03-2022 (Extended to 09-01-2023)
Expected Date of completion :31-05-2023

Scheduled progress as on 08-08-2022 - 100%

Achieved progress as on 08-08-2022 - 37%

Progress upto last week -36%

Current week progress -0.01%

Current Bill Status : Fifth bill submitted

Current Financial Progress : 24.84%

Images of works done at Site during last week (with time stamp)

STATUS OF WORK IN TERMS OF

COMPONENTS

- Regulator - foundation work (pile & open footing) completed. Girder 28/48 completed.
- Side Protection -
1)D/S-R/S-completed..
2)U/S-R/S- 486 m/600 m raft completed. 456m partially completed
- Deck Slab -7/12 completed
- Mechanical Works - Primary and secondary fabrication completed. Generator Cum Watchman Room - not started

Work done in the last week

- Deck slab between pier 6 and Pier 5 concreted.
- Civil works hindered due to river flowing full.



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA
(KASE)**

UPGRADATION OF GOVT. ITI MALAMPUZHA ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer:NITHISH. C

Name of Project Coordinator : Lakhan Murari

Name of contractor : M/S. PERFECTENGINEERS
Agreement date : 05/03/2020
Agreed Amount : Rs.11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date :06/03/2020
Project duration : 18 months
Scheduled Date of Completion. : 05/09/2021
Expected Date of completion. : 02/06/22

Scheduled progress as on 06/08/2022- 100%

Achieved progress as on 06/08/2022 - 77%

Last week progress - 75%

Current week progress - 76%

Current Bill Status : no of bill submitted - 6,amount:4,21,29,262

Current Financial Progress : 36.26%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components

- Smart classroom promethean and writing board fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

Works done in the last week

- Tile fixing at smart classroom at FF
- Electrical work
- External wall plastering
- AAC block work at FF
- Cable pulling
- Internal plastering at FF
- Tile fixing in toilet wall at FF



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of Project Engineer:NITHIN J B

Name of Project Coordinator : Lakhan Murari

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-07-2022

Status of Work in terms of components:

- Regulator - Primary concrete for all structure portion completed and secondary concreting in progress.
- Side Protection - U/S RHS and D/S LHS fully completed.
- U/S LHS raft concrete completed upto 102m and wall completed upto 70m.
- Mechanical Works -Fabrication of 11 shutters and painting of all completed.
- 9 Hoisting bridge spans completed

Works done in the last week

- Left Abutment one lift concrete.
- Fabrication of hoisting bridge mechanism.
- Secondary concrete on piers.
- Preparation of platform for erection of shutters.
- Heavy rain disrupted civil works as water level raised as Aliyar dam was opened.

Scheduled progress as on 08/08/2022 - 92%

Achieved progress as on 08/08/2022 - 79%

progress up to last week - 78%

Current week progress -1%

Current Bill Status : Sixth and part bill credited

Current Financial Progress : 50.92%

Images of works done at Site during last week



**Moongilmada LIS
(Civil)
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of Project Coordinator : Lakhan Murari

Name of contractor : M/s Vallamattam constructions
Agreement date : 18-09-2020
Agreed Amount : ₹15422222 Crores
Agreed Amount With GST : Rs. 18198221.96/-
Site Handover date : 03-06-2021
Project duration : 6 months
Scheduled Date of Completion :03-12-2021
Expected Date of completion :31-05-2022

Status of Work in terms of components:

- Pump House
- Conversion of abandoned RBC to water storage.
- Electrical Works

Works done in the last week

Electrical works ongoing

Scheduled progress as on 07/07/2022 - 100%

Achieved progress as on 07/07/2022 - 87%

Last week progress in : 87%

Current week progress : 0%

Current Bill Status : Part Bill-2

Current Financial Progress : 53%

Images of works done at Site during last week (with time stamp)



**Valiyeri LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Valiyeri LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd
Agreement date : 24-06-2021
Agreed Amount : ₹31004000 Rupees
Agreed Amount With GST : Rs. 36581180/-
Site Handover date : 25-06-2021
Project duration : 12 months
Scheduled Date of Completion :25-06-2022
Expected Date of completion :31-05-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

Work stopped due to heavy rain

Scheduled progress as on 07/07/2022 - 100%

Achieved progress as on 07/07/2022 - 95 %

Last week progress in : 95%

Current week progress : 0%

Current Bill Status : Part Bill-2

Current Financial Progress : 64%

Images of works done at Site during last week (with time stamp)



**Navithankulam LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at
Navithankulam LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd
Agreement date : 24-06-2021
Agreed Amount : ₹16327047.54 Rupees
Agreed Amount With GST : Rs. 19265916.09/-
Site Handover date : 25-06-2021
Project duration : 12 months
Scheduled Date of Completion :25-06-2022
Expected Date of completion :31-06-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

Work stopped due to heavy rain

Scheduled progress as on 07/07/2022 - 100%

Achieved progress as on 07/07/2022 - 75 %

Last week progress in : 75%

Current week progress : 0%

Current Bill Status : Nil

Current Financial Progress : first bill

Images of works done at Site during last week (with time stamp)



**Kunnamkatupathy
LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at
Kunnamkatupathy LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Mahendra Pvt Ltd
Agreement date : 18-11-2021
Agreed Amount : ₹36068276 Rupees
Agreed Amount With GST : Rs. 42560565.68/-
Site Handover date : 27-11-2021
Project duration : 6 months
Scheduled Date of Completion :29-05-2022
Expected Date of completion :31-06-2022

Scheduled progress as on 07/07/2022 - 100%

Achieved progress as on 07/07/2022 - 65 %

Last week progress in : 63%

Current week progress : 2%

Current Bill Status : Partbill-2

Current Financial Progress : 34%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

submain and mainline work

Work stopped due to heavy rain



**MOOLATHARA
RIGHT BANK CANAL
PHASE 1 FROM
KORAYAR TO
VARATTAYAR
(KIIFB)**

**KIIFB-Extension of Moolathara
right bank canal phase 1 from
korayar to varattayar**

Name of Project Engineer: NITHISH.C

Name of contractor : M/s Prathmesh & K.K.Constructions
Agreement date : 23-12-2021
Estimate P.A.C : Rs.158,50,00,000/-
CONTRACT P.A.C : Rs. 174,34,95000/-
Site Handover date : 31-12-2021
Project duration : 30 months
Scheduled Date of Completion :
Expected Date of completion :

Status of Work in terms of components:

- Site clearance

Works done in the last week

- .Tree cutting
- .Tree numbering
- .Design works

Scheduled progress as on 06/08/2022 - Nil

Achieved progress as on 06/08/2022 - Nil

Last week progress in : Nil

Current week progress : Nil

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN THRISSUR DISTRICT

**REGULATOR CUM
BRIDGE ACROSS
KURUMALI PUZHA
IN THRISSUR
DISTRICT.**

**CONSTRUCTION OF
KANATHODU REGULATOR CUM
BRIDGE ACROSS KURUMALI
PUZHA AT KUNDUKADAVU IN
PUDUKAD PANCHAYATH,
THRISSUR DISTRICT.**

Name of Project Engineer: RAHUL V R

Name of Project Coordinator : Pushparaj

Name of contractor : PGCC
Agreement date :05-01-2022
Agreed Amount : 262383481.27
Agreed Amount With GST : Rs.293869499.022
Site Handover date : 13-01-2022
Project duration : 18 months
Scheduled Date of Completion : 13-07-2023
Expected Date of completion : 13-07-2023

Status of Work in terms of components:

- Regulator -3.75%
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

- Revised GFC drawings was issued on 02-04-2022
- River boundary survey was completed on 18-02-2022
- Initial levels also been taken
- **Work delayed since 27/06/2022 due to heavy rain and rise in water level in the River**
- **Ring bund dismantled due to Rise in water level**

Scheduled progress as on 06-08-2022 - 18.5%

Achiever progress as on 06-08-2022 - 3.75%

Progress up to last week- 3.75%

Current week progress -0%

Current Bill Status : NIL

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**ITI CHALAKUDY
KIIFB-KASE**

UP GRADATION OF GOVT ITI CHALAKUDY ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: RAHUL V R

Name of contractor : Sidheek, M/S Sitco Associates
Agreement date : 28-10-2020
Agreed Amount : ₹ 7,47,51,405.13
Agreed Amount With GST : ₹ 8,37,21,573.74
Site Handover date : 06-11-2020
Project duration : 12 months
Scheduled Date of Completion : 05-11-2021
Expected Date of Completion :

Scheduled progress as on 06/08/2022- 0 %

Achieved progress as on 06/08/2022 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the last week

- As per drawings building setbacks are not available at the site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign



PROJECTS IN ERNAKULAM DISTRICT

**CHELLANAM
COASTAL
PROTECTION
[KIIFB]**

**KIIFB PROJECT- REFORMATION OF DAMAGED
SUNKEN SEA WALL AT CHELLANAM USING
TETRAPODS AND RUBBLE IN BETWEEN CP
STONE 976 AND 1052 FOR 10 KM STRETCHES
ALONG CHELLANAM COAST IN ERNAKULAM
DISTRICT - PHASE I FOR A LENGTH OF 7/350
KM IN BETWEEN CP 986 AND CP 1026**

**Name of Project Engineer : SREELAKSHMI S
Name of Project Coordinator : Mahadevan**

Name of contractor : M/s Uralungal Labour Contract Co-operative

Agreement date : 30-12-2021

Agreed Amount : ₹ 256,89,67,441.29

Agreed Amount With GST : ₹ 287,72,43,534.25

Site Handover date : 03-01-2022

Project duration : 16 months

Scheduled Date of Completion : 02-05-2023

Expected Date of Completion : 02-05-2023

Scheduled progress as on 07/08/2022- 44.63%

Achieved progress as on 07/08/2022 - 42.30%

Last week progress - 1.23%

Current week progress- 1.27%

Current Bill Status : C.C 2nd and Part Bill submitted Amount: 37.46Cr & C.C 1st and Part Bill passed Amount: 65.95Cr. Total Bill Amount = 103.42Cr

Current Financial Progress : 34.12%

Status of Work :

- 28655nos of 2T tetrapods cast.
- 23938nos of 3.5T tetrapods cast.
- Available mould 2T = 149 nos
- Available mould 3.5T = 163 nos

Total Boulders Supplied till 05.08.2022

- Core layer (10-50kg) = 88322.919 T
- Toe (200 to 400kg) = 40576.593 T
- Underlayer (150-200kg) = 53278.687 T
- Toe (250-350kg) = 96429.527 T
- Toe (350-700kg) = 48810.456 T
- Primary layer(500-800kg)=25423.48 T

Works done in the last week

- 11515nos 2T and 9060nos 3.5T tetrapods are placed.
- Supplying and laying of boulders in progress at SR-1,2,3,4,6 Harbour, SR-9,10,11,12,13, 14 Abad Area.

Images of works done at Site during last week



**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

**Name of Project Engineer: Remya P R
Name of Project Coordinator : Bibin Giri**

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion : 15-04-2023

Scheduled progress as on 08-08-2022 - 45%

Achieved progress as on 08-08-2022- 25.5%

Progress upto last week- 25.5%

Current week progress - 0%

Current Bill Status :cc 3rd & part bill under preparation & will be submitted soon

Current Financial Progress :20 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Regulator - 10%
- Lock Portion - 15.5%
- Side Protection -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

Piling works -
Lock portin- 56 piles,
Pier 1 , Pier 2 & Pier 3- 12nos piles completed.
Left abutment- 4 no.s completed.
Total -72 piles completed(Piling works completed).

***Ring bund demolished due to monsoon rain & flood. And river flows over the ring bund .It affects the progress of the work**



**ANTHAKARATHO
DU CANAL
(KIIFB)**

IMPROVEMENTS TO ANTHAKARATHODE IN THRIPPUNITHURA MUNICIPALITY

Name of Project Engineer: Princy Abraham

Name of Project Coordinator : Bibin Giri

Name of contractor : Southern Tech
Agreement date : 29-09-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 08-10-2018
Project duration :15 months
Scheduled Date of Completion :07-01-2021
Expected Date of completion :31-10-2022

Status of Work in terms of components:

- Cleaning & desilting-completed
- Side protection work- 85%
- Road and walkway formation- 80%
- Fencing and Handrail work- 70%
- Boat jetty -100%
- Skew bridge -100%
- Foot bridge-100%

Works done in the last week

- Presently, no work due to heavy rain

Scheduled progress as on 08-08-2022 - 98.5%

Achieved progress as on 08-08-2022 - 96%

Last week progress - 0%

Current week progress 0%

Current Bill Status : 4th bill approved

Current Financial Progress : 80%

Images of works done at Site during last week (with time stamp)



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY—PROVIDING STREET
LIGHTS ALONG THE PATHWAYS OF
ANTHAKARATHODE**

Name of Project Engineer: Princy Abraham

Name of Project Coordinator : Vishnu

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 10-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 15-11-2022

Status of Work in terms of components:

- Excavation and supply Laying of cable-90%
- Placing of lamp post, LED & feeder -80%
- Excavation and concreting-85%

Works done in the last week

- Presently, work is delayed due to heavy rain
- The remaining work depends on civil work (pathway).

Scheduled progress as on 08-08-2022- 100%

Achieved progress as on 08-08-2022- 93.1%

Last week progress - 0%

Current week progress 0%

Current Bill Status : Part Bill prepared

Current Financial Progress : 82%

Images of works done at Site during last week (with time stamp)



**BEAUTIFICATION
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIIPPUNITHURA
MUNICIPALITY–LANDSCAPING &
ARBORICULTURE, CONSTRUCTION OF
KIOSK AND TOILET AND OPERATION &
MAINTENANCE FOR ONE YEAR**

Name of Project Engineer: Princy Abraham

Name of Project Coordinator : Bibin Giri

Name of contractor : GRIDS,Digital Surveyors and
Engineering Consultants
Agreement date : 24-06-2021
Agreed Amount : ₹76.62 lakhs
Agreed Amount With GST : Rs. 8581690.00
Site Handover date : 03-07-2021
Project duration : 3 months
Scheduled Date of Completion : 02-10-2021
Expected Date of completion : 02-01-2022

Status of Work in terms of components:

- Landscaping & tress-6%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

Works done in the last week

Presently, no work due to heavy rain.

The remaining work depends on civil work (pathway).

Scheduled progress as on 08-08-2022- 40%

Achieved progress as on 08-08-2022- 6%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

UP GRADATION OF GOVT ITI KATTAPPANA ON PAR WITH INTERNATIONAL STANDARDS

**Name of Project Engineer: DON BABY
Name of Project Coordinator : Bibin Giri**

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 31-08-2022
Expected Date of completion : 15- 10-2022

Status of Work in terms of components:

- Brickwork-70%.
- plastering works-45%
- Electrical works-22.2%
- Grade beam concrete-100%
- Grade slab Concrete - 100%
- Roof beams and slab - 100%

Works done in the last week

- Brick works
- Electrical works
- Plastering works

Scheduled progress as on 07.08.2022- 100%

Achieved progress as on 07.08.2022 - 60.2%

Last week progress : 60.1%

Current week progress :0.1%

Current Bill Status : 4th and part bill

Current Financial Progress :48 %

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – III
(TOURISM)**

**ADDITIONAL WORK III OF ECO LODGE
CONSTRUCTION AT IDUKKI
(CONSTRUCTION OF MODULAR
KITCHEN,DRAINAGE,PARKING
YARD,SIDE WALL,WOOD WORK
POLISHING,ELECTRICAL WORKS &
GENERATOR ROOM).**

Name of Project Engineer:DON BABY

Name of Project Coordinator : Bibin Giri

Name of contractor : M/S VJ Raju and Co.
Agreement date : 21.10.2021
Agreed Amount : Rs.71,96,599.18
Agreed Amount With GST : Rs. 80,60,191.08
Site Handover date : 31-10-2021
Project duration : 03 months
Scheduled Date of Completion : 31-03-2022
Expected Date of completion : 14-05-2022

Status of Work in terms of components:

- Modular kitchen-100%
- Wood work polishing - 100%
- Electrical works - 100%
- Generator room-100%
- Drainage-100%
- Parking yard-100%
- Handrail- 100%

Works done in the last week

- Jungle clearance

Scheduled progress as on 10.08.2022- 100%

Achieved progress as on 10.08.2022 - 100%

Last week progress : 94%

Current week progress : 6%

Current Bill Status : 1st & Part Bill : ₹49,46,902.00 (incl.GST) submitted to Tourism Department on 14.03.2022

Current Financial Progress : 58.25%

Images of works done at Site during last week



PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVT. GUEST HOUSE PEERMADE ,
IDUKKI**

Name of Project Engineer: TEENU AUGUSTINE

Name of Project Coordinator : Sarath S R

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 31-10-2022

Scheduled progress as on 06-08-2022- 100 %

Achieved progress as on 06-08-2022 - 60.4 %

Last week progress -60.4 %

Current week progress - 0.0%

Current Bill Status : 2nd & Part Bill : ₹45,26,416.00 (incl. GST) submitted to Tourism Department on 18.06.2022

Current Financial Progress : 40.19%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Guest house renovation - 15%
- Service block renovation - 90%
- Water tank - 85%
- Parking shed - 32%
- Conference hall - 80%

Works done in the last week

- Work delayed due to heavy rain
- Plumbing works of annex building on progress
- Tile works of annex building completed



PANCHALIMEDU
(TOURISM)

**PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAM VILLAGE,
PEERMEDU TALUK, IDUKKI DISTRICT**

**Name of Project Engineer: TEENU AUGUSTINE
Name of Project Coordinator : Sarath S R**

Name of contractor : EASYINFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : 31-12-2022

Status of Work in terms of components:

- Renovation of panchalikulam - 50%
- Construction of pathway - 50%
- Proposed check dam - 25%
- Proposed lighting system - 0%
- Sitting benches - 0%
- Landscaping - 0%
- Rope cycling - 0%

Works done in the last week

- Work stopped due to heavy rain

Scheduled progress as on 06-08-2022 - 50 %

Achieved progress as on 06-08-2022 - 18 %

Last week progress - 18 %

Current week progress - 0 %

Current Bill Status : 1st & Part Bill ₹16,68,292 (incl. GST)

Current Financial Progress : 6.10%

Images of works done at Site during last week (with time stamp)



PEERMADE
(TOURISM)

**ADDITIONAL WORK AT ECOLODGE
CONSTRUCTED AT PEERMADE
(CONSTRUCTION OF PARKING YARD,
COMPOUND FENCING, SERVICE
BLOCK, AMBIENT LIGHTING AND
MODULAR KITCHEN AT ECOLODGE
PEERMADE)**

Name of Project Engineer: TEENU AUGUSTINE

Name of Project Coordinator : Sarath S R

Name of contractor : Outlook communications pvt.ltd.
Agreement date : 08-10-2021
Agreed Amount : ₹80,27,681.98
Agreed Amount With GST : Rs.9472664.74
Site Handover date : 11-10-2021
Project duration : 12 months
Scheduled Date of Completion : 10-10-2022
Expected Date of completion : 10-10-2022

Scheduled progress as on 06-08-2022 - 48 %

Achieved progress as on 06-08-2022 - 48 %

Last week progress - 48 %

Current week progress - 0 %

Current Bill Status : 1st & Part Bill : ₹27,37,936.00 (incl. GST) submitted to Tourism Department on 06.04.2022

Current Financial Progress : 28.90%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Fencing - 0%
- Service block - 85%
- Security cabin - 85%
- Diesel generator - 70%
- Modular kitchen - 90%
- Generator room - 50%
- Electrical works -0%
- Civil work for lamp post - 0%

Works done in the last week

- **No work done on last week**



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

UP GRADATION OF GOVT ITI ETTUMANOOR ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: Anjaly C R

Name of Project Coordinator : Sarath S R

Name of contractor : Swathy Construction
Agreement date : 30-07-2020
Agreed Amount : ₹ 6,95,25,557.81
Agreed Amount With GST : ₹ 7,78,68,624.74
Site Handover date : 10-08-2020
Project duration : 12 months
Scheduled Date of Completion : 09-08-2021
Expected Date of Completion : with in. 05.11.2022

Status of Work in terms of components:

- Main building civil works (99%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (100%)
- Road and ancillary works, compound wall (100%)
- Land development (90%)
- External water supply, sewerage system (100%)
- Rain water drainage (98%)
- Main building electrical works,ELV ,HVAC (75%)
- Fire protection works (99%)
- Furniture for main building and renovated smart class rooms (100%)

Works were done in the last week - Main building civil works

- Front ramp hand railing works completed.
- Hand railing work inside pump house.

Scheduled progress as on 06-08-2022- 98 %

Achieved progress as on 06-08-2022 - 89 % (As per revised Estimate)

Last week progress - 89%

Current week progress - 0%

**Current Bill Status : CC 8th and part bill submitted for scrutiny and pass.
Amount:Rs. 43,52,039.910**

Current Financial Progress : 82%

Images of works done at Site during last week (with time stamp)



**CLEARING WATER
HYACINTH
(TOURISM)**

**CLEARING WATER HYACINTH
AND PLASTIC WASTE MATERIAL
FROM VEMBANAD LAKE AT
NALUPANK HOUSE BOAT
TERMINAL**

Name of Project Engineer: Anjaly C R

Name of Project Coordinator : Gopakumar

Name of contractor : T.B.A.S Construction
Agreement date : 01/04/2022
Estimated Amount : ₹ 6,56,662.00
Agreed Amount : ₹ 7,18,966.00
Site Handover date : 11/04/2022
Project duration : 03 months
Scheduled Date of Completion : 11/07/2022
Expected Date of Completion : 11/07/2022

Status of Work in terms of components:

- Clearing of water hyacinth and waste material

Cause of work delay/Issues at the site.

- Removed hyacinth and plastic waste materials are replenishing continuously.
- Work will resume next week onwards with providing a barricade to restrict the hyacinth.

Works were done in the last week

- Removing of hyacinth near boat terminal

Scheduled progress as on 06-08-2022- 100%

Achieved progress as on 06-08-2022 - 100 %

Last week progress - 100 %

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress : First and Final bill under preparation

Images of works done at Site during last week (with time stamp)



**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE INSTITUTE
OF HOTEL MANAGEMENT
STUDIES AT PALA, KOTTAYAM
DISTRICT, CONSTRUCTION OF
ACADEMIC BLOCK**

Name of Project Engineer: DON BABY

Name of Project Coordinator : Gopakumar

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Scheduled progress as on 07-08-2022 - 90%

Achieved progress as on 07-08-2022 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : Total bill amount (1st & Part Bill to 13th & Part Bill) ₹ 11,35,31,433.00

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works were done in the last week

- No works have been done.
- AS revalidation in process (Department of Tourism)
- Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.



PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR WITH
INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

Name of Project Engineer: LEKSHMY GOPAN

Name of Project Coordinator : Omanakuttan

Name of contractor : Creators Construction

Agreement date : 15/10/2020

Agreed Amount : Rs 18 Cr

Agreed Amount With GST : Rs20,64,45672/-

Site Handover date : 31/10/2021

Project duration :18 months

Scheduled Date of Completion : 29/04/2023

Expected Date of completion :30/04/2023

Scheduled progress as on 6/08/2022 : 38%

Achieved progress as on 6/08/2022 : 28%

Last week progress in : 2%

Current week progress in: 2%

Current Bill Status : cc st and part bill passed. Amount: 1.37Cr

Current Financial Progress : 8%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (9%)
- Existing class room converted to smart classrooms (0%)
- Sump tank , substation works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

Works done in the last week :

- . Reinforcement works
- . Roof slab shuttering
- . Main building roof slab concrete
- . Hostel building column concrete



**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

MODERNIZING WATER TRANSPORT IN ALAPPUZHA CANALS-PHASE 01

**Name of Project Engineer: Stephy Sebastian
Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-08-2022

Status of Work in terms of components:

- All agreed works has been completed
- The repair of sunken road(near Pagoda resorts) is under progress.
- Construction of damaged road using interlock paver tiles in progress

Works done in the last week

- Laying of GSB for road in progress.
- WMM - final level achieved. interlock works will be progressed soon.
- Interlock work is completed
- some finishing work only pending

Scheduled progress as on 06-08-2022 - 100%

Achieved progress as on 06-08-2022 - 99.5%

Last week progress in 99%

Current week progress- .5%

Current Bill Status : Rs.47,65,31,121 upto 6th bill (Balance -5,56,02,88,367)

Current Financial Progress :90%

Images of works done at Site during last week (with time stamp)



**PUNNAMADA
(TOURISM WORK)**

Punnamada- Starting Point Pathway and Boat Landing at Alappuzha District.

**Name of Project Engineer: Stephy Sebastian
Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 30-08-2022
Expected Date of completion : 30-07-2022

Status of Work in terms of components:

- Pathway
- Solar Lighting

Works done in the last week

- Laying GSB
- Laying paver blocks
- Landscaping works
- Erection of solar LightLights
- Truss work for waiting sheds

Scheduled progress as on 06-08-2022- 98%

Achieved progress as on 06-08-2022- 90%

Last week progress - 80%

Current week progress - 10%

Current Bill Status : 1st & Part Bill ₹50,02,073.00 (incl. GST) and 2nd & Part Bill ₹57,94,300.00 (incl. GST) submitted to Tourism on 26.03.2022 and 24.06.2022 respectively.

Current Financial Progress : 82.79%

Images of works done at Site during last week (with time stamp)



**CHUNGAM
(TOURISM WORK)**

**CHUNGAM(CHAKREPURAKKAL)-
KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of Project Engineer: Stephy Sebastian

Name of Project Coordinator : Gopakumar

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 24-09-2022

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- Backfilling of earth and Construction of Rubble masonry Retaining wall for Pathway and Boat landing
- Backfilling behind Pile and slab retaining wall
- Anchor belt and beam- 69 completed. 30 to be completed.
- Filling of pavement completed using earth
- final levels of the earth filling have been taken in accompany with initial level of GSB

Scheduled progress as on 06-08-2022- 100%

Achieved progress as on 06-08-2022 - 76%

Last week progress - 70%

Current week progress - 6%

Current Bill Status : 1st & Part Bill ₹91,65,612.00 (incl. GST) and 2nd & Part Bill ₹1,29,06,381.00 (incl. GST) submitted to Tourism on 07.03.2022 and 21.06.2022 respectively.

Current Financial Progress : 62.71%

Images of works done at Site during last week (with time stamp)



**PUNNAMADA
(TOURISM WORK)**

**RENOVATION OF PUNNAMADA PARKING
AREA AND PREMISES AT ALAPPUZHA
DISTRICT**

Name of Project Engineer: Stephy Sebastian

Name of contractor : TBAS Construction, Aluva
Agreement date : 11/01/2022
Agreed Amount : Rs 87,81,166.60
Agreed Amount With GST : Rs 98,34,906.59
Site Handover date : 21/01/2022
Project duration : 12 months
Scheduled Date of Completion : 20/01/2023
Expected Date of completion : 20/12/2022

Status of Work in terms of components:

- Parking Area
- Landscaping
- Plumbing

Works done in the last week

- Clearing the site
- Removing the interlock
- Initial Level of earth levelling completed
- Quarry muck is ready for filling the ground
- The bund formation for the regulator have been started

Scheduled progress as on : 06-08-2022-

Achieved progress as on : 06-08-2022- 17 %

Last week progress - 15%

Current week progress - 2%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of Project Engineer: SILPA R

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 29-01-2022 as per EOT
Expected Date of completion : 15-02-2023

Status of Work in terms of components:

- 20m groynes – 5 nos- 2completed
- 30M GROYNES -7nos- 2 in progress, 3completed.
- 40M GROYNES – 9 nos -5completed.
- 50M GROYNES – 9 nos -6completed.
- Sea wall length-305 m – not started
- 172805.452 MT boulders reached out of 178922 MT (100%)
- 2T TETRAPODS –23151nos. casted out of 23902 nos. (96.86%)
- 5T TETRAPODS – 2955 nos. casted out of 2956 nos.(99.9%)
- Earthwork Excavation – 23131.66 m3 completed out of 45955.7 M3 (43%)

Works done in the last week

The total no.of tetrapods casted 2T-0& 5T-0nos

- Supplying and Laying of Boulders -0 MT
- Laying of tetrapods in G19, G13completed.
- 2361 Nos 5T tetrapods layed
- 12541 Nos 2T layed.
- **no work can be done without RE sanction due to the design changes and change of various items.**

Scheduled progress as on 06-08-2022 – 100 %

Achieved progress as on 06-08-2022 - 79 %

Last week progress - 0%

Current week progress -0%

Current Bill Status : 7th bill submitted for an Amt of Rs.48492386.46
Total bill amount - Rs. 450663433.14

Current Financial Progress : 87.84%

Images of works done at Site during last week (with time stamp)



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of Project Engineer: M A FASEELA NASAR

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹ 26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :15-06-2022 as per EOT
Expected Date of completion :15-02-2023

Scheduled progress as on 06-08-2022- 100 %

Achieved progress as on 06-08-2022-40 %

Last week progress - 1 %

Current week progress - 2 %

Current Bill Status: 6 part bill submitted for an amount of Rs 18,29,20,633/-

Current Financial Progress : 70 %

Images of works done at Site during last week (with time stamp)


Status of Work in terms of components:

- 20M GROYNES - 6 NOS- 2 started
- 25M GROYNES - 15 NOS- 2 cmplt, 14 started
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 60300.74 T (64%) 94497 MT
- 2T TETRAPODS - 10075 (100%) nos casted out of 9874 NOS
- 5T TETRAPODS - 2245 (94.13%) nos casted out of 2385 NOS
- GEOMAT - 64739 M2 (not done)
- EARTHWORK EXCAVATION - 3290 M3(not done)

Works done in the last week

The total no.of tetrapods casted 2T-0& 5T-0nos

- Supplying and Laying of Boulders - 2608.16 T.
- 333 5T tetrapod layed
- 986 2T tetrapod layed
- **no work can be done without RE sanction due to the design changes and change of various items**

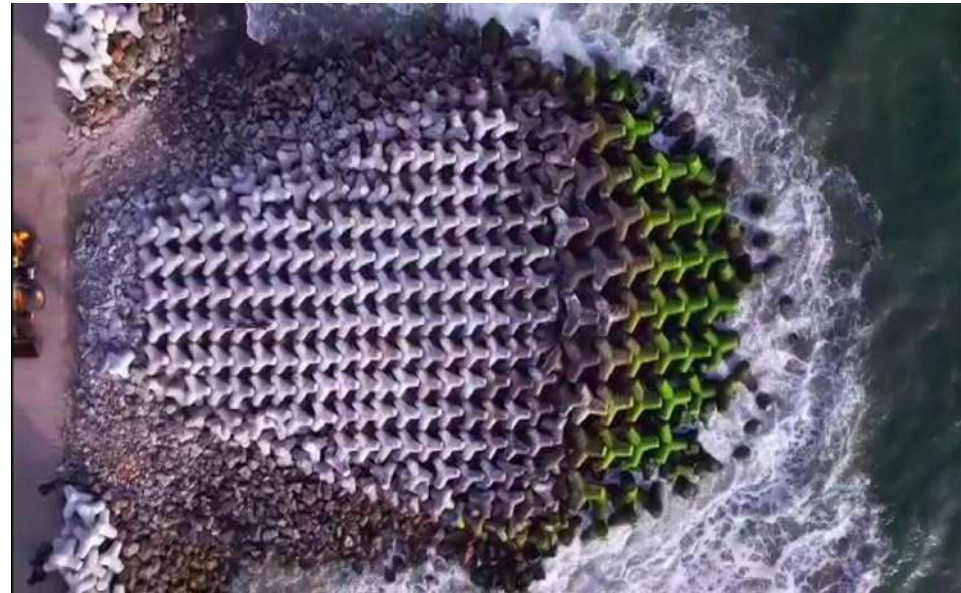

**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of Project Engineer: SILPA R

Name of Project Coordinator : RAJASEKHARAN PILLAI

Name of contractor : Ramalingam construction Company Pvt. Lmtd.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 15-06-2022 as per EOT
Expected Date of completion : 15-02-2023

Status of Work in terms of components:

- 1 20M GROYNES - 2 NOS-One is completed
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- 3completed and 2nos is in progress
- 4.61876.225MT boulders reached out of 74546 MT(83%)
5. 2T TETRAPODS -8930casted out of 8930NOS(100%)
6. 5T TETRAPODS - 1190nos casted out of 1199NOS(99%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

Works done in the last week -

The total no.of tetrapods casted 2T-0& 5T-0nos

- Groynes G1,G2 ,G3 & G5;G6 are completed.
- Supplying and laying of boulders-0T
- 772 5T tetrapod layed
- 4160 2T tetrapod layed
- **no work can be done without RE sanction due to the design changes and change of various items.**

Scheduled progress as on 06-08-2022 - 100%

Achieved progress as on 06-08-2022 -63 %

Last week progress in -0%

Current week progress in 0%

Current Bill Status :7th part bill submitted for an Amt of Rs. 12811052.37
Total bill amount - Rs. 170854619.44

Current Financial Progress in :85%

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

**Name of Project Engineer: M A FASEELA NASAR
Name of Project Coordinator : RAJASEKHARAN PILLAI**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 15-06-2022 as per EOT
Expected Date of completion : 15-02-2023

Scheduled progress as on 06-08-2022 - 100 %

Achieved progress as on 06-08-2022 - 75 %

Last week progress - 0 %

Current week progress - 0%

Current Status : 8 part bills submitted for an amt of Rs 23,13,12,922/-

Current Financial Progress in % : 80%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 cmplt
- 30M GROYNES - 10 NOS- 7 cmplt 1 pending due local issue, 1 ongoing
- 40M T GROYNE - 4 Nos -1 ongoing
- TOTAL QUANTITY OF BOULDERS - 76096.554 MT (75%) reached out of 101487 MT
- 2T TETRAPODS - 8941(100 %) nos casted out of 8941 NOS
- 5T TETRAPODS - 3432 (100 %) nos casted out of 3432 NOS
- GEOMAT - 4850 m2 (6 %) layed out of 76299 M2
- EARTHWORK EXCAVATION - (8191.37 m3 out of 62380 M3)

Works done in the last week

- 2T tetrapod casted - 0 nos.
- 5T tetrapod casted - 0 nos.
- Supplying and Laying of Boulders - nil
- Groyne G2, G3, G6, G7, G8, G9, G11, G15, G16 completed.
- 1881 5T tetrapods layed
- 5458 2T layed.
- **no work can be done without RE sanction due to the design changes and change of various items.**



**GROYNES SITE AT
KATTOOR
(KIIFB)**

**Construction of 34 nos. Groyne
at Kattoor from Ch.168.465KM
TO CH 171.627KM (Old CH
96.643KM TO CH 9.535 KM)**

Name of Project Engineer: SILPA R

Name of Project Coordinator : Mahadevan P

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 15-06-2022 as per EoT
Expected Date of completion : 15-10-2022

Scheduled progress as on 06-08-2022–100% (as per EoT given)

Achieved progress as on 06-08-2022- 80%

Last week progress - 0%

Current week progress -0%

Current Bill Status :8th bill submitted for an Amount of Rs.47715746.89/- .Total bill amount - Rs. 451641352.92

Current Financial Progress : 92.1%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groyne - 3 started out of 3
- 30m Groyne-5nos started out of 7
- 40m groyne - 19 nos started out of 24
- Total boulders quantity - 174010.85 MT boulders reached out of 174010 MT (100%)
- 2T TETRAPODS – 21553 nos (99.95%) casted out of 21562 nos.
- 5T TETRAPODS – 3144 (100%) nos. casted out of 3144 nos.
- Geomat - 14015.5m2
- Earthwork Excavation - 31767.090m3 out of 42122 M3

Works done in the last week

- 2T & 5T casting are completed
- Supplying and Laying of Boulders - nil
- 2548 Nos 5T tetrapods layed
- 12035 Nos 2T layed.
- **no work can be done without RE sanction due to the design changes and change of various items.**



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of Project Engineer:MEENU E S

Name of Project Coordinator : Omanakuttan

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion : 23/08/2021
Expected Date of completion : 30/10/2022

Status of Work in terms of components:

- Main building civil works –51%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works –3%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

- . Main building
- . Electrical works on going
- . Road work wmm completed

Scheduled progress as on 06/08/2022 - 100%

Achieved progress as on 06/08/2022 - 80%

Last week progress : 44%

Current week progress :5%

Current Bill Status :1st bill submitted to KASE, 2nd bill submitted to KASE,3rd bill submitted to KIIDC

Current Financial Progress : 56%

Images of works done at Site during last week (with time stamp)



**Thenmala
(Tourism Project)**

IMPROVEMENT AND DEVELOPING ECO-TOURISM AT THENMALA DAM IN KOLLAM DISTRICT

Name of Project Engineer: Meenu ES

Name of Project Coordinator : OMANAKUTTAN

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹3,45,61,108.96
Agreed Amount With GST : ₹4,07,82,108.57
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 31-08-2022

Scheduled progress as on 06/08/2022- 100%

Achieved progress as on 06/08/2022-59%

Last week progress -54%

Current week progress -5%

Current Bill Status : part bill preparation

Current Financial Progress : 58%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Shop (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)
pavilion(50%)

Works done in the last week

1. Toilet, security room and cloak room-plinth beam work completed.column shuttering work under progress.brick work in progress
2. Shed to shop -roof slab concrete completed
3. Pavilion-step Work progress
4. Seating area clearance completed.



**ITI
DHANUVACHAPU
RAM
(KASE)**

UPGRADATION OF GOVT. ITI DHANUVACHAPURAM ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: ATHEESH P MOHAN

Name of Project Coordinator : Sarath S R

Name of contractor : Heather Construction
 Agreement date : 25-11-2019
 Agreed Amount : ₹11.18 Cr
 Agreed Amount With GST : Rs. 12,52,34,417.4
 Site Handover date : 04-12-2019
 Project duration : 20 months
 Scheduled Date of Completion : 30-09-2022
 Expected Date of completion 30-09-2022

Scheduled progress as on 06-08-2022- 95 % (Scope of the work were increased as per the instructions from SPV)

Achieved progress as on 06-08-2022 - 95%

Last week progress - 94%

Current week progress -1%

Current Bill Status :15th bill submitted amount:2,02,42,253.35/-

Current Financial Progress :79.42%

Status of Work in terms of components:

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering completed
- GF primer work 100% Completed
- GF Electrical work completed
- GF plumbing work 100% completed
- FF Block Work 100% completed
- FF Ceiling work 100% completed
- FF plastering 100% completed
- FF Elec- concealed work completed
- GF Tile work 100%
- FF primer work 100% completed
- **Fire fighting works-delayed due to pending of approval from KASE (SPV)**

Works done in the last week

- Kerb stone works
- Sump tank plastering works
- cleaning works

Inauguration - review meeting conducted at site in presence of MLA, ITI officials etc.

Inauguration date fixed. Hon. CM will inaugurate the academic building on **12 th august 2022.**

ITI Planning to conduct 4 days inauguration function from 9th aug. to 12 th aug.



LIST OF TOURISM DEPARTMENT COMPLETED PROJECTS

(PHYSICAL PROGRESS 100%)

SL No.	Name of Project	Financial Progress	Remarks
1	Karappuzha Phase III - Construction of Viewing Tower, Bamboo Pavilion and Bridge (Wayanad)	100.00%	-
2	Karappuzha Phase III - Construction of Pathway, Fishing Dock, Pond, Gazebo, Parking yard and Landscaping (Wayanad)	100.00%	-
3	Development of Peruvannamuzhi Dam Tourism Project in Kozhikode District	65.22%	4 th and final bill amounting to ₹1,07,88,549.00 submitted to Department of Tourism for release of payment on 20.04.2022.
4	Additional Work I of Eco Lodge Construction at Idukki	100.00%	-
5	Additional Work II of Eco Lodge, Idukki	0.00%	First and part bill amounting to ₹36,81,648.00 submitted to Department of Tourism on 14.03.2022. (Contract PAC: ₹45,85,722.41). Revised Estimate preparation under progress.
6	Providing Temporary Rest Room cum Store (Container Type) for Life Guards at Alappuzha Beach	0.00%	First and final bill amounting to ₹11,96,272.00 submitted to Department of Tourism on 23.03.2022.
