


# KIIDC WEEKLY PROGRESS REPORT



KIIDC

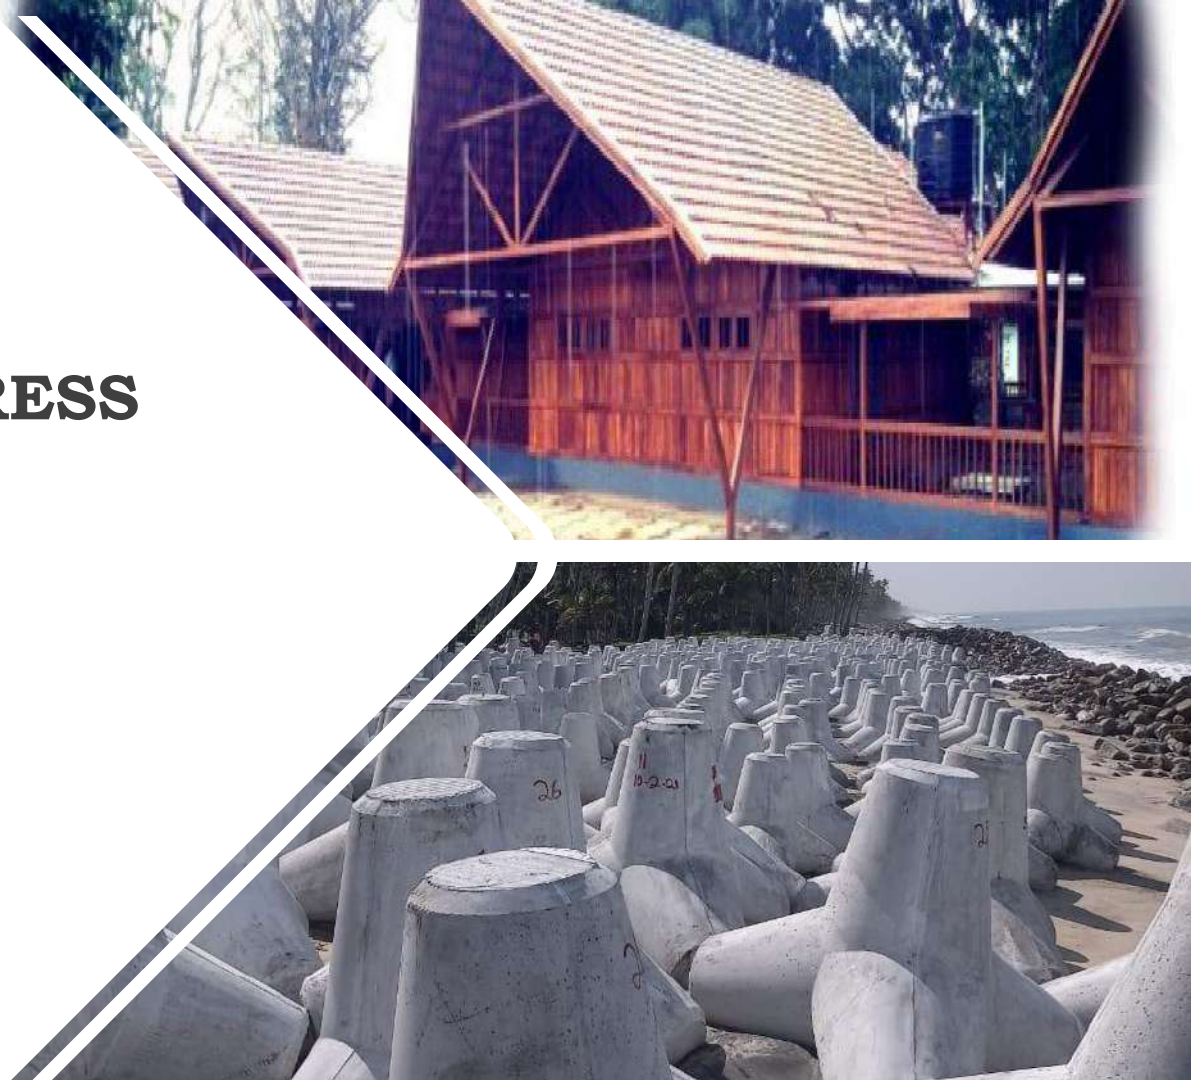

# **PROJECTS IN KANNUR DISTRICT**

**ITI KANNUR  
(KASE )**

# **UPGRADATION OF GOVT. ITI KANNUR ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer : Joel J Varghese  
Name of Project Coordinator : Visakh A.K**

Name of contractor : Shameer M A  
Agreement date : 26-08-2020  
Agreed Amount :Rs.3,40,93,937.97  
Agreed Amount With GST : Rs.3,64,82,353.00  
Site Handover date : 04-09-2020  
Project duration : 8 months  
Scheduled Date of Completion : 03-05-2021  
Expected Date of completion : 17-05-2022

**Scheduled progress as on 15-08-2022 54%**

**Achieved progress as on 15-08-2022 33%**

**Last week progress in 1%**

**Current week progress - 1%**

**Current Bill Status : 2nd Bill submitted**

**Current Financial Progress :31%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

Footing works 100 % completed  
Stub columns, Grade beam  
concreting 100% completed

Ground floor columns concreting  
100% completed

Block Work 95%

Internal Plastering 90%

External Plastering 80%

**Work done in last week**

Excavation for gate work  
Front gate security cabin  
footing  
mS pipe section setting



**REGULATOR  
ANCHARAKANDY  
RIVER AT  
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF  
REGULATOR WITH LOCK ACROSS  
ANCHARAKANDY RIVER AT  
PARAPRAM IN PINARAYI  
PANCHAYATH, KANNUR DISTRICT**

**Name of Project Engineer : Athul Ashar**

**Name of Project Coordinator : Visakh A K**

Name of contractor : PGCC  
Agreement date :06-11-2020  
Agreed Amount : ₹44.49 Cr  
Agreed Amount With GST : Rs. 498,385,551.00  
Site Handover date : 16-11-2020  
Project duration : 18 months  
Scheduled Date of Completion : 15-05-2022 (extended to 21-11-2022)  
Expected Date of completion : 30-06-2023

**Status of Work in terms of components:**

- Regulator - 70%
- Foot Bridge -57%
- Lock Portion -95%
- Side Protection -75%
- Mechanical Works -10%
- Generator Cum Watchman Room -60%
- Electrical Works -

**Works done in the last week**

- Switchroom main slab concrete done
- P2 to P3 footbridge concrete completed
- Piling work for right side U/S retail wall
- Bund dismantled due to heavy rain

**Scheduled progress as on 12-08-2022 100%**

**Achieved progress as on 12-08-2022 - 71%**

**progress upto last week = 69.5%**

**Current week progress - 1.5%**

**Current Bill Status :Eight Part Bill submitted**

**Current Financial Progress : 62%**

**Images of works done at Site during last week (with time stamp)**



**REGULATOR  
UMMENCHIRA RIVER  
AT  
CHEKKUPALAM(KIIFB)**

**KIIFB - CONSTRUCTION OF REGULATOR  
CUM BRIDGE ACROSS UMMENCHIRA  
RIVER AT CHEKKUPALAM IN PINARAYI  
PANCHAYATH,KANNUR DISTRICT**

**Name of Project Engineer : Joel J Varghese**

**Name of Project Coordinator : Visakh A K**

Name of contractor : PGCC  
Agreement date :04-05-2022  
Agreed Amount : ₹34.47Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 13-05-2022  
Project duration : 18 months  
Scheduled Date of Completion : 13-11-2023  
Expected Date of completion : 13-11-2023

Scheduled progress as on 15-08-2022 - 1%

Achieved progress as on 15-08-2022 - 1%

Progress upto last week-1 %

Current week progress - 1%

Current Bill Status :

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Regulator -
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

**Works done in the last week**

Alignment drawing has been prepared  
Letter sent Permission seeking from Social forestry  
Letter sent Permission for shifting equipment to DTPC  
Letter sent to KWA regarding the NoC





**RCB KUPPAM RIVER  
IN  
KOOVERY-KATTAM  
PALLY (KIIFB)**

**CONSTRUCTION OF REGULATOR  
CUM BRIDGE ACROSS KUPPAM  
RIVER IN KOOVERY-KATTAMPALLY  
IN CHAPPARAPADAVU PANCHAYAT ,  
THALIPARAMBA TALUK, KANNUR  
DISTRICT**

**Name of Project Engineer: Athul Ashar**

Name of contractor : Infab Infrastructures Ltd  
Agreement date :15-10-2019  
Agreed Amount : ₹ 18,57,64,823.98  
Agreed Amount With GST : 22,03,74,512.96 (as per RE)  
Site Handover date : 07-11-2019  
Project duration : 18 months  
Scheduled Date of Completion : 07-05-2021  
Expected Date of completion : NA

### Status of Work

- The contractor has filed a Writ Petition No 1217/2021 in the Hon'ble High Court of Kerala to stay all coercive steps like termination pursuant to the demand for extension of Bank Guarantee as seen in Ext.P17,till the disposal of this Writ petition.Court directed the 6th respondent(vigilance) to submit report on the matter.Vigilance made an enquiry regarding the matter and they will submit the report to the honourable court.Final decision will be taken according to the verdict from the court.

**Scheduled progress as on 12-08-2022 100%**

**Achieved progress as on 12-08-2022 - 0%**

**Progress up to last week-0 %**

**Current week progress - 0%**

**Current Bill Status :NA**

**Current Financial Progress :0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

**THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2**

Phase 1- 14 projects- As received - 40.95 crores		
Phase 2- 14 projects-AS received - 37.212 crores (Total AS received for 28 Projects – 78.162)		
	Phase 1	Phase 2
<ul style="list-style-type: none"> <li>MoU signed – 18 projects</li> </ul>	Pindali kalari, Andalurkav Temple, Illikunnu church, Kottiyoor siva temple, Makreri temple, Lokanarkav temple, Thrissillery temple, Thirunelli temple, Thiruvangad Ramaswamy temple, Jagannath temple	Kadirur suryanarayana temple, Chirakkakavu temple, Mridangasaileswary temple, Oorpazhichikaav temple, Puralimala temple, Peralassery temple, Valliyoorkav temple, Thacholi manikoth
<ul style="list-style-type: none"> <li>Agreement executed - 10 projects</li> </ul>	Pindali kalari, Andalurkav Temple, Kottiyoor siva temple- Streetscape, Kottiyoor siva temple-Tourist amenities, Lokanarkav temple, Makreri Subramanyaswmi temple, Illikunnu church, Jagannath temple	Puralimala temple, Pazhassiraja smrithimandapam
<ul style="list-style-type: none"> <li>Works started – 9 (GFC drawing prepared by KIIFB)</li> </ul>	Andalurkav temple, Illikunnu church, Pindali kalari, Kottiyoor temple- Streetscape, Kottiyoor siva temple- Tourist amenities, Jagannath temple, Lokanarkav temple, Makreri Subramanyaswami temple	Puralimala temple
<ul style="list-style-type: none"> <li>Selection notice issued - 8 projects</li> </ul>	Thiruvangad Ramaswamy temple, Thirunelli Temple, Thrissillery Temple	Sree Thacholi Manikoth Temple, Vadakara Tazhe angadi, Peralassery Temple, Chirakkakav temple, Thalakkal Chandu Museum - Panamaram

**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

**THALASSERY HERITAGE PROJECT - Phase 1 & Phase 2**

	Phase 1	Phase 2
<ul style="list-style-type: none"> <li>• Tender to be finalized - 2 Projects</li> </ul>	Municipal Stadium (THP Office), Kakkulangara Mosque (Letter submitted to Tourism for tender excess approval)	
<ul style="list-style-type: none"> <li>• To be retendered - 2 projects (After revising the TS in DSR 2018)</li> </ul>	Odathil Mosque and Paris Hotel Street	Kadirur Surya Narayana Temple
<ul style="list-style-type: none"> <li>• TS to be issued - 4 projects</li> </ul>		Sree Mridanga Saileswari Temple, Thodeekalam Siva Temple, Sree Oorpazhachi Kavu Temple, Valliyoorkavu temple
<ul style="list-style-type: none"> <li>• To be dropped - 2 projects (NOC not received)</li> </ul>		Pazhassi Kovilakam (Mattannur), Arakkal Kettu (Total amount – 10.5Cr)

**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT - THALASSERY  
HERITAGE PROJECT - PHASE 1  
-Pazhassi Circuit - Pindali Kalari  
House(Pathway,Conservation of  
Kalarithara,Pond restoration ,Seating,  
Landscaping ,Electrification)at  
Iritty,Kannur**

**Name of Project Engineer:Joel J Varghese**

**Name of Project Coordinator : Visakh A.K**

Name of contractor : M/s Classic Builders  
Agreement date : 17-02-2021  
Agreed Amount : ₹ 0.6238 Cr  
Agreed Amount With GST : Rs. 6987127.71  
Site Handover date :  
Project duration : 12 months  
Scheduled Date of Completion : 27-02-2022  
Expected Date of completion :

Scheduled progress as on 15-08-2022 : 52%

Achieved progress as on 15-08-2022 - 38%

Progress upto last week - 1%

Current week progress -1%

Current Bill Status : Ready for Part 1 bill

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

Gallery Work 100 % completed  
Kalarithara 50%  
Kalasamandaapam 25%  
Pond 25%

**Works done last Week**

**Heavy rainfall no work done**

Unavailability of brick



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 - Cultural Circuit -Andalur Kavvu**

**Name of Project Engineer: Athul Ashar**

**Name of Project Coordinator : Visakh A.K**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.5189 Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 1.701 Cr  
Project duration : 12 months  
Scheduled Date of Completion : 26-02-2022  
Expected Date of completion :

**Status of Work in terms of components:**

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

**Work done in last week**

- work stopped due to heavy rain



**Scheduled progress as on 12-08-2022 : 100%**

**Achieved progress as 12-08-2022 - 17 %**

**Progress upto last week - 0%**

**Current week progress -0%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**





**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -illikunnu**

**Name of Project Engineer: Athul Ashar  
Name of Project Coordinator : Visakh A.K**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26/02/2021  
Agreed Amount : ₹ 8300000  
Agreed Amount With GST : Rs  
Site Handover date :  
Project duration : 12 months  
Scheduled Date of Completion : 26/02/2022  
Expected Date of completion :

**Status of Work in terms of components of cemetery :**

- Land scaping of cemetery area
- Lighting
- Conservation of ceiling, wood work, joinery

**Work done in last week**

- Polishing work

**Scheduled progress as on 12-08-2022 : 100%**

**Achieved progress as on 12-08-2022 - 35%**

**Progress upto last week - 34%**

**Current week progress -1%**

**Current Bill Status : 1st bill submitted**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

# **KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -Jaganath Temple**

**Name of Project Engineer: Athul Ashar**

**Name of Project Coordinator : Visakh A.K**

Name of contractor : Sri. Varkeychan Vallamattam  
Agreement date : 26/02/2021  
Agreed Amount : ₹ 1,48,17,938.56  
Agreed Amount With GST : 1.56cr

Site Handover date : 08/03/2021  
Project duration : 12 months  
Scheduled Date of Completion : 08/03/2022  
Expected Date of completion :

**Status of Work in terms of components :**

- Pathway
- Rivival of pond
- Compound wall
- Landscaping

**Work done in last week**

- Work stopped due to heavy rain

**Scheduled progress as on 12-08-2022 : 100%**

**Achieved progress as 12-08-2022 - 27%**

**Progress upto last week- 0%**

**Current week progress -1%**

**Current Bill Status : Nil**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT - THALASSERY  
HERITAGE PROJECT-Makreri  
Subramanyaswami Temple (Cultural  
Circuit)**

**Name of Project Engineer: Athul Ashar**

**Name of Project Coordinator : Visakh A.K**

Name of contractor : M/S Saaj Constructions  
Agreement date : 17/06/2021  
Agreed Amount : ₹ 1,83,50,573.45/-  
Agreed Amount With GST : 2,05,52,642.26/-  
Site Handover date : 27.06.2021  
Project duration : 12months  
Scheduled Date of Completion : 27/06/2022  
Expected Date of completion :

### Status of Work in terms of components :

- Ootupura
- Toilet block
- Landscaping
- Water supply and Sanitary Arrangements
- street scape of Paving of Chuttambalam
- Stone paving
- Conservation of pond
- Electrification

### Work done in last week

- Ootupura laterite masonry started
- Plinth belt concrete for toilet completed
- Reinforcement for toilet plinth progressing.

Scheduled progress as on 12-08-2022 : 100 %

Achieved progress as 12-08-2022 - 12%

Last week progress - 11%

Current week progress -1%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT –THALASSERY HERITAGE  
PROJECT-PHASE 1-pazhassi circuit –kottiyoor shiva  
temple(streetscape,landscaping,agrashala,carpark  
ing,stage and electrical work at kottiyoor shiva  
temple in irrity,Kannur district)**

**Name of Project Engineer :Basil George**

**Name of Project Coordinator : Visakh A.K**

Name of contractor : M/s Rubicon construction  
Agreement date : 05/10/2021  
Agreed Amount : ₹ 1.21 cr  
Agreed Amount With GST : RS 1,36,06,740.60  
Site Handover date : 14/10/2021  
Project duration : 12 months  
Scheduled Date of Completion : 13-10-2022  
Expected Date of completion : 13/10/2022

**Status of Work in terms of components:**

- Streetscape
- Landscaping
- Agrashala
- Car parking
- Stage
- electrification

**Work done in last week**

Work has delayed due to heavy rain.

**Scheduled progress as on 12/08/2022 : 80%**

**Achieved progress as 12-08-2022 - 50%**

**Last week progress - 0%**

**Current week progress -0%**

**Current Bill Status : 1st bill submitted**

**Current Financial Progress : 17%**

**Images of works done at Site during last week (with time stamp)**





# COMPREHENSIVE DEVELOPMENT OF MUZHAPPILANGAD AND DHARMADOM BEACH IN KANNUR DISTRICT

**IN PRINCIPLE SANCTION : 233.71 Cr**

**FUNDING AGENCY : KIIFB**

**The whole project is divided into 4 Character areas**

**AS Amount for Character Area 1 : 79.51 Cr**

**CA 1 - AS DATE : 17/03/2022**

**CA 1- TS DATE : 22/03/2022**

## **CHARACTER AREA 1**

- ❖ CRZ clearance obtained
- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai and revised architectural drawing prepared by consultant architect received on 01.12.2021
- ❖ KIIFB approved Character area 1 for an amount 79.51 Cr on 17.03.2022
- ❖ Work tendered and tender opened on 23.04.2022
- ❖ Selection notice issued to ULCCS. Agreement to be executed

## **CHARACTER AREA 2**

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

## **CHARACTER AREA 3**

- ❖ Survey works completed
- ❖ EIA study completed
- ❖ Sea side retaining wall design prepared by IIT Chennai
- ❖ Revised DPR will be submitted to KIIFB after obtaining the revised drawings

## **CHARACTER AREA 4**

- ❖ DPR and detailed project components are under preparation with Consultant architect CBRE

# **PROJECTS IN WAYANAD DISTRICT**

**Community micro  
irrigation at  
Athichal  
Mundankolly  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Athichal  
Mundankolly in Ambalavayal  
Panchayath Wayanad district -  
CMI Part**

**Name of Project Engineer: Athul Ashar**

**Name of Project Coordinator : Visakh Ak**

**Name of contractor** : M/S Mahindra EPC Irrigation limited  
**Agreement date** : 13-04-2022  
**Agreed Amount** : 2.14 Crores  
**Agreed Amount With GST** :  
**Site Handover date** : 22-04-2022  
**Project duration** : 6 months  
**Scheduled Date of Completion** :21-10-2022  
**Expected Date of completion** :21-10-2022

**Status of Work in terms of components:**

- Main line
- Submain line
- Automation

**Works done in the last week**

- Survey completed
- Alignment marking is restarted

**Scheduled progress as on 12/08/2022 - 40 %**

**Achieved progress as on 12/08/2022 - 10 %**

**Last week progress in : 8%**

**Current week progress : 2%**

**Current Bill Status : Nil**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**

**Community micro  
irrigation at  
Athichal  
Mundankolly  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Athichal  
Mundankolly in Ambalavayal  
Panchayath Wayanad district -  
Civil**

**Name of Project Engineer: Athul Ashar**

**Name of Project Coordinator : Visakh Ak**

**Name of contractor** : Shri Saji mathew  
**Agreement date** : 04-04-2022  
**Agreed Amount** : 25.05 Lakhs  
**Agreed Amount With GST** :  
**Site Handover date** : 13-04-2022  
**Project duration** : 4 months  
**Scheduled Date of Completion** :12-08-2022  
**Expected Date of completion** :12-08-2022

**Status of Work in terms of components:**

- Irrigation room
- Sump tank
- Electrical Works

**Works done in the last week**

Work not yet started

**Scheduled progress as on 12/08/2022 - 50 %**

**Achieved progress as on 12/08/2022 - 0 %**

**Last week progress in : 0%**

**Current week progress : 0%**

**Current Bill Status :**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**

**THALASSERY  
HERITAGE PROJECT  
(KIIFB-TOURISM )**

KIIFB Project - KIIFB Project- Thalassery Heritage Project - Phase 2 - Pazhassi Circuit -Valliyoorkavu temple - Streetscape (Stone steps to temple, Lamp Post, Electrification) at Mananthavady in Wayanad District – Conducting test on given samples of cement, Aggregate, Laterite and Sadarhalli granite stone

**Name of Project Engineer :Athul ashar**

**Name of Project Coordinator : Visakh A.K**

Name of contractor : Shri. Ameer Ali N  
Agreement date : 30 -04-2022  
Agreed Amount : 3673949.76  
Agreed Amount With GST :  
Site Handover date : 12/05/2021  
Project duration : 6 months  
Scheduled Date of Completion : 11-11-2022  
Expected Date of completion : 11-11-2022

**Status of Work in terms of components:**

- Stone steps to temple
- Lamp post
- electrification

**Work done in last week**

Work has delayed due to heavy rain.

**Scheduled progress as on 12/08/2022 : 60%**

**Achieved progress as 12-08-2022 - 50%**

**Last week progress - 50%**

**Current week progress -0%**

**Current Bill Status : nil**

**Current Financial Progress : nil**

**Images of works done at Site during last week (with time stamp)**





# PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS  
POONUR  
PUZHA-POOLAKAD  
AVU (KIIFB)**

**KIIFB PROJECT CONSTRUCTION  
OF RCB ACROSS POONUR PUZHA  
NEAR KWA PUMPING HOUSE AT  
POOLAKADAVU IN KURUVATTOOR  
PANCHAYATH**

**Name of Project Engineer: Athul Ashar**

**Name of Project Coordinator : Bibin Giri**

Name of contractor : ULCCS Ltd.  
Agreement date : 18-08-2021  
Agreed Amount : ₹22,68,45,702.29  
Agreed Amount With GST : Rs.  
Site Handover date : 27-08-2021  
Project duration : 18 months  
Scheduled Date of Completion : 26-02-2023  
Expected Date of completion : 26-02-2023

**Status of Work in terms of components:**

- Regulator -17%
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

**Works done in the last week**

- Bar bending for Pile cap and Pile
- Major works are suspended due to high flood

**Scheduled progress as on 12-08-2022 - 29%**

**Achieved progress as on 12-08-2022- 17%**

**Progress upto last week- 16 %**

**Current week progress - 1 %**

**Current Bill Status : CC First and part under preparation**

**Current Financial Progress : nil**

**Images of works done at Site during last week (with time stamp)**



**ITI KOYILANDY  
(KASE)**

**UPGRADATION OF GOVT. ITI  
KOYILANDY ON PAR WITH  
INTERNATIONAL STANDARDS**

**Name of Project Engineer : Basil George**

**Name of Project Coordinator : Sethumadhavan K.P  
(Additional charge)**

Name of contractor : ULCCS Ltd.  
Agreement date : 14-08-2020  
Agreed Amount : ₹4.22 Cr  
Agreed Amount With GST : Rs. 4,22,86,606  
Site Handover date : 14-08-2020  
Project duration : 12 months  
Scheduled Date of Completion :13-08-2021  
Expected Date of completion :13-11-2021

**Status of Work in terms of components:**

- Main Building Civil works – 85%
- Main Building Electrical works – 80%
- Main Building ELV Works - 75%

**Works done in the last week**

- Work delayed due to not getting approval for RE from KASE

**Scheduled progress as on 12-08-2022- 100%**

**Achieved progress as on 12-08-2022 - 85%**

**Last week progress- 0%**

**Current week progress - 0%**

**Current Bill Status : CC 3rd and part submitted**

**Current Financial Progress : 34.3%**

**Images of works done at Site during last week (with time stamp)**



**THALASSERY  
HERITAGE  
PROJECT  
(KIIFB-TOURISM )**

**KIIFB PROJECT –THALASSERY HERITAGE  
PROJECT-PHASE 1-pazhassi circuit –  
Lokanarkavu Temple (Conservation of  
Thantrimadom, Folklore, Oottupura,Chiras,  
Plumbing and Electrification at  
Lokanarkavu Temple in Vadakara,  
Kozhikode District)**

**Name of Project Engineer: Basil George**

**Name of Project Coordinator : Visakh Ak**

Name of contractor : Saaj Constructions  
Agreement date : 17-06-2021  
Agreed Amount : ₹ 3,78,74,574.27/-  
Agreed Amount With GST : Rs.  
Site Handover date : 26-06-2021  
Project duration : 12 months  
Scheduled Date of Completion :25/06/2022  
Expected Date of completion :31/03/2023

**Status of Work in terms of components:**

- thanthrimadam up to plinth belt were completed.
- big chira side protection work in progress.
- compound wall work

**Workshops done in the last week**

Compound wall-  
pointing  
Pavement works-gsb  
laying

Scheduled progress as on 12-08-2022- 90%

Achieved progress as on 12-08-2022 - 8%

Last week progress- 0%

Current week progress - 0%

Current Bill Status :

Current Financial Progress :

Images of works done at Site during last week (with time stamp)



**RCB  
PERINCHERIKADAVU  
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM  
BRIDGE AT U/S OF  
PERINCHERIKADAVU IN KUTTIADY  
RIVER (GULIKAPUZHA) AT KOZHIKODE  
DISTRICT**

**Name of Project Engineer : Basil George**

**Name of Project Coordinator : Sethumadhavan K.P  
(Additional charge)**



**Name of contractor** : TBAS – EKK Consortium  
**Agreement date** : 07-09-2020  
**Agreed Amount** : ₹ 61,13,34,133.18/-  
**Agreed Amount With GST** : ₹ 68,46,94,229/-  
**Site Handover date** : 17-09-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :16-03-2022 (Extended to 15-04-2023)  
**Expected Date of completion** :01-03-2024

**Scheduled progress as on 12-08-2022 - 85%**

**Achieved progress as on 12-08-2022 - 24%**

**Progress upto last week--24%**

**Current week progress 0%**

**Current Bill Status : 2 nd bill submitted**

**Current Financial Progress : 17%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Regulator -14%
- Lock Portion -
- Side Protection -35%
- Deck Slab -
- Approach Road -
- Mechanical Works-
- Generator Cum Watchman Room-
- Electrical Works -

**Works done in last week**

Work delayed due to heavy rain.  
RE submitted to KIIFB for Scrutiny



**PROJECTS IN  
MALAPPURAM  
DISTRICT**

**Puzhankavu  
Regulator  
(KIIFB)**

# **KIIFB Project - Construction of Regulator at Puzhankavu across Kadalundi River**

**Name of Project Engineer : RAHEES.P**

**Name of Project Coordinator : Pushparaj**

Name of contractor : Infab Infrastructure Pvt Ltd  
Agreement date : 17-12-2019  
Agreed Amount : ₹ 9,79,65,435.62  
Agreed Amount With GST : Rs. 10,97,21,287.89  
Site Handover date : 17-12-2019  
Project duration : 18 months  
Scheduled Date of Completion :16/06/2021-(Extended to 21-11-2022)  
Expected Date of completion :21-11-2022

**Status of Work in terms of components:**

- Regulator -100%
- Side Protection -95%
- Mechanical Works -90%
- Generator Cum Watchman Room -50%
- Electrical Works -

**Works done in the last week.**

- Continuing Heavy flow of water at site.
- RE res-submission work progressing..
- Guard room truss work completed and waiting for the sheet .

**Scheduled progress as on 12-08-2022-95.6%**

**Achieved progress as on 12-08-2022 -95.6%**

**Progress upto last week -95.50%**

**Current week progress - 0.10%**

**Current Bill Status : Total Bill submitted ₹7.10 Crores (9th part bill)**

**Current Financial Progress in :72.53%**

**Images of works done at Site during last week**



**RCB  
Moothikkayam  
(KIIFB)**

# **KIIFB - Construction of Regulator cum Bridge across thoothapuzha keezhmurikadavu moothikkayam in moorkanad panchayath**

**Name of Project Engineer: Sethu Madhavan**

**Name of Project Coordinator : Lakhan Murari**

Name of contractor : M/s PGCC Pvt,Ltd  
Agreement date : 18/09/2020  
Agreed Amount : ₹57.56 Cr  
Agreed Amount With GST : Rs. 64.46 crore  
Site Handover date : 26-09-2020  
Project duration : 18 months  
Scheduled Date of Completion :26-03-2022 (Extended to 09-01-2023)  
Expected Date of completion :31-05-2023

**Scheduled progress as on 08-08-2022 - 100%**

**Achieved progress as on 08-08-2022 - 37%**

**Progress upto last week -36%**

**Current week progress -0.01%**

**Current Bill Status : Fifth bill submitted**

**Current Financial Progress : 24.84%**

**Images of works done at Site during last week (with time stamp)**

**STATUS OF WORK IN TERMS OF**

**COMPONENTS**

- Regulator - foundation work (pile & open footing) completed. Girder 28/48 completed.
- Side Protection -  
1)D/S-R/S-completed..  
2)U/S-R/S- 486 m/600 m raft completed. 456m partially completed
- Deck Slab -7/12 completed
- Mechanical Works - Primary and secondary fabrication completed.Generator Cum Watchman Room - not started

**Work done in the last week**

- Deck slab between pier 6 and Pier 5 concreted.
- Civil works hindered due to river flowing full.



# PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA  
(KASE)**

# **UPGRADATION OF GOVT. ITI MALAMPUZHA ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer:NITHISH. C**

**Name of Project Coordinator : Lakhan Murari**



**Name of contractor** : M/S. PERFECTENGINEERS  
**Agreement date** : 05/03/2020  
**Agreed Amount** : Rs.11,61,93,745/-  
**Agreed Amount With GST** : Rs. 13,01,36,994.40/-  
**Site Handover date** :06/03/2020  
**Project duration** : 18 months  
**Scheduled Date of Completion.** : 05/09/2021  
**Expected Date of completion.** : 02/06/22

**Status of Work in terms of components**

- Smart classroom promethean and writing board fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

**Works done in the last week**

- Tile fixing at smart classroom at FF
- Electrical work
- External wall plastering
- AAC block work at FF
- Cable pulling
- Internal plastering at FF
- Tile fixing in toilet wall at FF

**Scheduled progress as on 12/08/2022- 100%**

**Achieved progress as on 12/08/2022 - 78%**

**Last week progress - 75%**

**Current week progress - 70%**

**Current Bill Status : no of bill submitted - 6,amount:4,21,29,262**

**Current Financial Progress : 36.26%**

**Images of works done at Site during last week (with time stamp)**



VADAKARAPALLY  
REGULATOR  
(KIIFB)

Construction of Regulator across Chittur  
Puzha at Vadakarapally Palathulli in  
Peruvembu Grama Panchayt in Palakkad  
District

**Name of Project Engineer:NITHIN J B**

**Name of Project Coordinator : Lakhan Murari**

**Name of contractor** : Poonam grah nirman Pvt ltd  
**Agreement date** : 04-01-2021  
**Agreed Amount** : ₹18.95 Cr  
**Agreed Amount With GST** : Rs. 21,23,18,001.2  
**Site Handover date** : 12-01-2021  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 12-07-2022  
**Expected Date of completion** : 12-07-2022

**Scheduled progress as on 12/08/2022 - 93%**

**Achieved progress as on 12/08/2022 - 80%**

**progress up to last week - 79%**

**Current week progress -2 %**

**Current Bill Status : Sixth and part bill credited**

**Current Financial Progress : 50.92%**

**Status of Work in terms of components:**

- Regulator - Primary concrete for all structure portion completed and secondary concreting in progress.
- Side Protection - U/S RHS and D/S LHS fully completed.
- U/S LHS raft concrete completed upto 102m and wall completed upto 70m.
- Mechanical Works -Fabrication of 11 shutters and painting of all completed.
- 9 Hoisting bridge spans completed

**Works done in the last week**

- Left Abutment one lift concrete.
- Fabrication of hoisting bridge mechanism.
- Secondary concrete on piers.
- Preparation of platform for erection of shutters.
- Heavy rain disrupted civil works as water level raised as Aliyar dam was opened.

**Images of works done at Site during last week**



**Moongilmada LIS  
(Civil)  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Moongilmada  
LIS in eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

**Name of Project Coordinator : Lakhan Murari**

Name of contractor : M/s Vallamattam constructions  
Agreement date : 18-09-2020  
Agreed Amount : ₹15422222 Crores  
Agreed Amount With GST : Rs. 18198221.96/-  
Site Handover date : 03-06-2021  
Project duration : 6 months  
Scheduled Date of Completion :03-12-2021  
Expected Date of completion :31-05-2022

**Status of Work in terms of components:**

- Pump House
- Conversion of abandoned RBC to water storage.
- Electrical Works

**Works done in the last week**

Electrical works ongoing

**Scheduled progress as on 12/08/2022 - 100%**

**Achieved progress as on 12/08/2022 - 87%**

**Last week progress in : 87%**

**Current week progress : 0%**

**Current Bill Status : Part Bill-2**

**Current Financial Progress : 53%**

**Images of works done at Site during last week (with time stamp)**



**Valiyeri LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at Valiyeri LIS in  
eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd  
Agreement date : 24-06-2021  
Agreed Amount : ₹31004000 Rupees  
Agreed Amount With GST : Rs. 36581180/-  
Site Handover date : 25-06-2021  
Project duration : 12 months  
Scheduled Date of Completion :25-06-2022  
Expected Date of completion :31-05-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

AUTOMATION WORKS

**Scheduled progress as on 13/08/2022 - 100%**

**Achieved progress as on 13/08/2022 - 95 %**

**Last week progress in : 95%**

**Current week progress : 0%**

**Current Bill Status : Part Bill-2**

**Current Financial Progress : 64%**

**Images of works done at Site during last week (with time stamp)**



**Navithankulam LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at  
Navithankulam LIS in  
eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**



**Name of contractor** : M/s Jain Irrigation Systems Pvt Ltd  
**Agreement date** : 24-06-2021  
**Agreed Amount** : ₹16327047.54 Rupees  
**Agreed Amount With GST** : Rs. 19265916.09/-  
**Site Handover date** : 25-06-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** :25-06-2022  
**Expected Date of completion** :31-06-2022

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

WAITING TO  
COMPLETE CIVIL  
WORKS

**Scheduled progress as on 13/08/2022 - 100%**

**Achieved progress as on 13/08/2022 - 75 %**

**Last week progress in : 75%**

**Current week progress : 0%**

**Current Bill Status : Nil**

**Current Financial Progress : first bill**

**Images of works done at Site during last week (with time stamp)**



**Kunnamkatupathy  
LIS  
WRD-RKI**

**KIIDC-Providing Community  
micro irrigation at  
Kunnamkatupathy LIS in  
eruthenpathy Panchayath  
palakkad district**

**Name of Project Engineer: Amal Padmu LP**

Name of contractor : M/s Mahendra Pvt Ltd  
Agreement date : 18-11-2021  
Agreed Amount : ₹36068276 Rupees  
Agreed Amount With GST : Rs. 42560565.68/-  
Site Handover date : 27-11-2021  
Project duration : 6 months  
Scheduled Date of Completion :29-05-2022  
Expected Date of completion :31-06-2022

Scheduled progress as on 13/08/2022 - 100%

Achieved progress as on 13/08/2022 - 66 %

Last week progress in : 65%

Current week progress : 1%

Current Bill Status : Partbill-2

Current Financial Progress : 34%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

**Works done in the last week**

submain and mainline work



**MOOLATHARA  
RIGHT BANK CANAL  
PHASE 1 FROM  
KORAYAR TO  
VARATTAYAR  
(KIIFB)**

**KIIFB-Extension of Moolathara  
right bank canal phase 1 from  
korayar to varattayar**

**Name of Project Engineer: NITHISH.C**

**Name of contractor** : M/s Prathmesh & K.K.Constructions  
**Agreement date** : 23-12-2021  
**Estimate P.A.C** : Rs.158,50,00,000/-  
**CONTRACT P.A.C** : Rs. 174,34,95000/-  
**Site Handover date** : 31-12-2021  
**Project duration** : 30 months  
**Scheduled Date of Completion** :  
**Expected Date of completion** :

**Status of Work in terms of components:**

- Site clearance

**Works done in the last week**

- .Tree cutting
- .Tree numbering
- .Design works

**Scheduled progress as on 13/08/2022 - Nil**

**Achieved progress as on 13/08/2022- Nil**

**Last week progress in : Nil**

**Current week progress : Nil**

**Current Bill Status : Nil**

**Current Financial Progress : Nil**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN THRISSUR DISTRICT

**REGULATOR CUM  
BRIDGE ACROSS  
KURUMALI PUZHA  
IN THRISSUR  
DISTRICT.**

**CONSTRUCTION OF  
KANATHODU REGULATOR CUM  
BRIDGE ACROSS KURUMALI  
PUZHA AT KUNDUKADAVU IN  
PUDUKAD PANCHAYATH,  
THRISSUR DISTRICT.**

**Name of Project Engineer: RAHUL V R**

**Name of Project Coordinator : Pushparaj**

Name of contractor : PGCC  
Agreement date :05-01-2022  
Agreed Amount : 262383481.27  
Agreed Amount With GST : Rs.293869499.022  
Site Handover date : 13-01-2022  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2023  
Expected Date of completion : 13-07-2023

**Status of Work in terms of components:**

- Regulator -3.75%
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

**Works done in the last week**

- Revised GFC drawings was issued on 02-04-2022
- River boundary survey was completed on 18-02-2022
- Initial levels also been taken
- **Work delayed since 27/06/2022 due to heavy rain and rise in water level in the River**
- **Ring bund dismantled due to Rise in water level**

**Scheduled progress as on 13-08-2022 - 19%**

**Achiever progress as on 13-08-2022 - 3.75%**

**Progress up to last week- 3.75%**

**Current week progress -0%**

**Current Bill Status : NIL**

**Current Financial Progress : 0%**

**Images of works done at Site during last week (with time stamp)**





**ITI CHALAKUDY  
KIIFB-KASE**

# **UP GRADATION OF GOVT ITI CHALAKUDY ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: RAHUL V R**

Name of contractor : Sidheek, M/S Sitco Associates  
Agreement date : 28-10-2020  
Agreed Amount : ₹ 7,47,51,405.13  
Agreed Amount With GST : ₹ 8,37,21,573.74  
Site Handover date : 06-11-2020  
Project duration : 12 months  
Scheduled Date of Completion : 05-11-2021  
Expected Date of Completion :

Scheduled progress as on 13/08/2022- 0 %

Achieved progress as on 13/08/2022 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

### Works done in the last week

- As per drawings building setbacks are not available at the site. The proposed building and setbacks drawings are need to be redesigned according to existing boundary condition
- Decision were taken for redesign



# PROJECTS IN ERNAKULAM DISTRICT

**CHELLANAM  
COASTAL  
PROTECTION  
[KIIFB]**

**KIIFB PROJECT- REFORMATION OF DAMAGED  
SUNKEN SEA WALL AT CHELLANAM USING  
TETRAPODS AND RUBBLE IN BETWEEN CP  
STONE 976 AND 1052 FOR 10 KM STRETCHES  
ALONG CHELLANAM COAST IN ERNAKULAM  
DISTRICT - PHASE I FOR A LENGTH OF 7/350  
KM IN BETWEEN CP 986 AND CP 1026**

**Name of Project Engineer : SREELAKSHMI S  
Name of Project Coordinator : Mahadevan**

Name of contractor : M/s Uralungal Labour Contract Co-operative

Agreement date : 30-12-2021

Agreed Amount : ₹ 256,89,67,441.29

Agreed Amount With GST : ₹ 287,72,43,534.25

Site Handover date : 03-01-2022

Project duration : 16 months

Scheduled Date of Completion : 02-05-2023

Expected Date of Completion : 02-05-2023

Scheduled progress as on 14/08/2022- 46.07%

Achieved progress as on 14/08/2022 - 43.77%

Last week progress - 1.27%

Current week progress- 1.47%

Current Bill Status : C.C 2nd and Part Bill submitted Amount: 37.46Cr & C.C 1st and Part Bill passed Amount: 65.95Cr. Total Bill Amount = 103.42Cr

Current Financial Progress : 34.12%

Images of works done at Site during last week

### Status of Work :

- 30004nos of 2T tetrapods cast.
- 24774nos of 3.5T tetrapods cast.
- Available mould 2T = 149 nos
- Available mould 3.5T = 163 nos

### Total Boulders Supplied till 11.08.2022

- Core layer (10-50kg) = 91130.893 T
- Toe (200 to 400kg) = 41131.113 T
- Underlayer (150-200kg) = 54541.427 T
- Toe ( 250-350kg) = 100703.589 T
- Toe (350-700kg) = 49741.156 T
- Primary layer(500-800kg)= 25423.48 T

### Works done in the last week

- 12101nos 2T and 9649nos 3.5T tetrapods are placed.
- Supplying and laying of boulders in progress at SR-1,2,3,4,6 Harbour, SR-9,10,11,12,13, 14 Abad Area.



**RCB  
KONOTHUPUZHA  
(KIIFB)**

**Construction of Regulator with  
lock across Konothupuzha at  
Puthenkavu in Udayamperoor  
Panchayath in Ernakulam  
District**

**Name of Project Engineer: Remya P R  
Name of Project Coordinator : Bibin Giri**

Name of contractor : Marymatha construction  
Agreement date : 04-01-2021  
Agreed Amount : ₹24.36 Cr  
Agreed Amount With GST : Rs. 272,843,729.92  
Site Handover date : 14-01-2021  
Project duration : 18 months  
Scheduled Date of Completion : 13-07-2022  
Expected Date of completion : 15-04-2023

Scheduled progress as on 13-08-2022 - 45%

Achieved progress as on 13-08-2022- 25.5%

Progress upto last week- 25.5%

Current week progress - 0%

Current Bill Status :cc 3rd & part bill under preparation & will be submitted soon

Current Financial Progress :20 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Regulator - 10%
- Lock Portion - 15.5%
- Side Protection -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

**Works done in the last week**

Piling works -  
Lock portin- 56 piles,  
Pier 1 , Pier 2 & Pier 3- 12nos piles completed.  
Left abutment- 4 no.s completed.  
Total -72 piles completed(Piling works completed).

**\*Ring bund demolished due to monsoon rain & flood. And river flows over the ring bund .It affects the progress of the work**



**ANTHAKARATHO  
DU CANAL  
(KIIFB)**

# **IMPROVEMENTS TO ANTHAKARATHODE IN THRIPPUNITHURA MUNICIPALITY**

**Name of Project Engineer: Princy Abraham**

**Name of Project Coordinator : Bibin Giri**



Name of contractor : Southern Tech  
Agreement date : 29-09-2018  
Agreed Amount : ₹8.35 Cr  
Agreed Amount With GST : Rs. 12,52,34,417.4  
Site Handover date : 08-10-2018  
Project duration : 15 months  
Scheduled Date of Completion : 07-01-2021  
Expected Date of completion : 31-10-2022

**Status of Work in terms of components:**

- Cleaning & desilting-completed
- Side protection work- 85%
- Road and walkway formation- 80%
- Fencing and Handrail work- 70%
- Boat jetty -100%
- Skew bridge -100%
- Foot bridge-100%

**Works done in the last week**

- Presently, no work due to heavy rain

**Scheduled progress as on 13-08-2022 - 98.5%**

**Achieved progress as on 13-08-2022 - 96%**

**Last week progress - 0%**

**Current week progress 0%**

**Current Bill Status : 4th bill approved**

**Current Financial Progress : 80%**

**Images of works done at Site during last week (with time stamp)**



**ELECTRICAL  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY–PROVIDING STREET  
LIGHTS ALONG THE PATHWAYS OF  
ANTHAKARATHODE**

**Name of Project Engineer: Princy Abraham**

**Name of Project Coordinator : Vishnu**

Name of contractor : Essjay Electro links  
Agreement date : 31-12-2020  
Agreed Amount : ₹50.27 lakhs  
Agreed Amount With GST : Rs. 5630313.00  
Site Handover date : 10-01-2021  
Project duration : 5 months  
Scheduled Date of Completion : 30-05-2021  
Expected Date of completion : 15-11-2022

**Status of Work in terms of components:**

- Excavation and supply Laying of cable-90%
- Placing of lamp post, LED & feeder -80%
- Excavation and concreting-85%

**Works done in the last week**

- Presently, work is delayed due to heavy rain
- Pole fixing at Konothupuzha side started.
- The remaining work depends on civil work (pathway).

**Scheduled progress as on 13-08-2022- 100%**

**Achieved progress as on 13-08-2022- 93.1%**

**Last week progress - 0%**

**Current week progress 0%**

**Current Bill Status : Part Bill prepared**

**Current Financial Progress : 82%**

**Images of works done at Site during last week (with time stamp)**



**BEAUTIFICATION  
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO  
ANTHAKARATHODE IN  
THRIPPUNITHURA  
MUNICIPALITY–LANDSCAPING &  
ARBORICULTURE, CONSTRUCTION OF  
KIOSK AND TOILET AND OPERATION &  
MAINTENANCE FOR ONE YEAR**

**Name of Project Engineer: Princy Abraham**

**Name of Project Coordinator : Bibin Giri**

**Name of contractor** : GRIDS,Digital Surveyors and  
Engineering Consultants  
**Agreement date** : 24-06-2021  
**Agreed Amount** : ₹76.62 lakhs  
**Agreed Amount With GST** : Rs. 8581690.00  
**Site Handover date** : 03-07-2021  
**Project duration** : 3 months  
**Scheduled Date of Completion** : 02-10-2021  
**Expected Date of completion** : 02-01-2022

**Status of Work in terms of components:**

- Landscaping & tress-6%
- Construction of Kiosk & Toilet-0%
- Providing signage boards-0%

**Works done in the last week**

Presently, no work due to heavy rain.

The remaining work depends on civil work (pathway).

**Scheduled progress as on 13-08-2022- 40%**

**Achieved progress as on 13-08-2022- 6%**

**Last week progress - 0%**

**Current week progress - 0%**

**Current Bill Status : NIL**

**Current Financial Progress : 0 %**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN IDUKKI DISTRICT

**ITI  
KATTAPPANA  
(KASE)**

# **UP GRADATION OF GOVT ITI KATTAPPANA ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: DON BABY  
Name of Project Coordinator : Bibin Giri**

**Name of contractor** : Anchanical constructions  
**Agreement date** : 16.10.2020  
**Agreed Amount** : Rs 4,76,87,560.83  
**Agreed Amount With GST** : Rs 5,34,10,068.1  
**Site Handover date** : 04-12-2019  
**Project duration** : 08 months  
**Scheduled Date of Completion** : 31-08-2022  
**Expected Date of completion** : 15- 10-2022

### Status of Work in terms of components:

- Brickwork-70%.
- plastering works-58%
- Electrical works-22.2%
- Grade beam concrete-100%
- Grade slab Concrete - 100%
- Roof beams and slab - 100%

### Works done in the last week

- Brick works
- Electrical works
- Plastering works
- Water proofing works

**Scheduled progress as on 13.08.2022- 90%**

**Achieved progress as on 13.08.2022 - 60.3%**

**Last week progress : 60.2%**

**Current week progress :0.1%**

**Current Bill Status : 4th and part bill**

**Current Financial Progress :48 %**

### Images of works done at Site during last week





**ECO-LODGE  
IDUKKI  
ADDITIONAL  
WORKS – III  
(TOURISM)**

**ADDITIONAL WORK III OF ECO LODGE  
CONSTRUCTION AT IDUKKI  
(CONSTRUCTION OF MODULAR  
KITCHEN,DRAINAGE,PARKING  
YARD,SIDE WALL,WOOD WORK  
POLISHING,ELECTRICAL WORKS &  
GENERATOR ROOM).**

**Name of Project Engineer:DON BABY**

**Name of Project Coordinator : Bibin Giri**

Name of contractor : M/S VJ Raju and Co.  
Agreement date : 21.10.2021  
Agreed Amount : Rs.71,96,599.18  
Agreed Amount With GST : Rs. 80,60,191.08  
Site Handover date : 31-10-2021  
Project duration : 03 months  
Scheduled Date of Completion : 31-03-2022  
Expected Date of completion : 14-05-2022

**Status of Work in terms of components:**

- Modular kitchen-100%
- Wood work polishing - 100%
- Electrical works - 100%
- Generator room-100%
- Drainage-100%
- Parking yard-100%
- Handrail- 100%

**Works done in the last week**

- Jungle clearance

**Scheduled progress as on 13.08.2022- 100%**

**Achieved progress as on 13.08.2022 - 100%**

**Last week progress : 94%**

**Current week progress : 6%**

**Current Bill Status : 1st & Part Bill : ₹49,46,902.00 (incl.GST) submitted to Tourism Department on 14.03.2022**

**Current Financial Progress : 58.25%**

**Images of works done at Site during last week**



PEERMADE  
GUEST HOUSE  
RENOVATION  
(TOURISM)

**UPGRADATION AND RENOVATION OF  
GOVT. GUEST HOUSE PEERMADE ,  
IDUKKI**

**Name of Project Engineer: TEENU AUGUSTINE**

**Name of Project Coordinator : Sarath S R**

**Name of contractor** :SRI BIBY SCARIA  
**Agreement date** : 30-06-2020  
**Agreed Amount** : Rs.1,45,51,908.00  
**Agreed Amount With GST** : Rs. 1,71,71,251.44  
**Site Handover date** : 13-07-2020  
**Project duration** : 9 months  
**Scheduled Date of Completion** :13-04-2021  
**Expected Date of completion** : 31-10-2022

**Scheduled progress as on 13-08-2022- 100 %**

**Achieved progress as on 13-08-2022 - 62 %**

**Last week progress -60.4 %**

**Current week progress - 0.6%**

**Current Bill Status** : 2nd & Part Bill : ₹45,26,416.00 (incl. GST) submitted to Tourism Department on 18.06.2022

**Current Financial Progress** : 40.19%

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Guest house renovation - 15%
- Service block renovation - 95%
- Water tank - 85%
- Parking shed - 35%
- Conference hall - 80%

**Works done in the last week**

- Plumbing works,painting works of annex building on progress
- Tile works of annex building completed



PANCHALIMEDU  
(TOURISM)

**PANCHALIMEDU TOURISM PROJECT  
PHASE – 2  
PERUVANTHANAM VILLAGE,  
PEERMEDU TALUK, IDUKKI DISTRICT**

**Name of Project Engineer: TEENU AUGUSTINE  
Name of Project Coordinator : Sarath S R**

Name of contractor : EASYINFRA INC, TVM  
Agreement date : 22/12/2020  
Agreed Amount : ₹2,43,99,440.78  
Agreed Amount With GST : Rs. 2,73,27,373.67  
Site Handover date : 01-01-2021  
Project duration : 12 months  
Scheduled Date of Completion : 31-12-2021  
Expected Date of completion : 31-12-2022

**Status of Work in terms of components:**

- Renovation of panchalikulam - 50%
- Construction of pathway - 50%
- Proposed check dam - 25%
- Proposed lighting system - 0%
- Sitting benches - 0%
- Landscaping - 0%
- Rope cycling - 0%

**Works done in the last week**

- Work stopped due to heavy rain

**Scheduled progress as on 13-08-2022 - 50 %**

**Achieved progress as on 13-08-2022 - 18 %**

**Last week progress - 18 %**

**Current week progress - 0 %**

**Current Bill Status : 1st & Part Bill ₹16,68,292 (incl. GST)**

**Current Financial Progress : 6.10%**

**Images of works done at Site during last week (with time stamp)**



PEERMADE  
(TOURISM)

**ADDITIONAL WORK AT ECOLODGE  
CONSTRUCTED AT PEERMADE  
(CONSTRUCTION OF PARKING YARD,  
COMPOUND FENCING, SERVICE  
BLOCK, AMBIENT LIGHTING AND  
MODULAR KITCHEN AT ECOLODGE  
PEERMADE)**

**Name of Project Engineer: TEENU AUGUSTINE**

**Name of Project Coordinator : Sarath S R**

**Name of contractor** : Outlook communications pvt.ltd.  
**Agreement date** : 08-10-2021  
**Agreed Amount** : ₹80,27,681.98  
**Agreed Amount With GST** : Rs.9472664.74  
**Site Handover date** : 11-10-2021  
**Project duration** : 12 months  
**Scheduled Date of Completion** : 10-10-2022  
**Expected Date of completion** : 10-10-2022

**Scheduled progress as on 13-08-2022 - 48 %**

**Achieved progress as on 13-08-2022 - 48 %**

**Last week progress - 48 %**

**Current week progress - 0 %**

**Current Bill Status** : 1st & Part Bill : ₹27,37,936.00 (incl. GST) submitted to Tourism Department on 06.04.2022

**Current Financial Progress** : 28.90%

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Fencing - 0%
- Service block - 85%
- Security cabin - 85%
- Diesel generator - 70%
- Modular kitchen - 90%
- Generator room - 50%
- Electrical works -0%
- Civil work for lamp post - 0%

**Works done in the last week**

- **No work done on last week**





# PROJECTS IN KOTTAYAM DISTRICT

**ITI  
ETTUMANOOR  
(KASE)**

# **UP GRADATION OF GOVT ITI ETTUMANOOR ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: Anjaly C R**

**Name of Project Coordinator : Sarath S R**

Name of contractor : Swathy Construction

Agreement date : 30-07-2020

Agreed Amount : ₹ 6,95,25,557.81

Agreed Amount With GST : ₹ 7,78,68,624.74

Site Handover date : 10-08-2020

Project duration : 12 months

Scheduled Date of Completion : 09-08-2021

Expected Date of Completion : with in. 05.11.2022

Scheduled progress as on 13-08-2022- 98 %

Achieved progress as on 13-08-2022 - 89 % ( As per revised Estimate)

~~Last week progress - 89%~~

Current week progress - 0%

Current Bill Status : CC 8<sup>th</sup> and part bill submitted for scrutiny and pass.  
Amount:Rs. 43,52,039.910

Current Financial Progress : 82%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Main building civil works (99%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (100%)
- Road and ancillary works, compound wall (100%)
- Land development (90%)
- External water supply, sewerage system (100%)
- Rain water drainage (98%)
- Main building electrical works,ELV ,HVAC (75%)
- Fire protection works (99%)
- Furniture for main building and renovated smart class rooms (100%)

**Works were done in the last week - Main building civil works**

- Entrance grill door work started.



**CLEARING WATER  
HYACINTH  
(TOURISM)**

**CLEARING WATER HYACINTH  
AND PLASTIC WASTE MATERIAL  
FROM VEMBANAD LAKE AT  
NALUPANK HOUSE BOAT  
TERMINAL**

**Name of Project Engineer: Anjaly C R**

**Name of Project Coordinator : Gopakumar**

Name of contractor : T.B.A.S Construction  
Agreement date : 01/04/2022  
Estimated Amount : ₹ 6,56,662.00  
Agreed Amount : ₹ 7,18,966.00  
Site Handover date : 11/04/2022  
Project duration : 03 months  
Scheduled Date of Completion : 11/07/2022  
Expected Date of Completion : 11/07/2022

**Status of Work in terms of components:**

- Clearing of water hyacinth and waste material

**Cause of work delay/Issues at the site.**

- Removed hyacinth and plastic waste materials are replenishing continuously.
- Work will resume next week onwards with providing a barricade to restrict the hyacinth.

**Works were done in the last week**

- Removing of hyacinth near boat terminal

Scheduled progress as on 13-08-2022- 100%

Achieved progress as on 13-08-2022 - 100 %

Last week progress - 100 %

Current week progress - 0%

Current Bill Status : NIL

Current Financial Progress : First and Final bill under preparation

Images of works done at Site during last week (with time stamp)



**SIHM PALA  
(TOURISM)**

**SETTING UP OF STATE INSTITUTE  
OF HOTEL MANAGEMENT  
STUDIES AT PALA, KOTTAYAM  
DISTRICT, CONSTRUCTION OF  
ACADEMIC BLOCK**

**Name of Project Engineer: DON BABY**

**Name of Project Coordinator : Gopakumar**

Name of contractor : SITCO Associates  
Agreement date : 01-03-2016  
Agreed Amount : ₹13.48 Cr  
Site Handover date : 10-03-2016  
Project duration : 18 months  
Scheduled Date of Completion : 31/10/2017  
Expected Date of completion : 31/12/2021

Scheduled progress as on 13-08-2022 - 90%

Achieved progress as on 13-08-2022 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : Total bill amount (1st & Part Bill to 13th & Part Bill) ₹ 11,35,31,433.00

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

**Works were done in the last week**

- No works have been done.
- AS revalidation in process (Department of Tourism)
- Materials for the brickworks are yet to be procure at site.
- Excavation works are delayed due to heavy rain.



# PROJECTS IN ALAPPUZHA DISTRICT



**ITI  
CHENGANNUR  
(KASE)**

**UP-GRADATION OF GOVT ITI  
CHENGANNUR ON PAR WITH  
INTERNATIONAL  
STANDARDS - PHASE 1- REV 3**

**Name of Project Engineer: LEKSHMY GOPAN  
Name of Project Coordinator : Omanakuttan**

Name of contractor : Creators Construction

Agreement date : 15/10/2020

Agreed Amount : Rs 18 Cr

Agreed Amount With GST : Rs20,64,45672/-

Site Handover date : 31/10/2021

Project duration :18 months

Scheduled Date of Completion : 29/04/2023

Expected Date of completion :30/04/2023

Scheduled progress as on 13/08/2022 : 38%

Achieved progress as on 13/08/2022 : 28%

Last week progress in : 2%

Current week progress in: 2%

Current Bill Status : cc st and part bill passed. Amount: 1.37Cr

Current Financial Progress : 8%

Images of works done at Site during last week (with time stamp)

### **Status of Work in terms of components:**

- Main building civil works (9%)
- Existing class room converted to smart classrooms (0%)
- Sump tank , substation works (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (0%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room Converted to smart classrooms (0%)

### **Works done in the last week :**

- . Reinforcement works
- . Roof slab shuttering
- . Main building roof slab concrete
- . Hostel building column concrete



**ALAPPUZHA  
CANALS  
PHASE.01  
(KIIFB)**

# **MODERNIZING WATER TRANSPORT IN ALAPPUZHA CANALS-PHASE 01**

**Name of Project Engineer: Stephy Sebastian  
Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 15-02-2019  
Agreed Amount : ₹48.35 Cr  
Agreed Amount With GST : Rs. 54,15,71,596.79  
Site Handover date : 19-02-2019  
Project duration : 12 months  
Scheduled Date of Completion : 18-02-2020  
Expected Date of completion : 30-08-2022

**Status of Work in terms of components:**

- All agreed works has been completed
- The repair of sunken road(near Pagoda resorts) is under progress.
- Construction of damaged road using interlock paver tiles in progress

**Works done in the last week**

- Laying of GSB for road in progress.
- WMM - final level achieved. interlock works will be progressed soon.
- Interlock work is completed
- some finishing work only pending

**Scheduled progress as on 13-08-2022 - 100%**

**Achieved progress as on 13-08-2022 - 99.5%**

**Last week progress in 99%**

**Current week progress- .5%**

**Current Bill Status : Rs.47,65,31,121 upto 6th bill (Balance -5,56,02,88,367)**

**Current Financial Progress :90%**

**Images of works done at Site during last week (with time stamp)**



**PUNNAMADA  
(TOURISM WORK )**

# **Punnamada- Starting Point Pathway and Boat Landing at Alappuzha District.**

**Name of Project Engineer: Stephy Sebastian  
Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 1.11 Cr  
Agreed Amount With GST : Rs. 1,23,77,355.31  
Site Handover date : 05-05-2021  
Project duration : 6 months  
Scheduled Date of Completion : 30-08-2022  
Expected Date of completion : 30-07-2022

**Status of Work in terms of components:**

- Pathway  
Solar Lighting

**Works done in the last week**

- Laying GSB
- Laying paver blocks
- Landscaping works
- Erection of solar LightLights
- Truss work for waiting sheds

**Scheduled progress as on 13-08-2022- 98%**

**Achieved progress as on 13-08-2022- 90%**

**Last week progress - 80%**

**Current week progress - 10%**

**Current Bill Status :** 1st & Part Bill ₹50,02,073.00 (incl. GST) and 2nd & Part Bill ₹57,94,300.00 (incl. GST) submitted to Tourism on 26.03.2022 and 24.06.2022 respectively.

**Current Financial Progress : 82.79%**

**Images of works done at Site during last week (with time stamp)**



**CHUNGAM  
(TOURISM WORK )**

**CHUNGAM(CHAKREPURAKKAL)-  
KAYALCHIRA PATHWAY  
DEVELOPMENT AND BOAT  
LANDING BY THE SIDE OF  
PUNNAMADA RIVER, At  
ALAPPUZHA DISTRICT**

**Name of Project Engineer: Stephy Sebastian**

**Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 26-02-2021  
Agreed Amount : ₹ 2.99 Cr  
Agreed Amount With GST : Rs. 3,34,07,087.37  
Site Handover date : 05-05-2021  
Project duration : 9 months  
Scheduled Date of Completion : 04-02-2022  
Expected Date of completion : 24-09-2022

**Status of Work in terms of components:**

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

**Works done in the last week**

- Backfilling of earth and Construction of Rubble masonry Retaining wall for Pathway and Boat landing
- Backfilling behind Pile and slab retaining wall
- Anchor belt and beam- 69 completed. 30 to be completed.
- Filling of pavement completed using earth
- final levels of the earth filling have been taken in accompany with initial level of GSB

**Scheduled progress as on 13-08-2022- 100%**

**Achieved progress as on 13-08-2022 - 76%**

**Last week progress - 70%**

**Current week progress - 6%**

**Current Bill Status :** 1st & Part Bill ₹91,65,612.00 (incl. GST) and 2nd & Part Bill ₹1,29,06,381.00 (incl. GST) submitted to Tourism on 07.03.2022 and 21.06.2022 respectively.

**Current Financial Progress : 62.71%**

**Images of works done at Site during last week (with time stamp)**





**PUNNAMADA  
(TOURISM WORK )**

**RENOVATION OF PUNNAMADA PARKING  
AREA AND PREMISES AT ALAPPUZHA  
DISTRICT**

**Name of Project Engineer: Stephy Sebastian**

Name of contractor : TBAS Construction, Aluva  
Agreement date : 11/01/2022  
Agreed Amount : Rs 87,81,166.60  
Agreed Amount With GST : Rs 98,34,906.59  
Site Handover date : 21/01/2022  
Project duration : 12 months  
Scheduled Date of Completion : 20/01/2023  
Expected Date of completion : 20/12/2022

Scheduled progress as on : 13-08-2022-

Achieved progress as on : 13-08-2022- 17 %

Last week progress - 15%

Current week progress - 2%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**Status of Work in terms of components:**

- Parking Area
- Landscaping
- Plumbing

**Works done in the last week**

- Clearing the site
- Removing the interlock
- Initial Level of earth levelling completed
- Quarry muck is ready for filling the ground
- The bund formation for the regulator have been started



**GROYNES AT  
AMBALAPUZHA  
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСCP  
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at  
Ambalapuzha South, North panchayath and  
Punnapra South Panchayath**

**Name of Project Engineer: SILPA R**

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 51.3 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 29-01-2022 as per EOT  
**Expected Date of completion** : 15-02-2023

**Status of Work in terms of components:**

- 20m groynes – 5 nos- 2completed
- 30M GROYNES -7nos- 2 in progress, 3completed.
- 40M GROYNES – 9 nos -5completed.
- 50M GROYNES – 9 nos -6completed.
- Sea wall length-305 m – not started
- 172805.452 MT boulders reached out of 178922 MT (100%)
- 2T TETRAPODS –23151nos. casted out of 23902 nos. (96.86%)
- 5T TETRAPODS – 2955 nos. casted out of 2956 nos.(99.9%)
- Earthwork Excavation – 23131.66 m3 completed out of 45955.7 M3 (43%)

**Works done in the last week**

The total no.of tetrapods casted 2T-0& 5T-0nos

- Supplying and Laying of Boulders -0 MT
- Laying of tetrapods in G19, G13completed.
- 2361 Nos 5T tetrapods layed
- 12541 Nos 2T layed.
- **no work can be done without RE sanction due to the design changes and change of various items.**

**Scheduled progress as on 13-08-2022 – 100 %**

**Achieved progress as on 13-08-2022 - 79 %**

**Last week progress - 0%**

**Current week progress -0%**

**Current Bill Status** : 7 th bill submitted for an Amt of Rs.48492386.46  
Total bill amount - Rs. 450663433.14

**Current Financial Progress : 87.84%**

**Images of works done at Site during last week (with time stamp)**



**GROYNES AT  
ARATTUPUZHA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
21NOS GROYNES AT  
ARATTUPUZHA IN BET.CH.56.6  
TO 57.8 KM AT ARATTUPUZHA**

**Name of Project Engineer: M A FASEELA NASAR**

**Name of contractor** : Ramalingam construction Company Pvt. Ltd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹ 26. 23Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** :15-06-2022 as per EOT  
**Expected Date of completion** :15-02-2023

**Scheduled progress as on 13-08-2022- 100 %**

**Achieved progress as on 13-08-2022-40 %**

**Last week progress - 1 %**

**Current week progress - 2 %**

**Current Bill Status: 6 part bill submitted for an amount of Rs 18,29,20,633/-**

**Current Financial Progress : 70 %**

**Images of works done at Site during last week (with time stamp)**


**Status of Work in terms of components:**

- 20M GROYNES - 6 NOS- 2 started
- 25M GROYNES - 15 NOS- 2 cmplt, 14 started
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 60300.74 T (64% ) 94497 MT
- 2T TETRAPODS - 10075 ( 100% ) nos casted out of 9874 NOS
- 5T TETRAPODS - 2245 (94.13% ) nos casted out of 2385 NOS
- GEOMAT - 64739 M2 ( not done )
- EARTHWORK EXCAVATION - 3290 M3(not done)

**Works done in the last week**

The total no.of tetrapods casted 2T-0& 5T-0nos

- Supplying and Laying of Boulders - 2608.16 T.
- 333 5T tetrapod layed
- 986 2T tetrapod layed
- **no work can be done without RE sanction due to the design changes and change of various items**

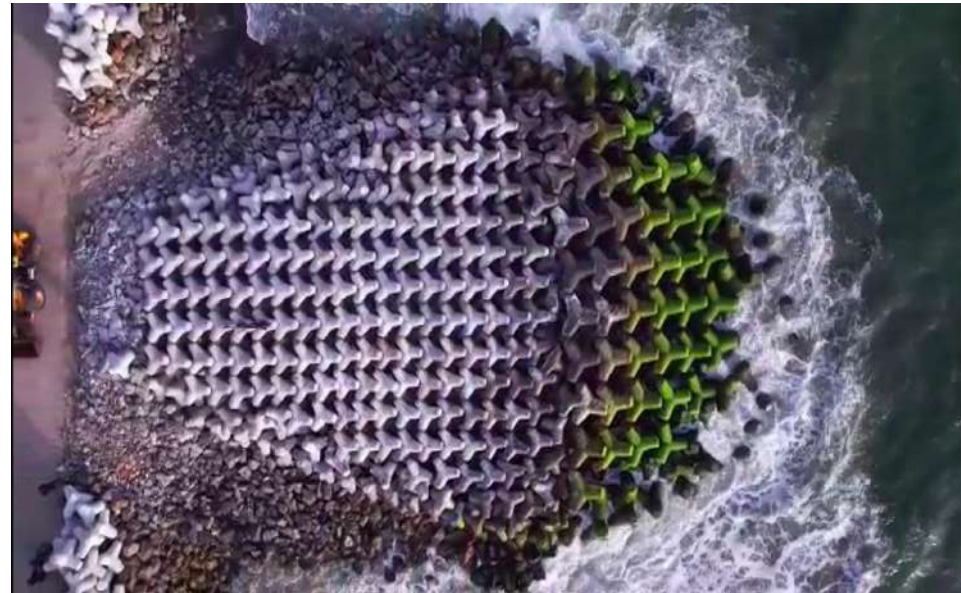

**GROYNE SITE  
AT  
PATHIYANKARA  
(KIIFB)**

**KIIFB  
PROJECT-CONSTRUCTION OF  
13NOS GROUYNE AT  
PATHIYANKARA IN BET.CH.60.1  
TO 61.6KM AT  
THRIKKUNNAPUZHA.**

**Name of Project Engineer: SILPA R**

**Name of Project Coordinator : RAJASEKHARAN PILLAI**

**Name of contractor** : Ramalingam construction Company Pvt. Lmtd.  
**Agreement date** : 22.07.2020  
**Agreed Amount** : ₹20.08Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 15-06-2022 as per EOT  
**Expected Date of completion** : 15-02-2023

**Status of Work in terms of components:**

- 1 20M GROYNES - 2 NOS-One is completed
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- 3completed and 2nos is in progress
- 4.61876.225MT boulders reached out of 74546 MT(83%)
5. 2T TETRAPODS -8930casted out of 8930NOS(100%)
6. 5T TETRAPODS - 1190nos casted out of 1199NOS(99%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

**Works done in the last week -**

The total no.of tetrapods casted 2T-0& 5T-0nos

- . Groynes G1,G2 ,G3 & G5;G6 are completed.
- . Supplying and laying of boulders-0T
- . 772 5T tetrapod layed
- . 4160 2T tetrapod layed
- . **no work can be done without RE sanction due to the design changes and change of various items.**

**Scheduled progress as on 13-08-2022 - 100%**

**Achieved progress as on 13-08-2022 -63 %**

**Last week progress in -0%**

**Current week progress in 0%**

**Current Bill Status** :7th part bill submitted for an Amt of Rs. 12811052.37  
Total bill amount - Rs. 170854619.44

**Current Financial Progress in :85%**

**Images of works done at Site during last week (with time stamp)**





**GROYNE SITE  
AT.  
VATTACHAL  
(KIIFB)**

**KIIFB  
PROJECT – CONSTRUCTION OF  
16 NOS GROUYNE AT  
VATTACHAL IN BET. CH.53.4 TO  
CH.55.2 KM(1.8KM)  
AT ARATTUPUZHA GP**

**Name of Project Engineer: M A FASEELA NASAR  
Name of Project Coordinator : RAJASEKHARAN PILLAI**

Name of contractor : Ramalingam construction Company Pvt. Ltd.  
Agreement date : 22.07.2020  
Agreed Amount : ₹28. 83Cr  
Agreed Amount With GST : Rs.  
Site Handover date : 30-07-2020  
Project duration : 18 months  
Scheduled Date of Completion :15-06-2022 as per EOT  
Expected Date of completion :15-02-2023

Scheduled progress as on 13-08-2022 - 100 %

Achieved progress as on 13-08-2022 - 75 %

Last week progress - 0 %

Current week progress - 0%

Current Status : 8 part bills submitted for an amt of Rs 23,13,12,922/-

Current Financial Progress in % : 80%

Images of works done at Site during last week (with time stamp)

### Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 cmpltd
- 30M GROYNES - 10 NOS- 7 cmpltd 1 pending due local issue, 1 ongoing
- 40M T GROYNE - 4 Nos -1 ongoing
- TOTAL QUANTITY OF BOULDERS - 76096.554 MT (75%) reached out of 101487 MT
- 2T TETRAPODS - 8941( 100 %) nos casted out of 8941 NOS
- 5T TETRAPODS - 3432 (100 %) nos casted out of 3432 NOS
- GEOMAT - 4850 m2 (6 %) layed out of 76299 M2
- EARTHWORK EXCAVATION - (8191.37 m3 out of 62380 M3)

### Works done in the last week

- 2T tetrapod casted - 0 nos.
- 5T tetrapod casted - 0 nos.
- Supplying and Laying of Boulders - nil
- Groyne G2, G3, G6, G7, G8, G9, G11, G15, G16 completed.
- 1881 5T tetrapods layed
- 5458 2T layed.
- **no work can be done without RE sanction due to the design changes and change of various items.**



**GROYNES SITE AT  
KATTOOR  
(KIIFB)**

**Construction of 34 nos. Groyne  
at Kattoor from Ch.168.465KM  
TO CH 171.627KM (Old CH  
96.643KM TO CH 9.535 KM)**

**Name of Project Engineer: SILPA R**

**Name of Project Coordinator : Mahadevan P**

**Name of contractor** : Ramalingam Construction Company Pvt Ltd.  
**Agreement date** : 22-07-2020  
**Agreed Amount** : ₹ 49.04 Cr  
**Agreed Amount With GST** : Rs.  
**Site Handover date** : 30-07-2020  
**Project duration** : 18 months  
**Scheduled Date of Completion** : 15-06-2022 as per EoT  
**Expected Date of completion** : 15-10-2022

**Status of Work in terms of components:**

- 20m groyne - 3 started out of 3
- 30m Groyne-5nos started out of 7
- 40m groyne - 19 nos started out of 24
- Total boulders quantity - 174010.85 MT boulders reached out of 174010 MT (100%)
- 2T TETRAPODS – 21553 nos (99.95%) casted out of 21562 nos.
- 5T TETRAPODS – 3144 (100%) nos. casted out of 3144 nos.
- Geomat - 14015.5m2
- Earthwork Excavation - 31767.090m3 out of 42122 M3

**Works done in the last week**

- 2T & 5T casting are completed
- Supplying and Laying of Boulders - nil
- 2548 Nos 5T tetrapods layed
- 12035 Nos 2T layed.
- **no work can be done without RE sanction due to the design changes and change of various items.**

**Scheduled progress as on 13-08-2022–100% (as per EoT given)**

**Achieved progress as on 13-08-2022- 80%**

**Last week progress - 0%**

**Current week progress -0%**

**Current Bill Status** :8th bill submitted for an Amount of Rs.47715746.89/- .Total bill amount - Rs. 451641352.92

**Current Financial Progress : 92.1%**

**Images of works done at Site during last week (with time stamp)**



# PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE  
(KASE)**

**UPGRADATION OF GOVT. ITI  
CHANDANATHOPE ON PAR  
WITH INTERNATIONAL  
STANDARDS**

**Name of Project Engineer:MEENU E S**

**Name of Project Coordinator : Omanakuttan**

Name of contractor : Asian Constructions  
Agreement date : 16-12-2020  
Agreed Amount : ₹3.65 Cr  
Agreed Amount With GST : Rs. 4,09,28,822.77  
Site Handover date : 24-12-2020  
Project duration : 8 months  
Scheduled Date of Completion : 23/08/2021  
Expected Date of completion : 30/10/2022

**Status of Work in terms of components:**

- Main building civil works –51%
- Front gate with security cabin – 0%
- Compound wall – 0%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works –3%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

**Works done in the last week**

- . Main building
- . Electrical works on going
- . Road work wmm completed

**Scheduled progress as on 13/08/2022 - 100%**

**Achieved progress as on 13/08/2022 - 80%**

**Last week progress : 44%**

**Current week progress :5%**

**Current Bill Status :1st bill submitted to KASE, 2nd bill submitted to KASE,3rd bill submitted to KIIDC**

**Current Financial Progress : 56%**

**Images of works done at Site during last week (with time stamp)**



**Thenmala  
(Tourism Project)**

# **IMPROVEMENT AND DEVELOPING ECO-TOURISM AT THENMALA DAM IN KOLLAM DISTRICT**

**Name of Project Engineer: Meenu ES**

**Name of Project Coordinator : OMANAKUTTAN**



**Name of contractor** : Tomy Vallamattom  
Construction  
**Agreement date** : 29-10-2020  
**Agreed Amount** : ₹3,45,61,108.96  
**Agreed Amount With GST** : ₹4,07,82,108.57  
**Site Handover date** : 09-11-2020  
**Project duration** : 15 months  
**Scheduled Date of Completion** : 08-02-2022  
**Expected Date of completion** : 31-08-2022

**Scheduled progress as on 13/08/2022- 100%**

**Achieved progress as on 13/08/2022-59%**

**Last week progress -54%**

**Current week progress -5%**

**Current Bill Status : part bill preparation**

**Current Financial Progress : 58%**

**Images of works done at Site during last week (with time stamp)**

**Status of Work in terms of components:**

- Shop (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)  
pavilion(50%)

**Works done in the last week**

1. Toilet, security room and cloak room-plinth beam work completed.column shuttering work under progress.brick work in progress
2. Shed to shop -roof slab concrete completed
3. Pavilion-step Work progress
4. Seating area clearance completed.



**ITI  
DHANUVACHAPU  
RAM  
(KASE)**

# **UPGRADATION OF GOVT. ITI DHANUVACHAPURAM ON PAR WITH INTERNATIONAL STANDARDS**

**Name of Project Engineer: ATHEESH P MOHAN**

**Name of Project Coordinator : Sarath S R**

Name of contractor	: Heather Construction
Agreement date	: 25-11-2019
Agreed Amount	: ₹11.18 Cr
Agreed Amount With GST	: Rs. 12,52,34,417.4
Site Handover date	: 04-12-2019
Project duration	: 20 months
Scheduled Date of Completion	:30-09-2022
Expected Date of completion	30-09-2022

**Scheduled progress as on 12-08-2022- 95 %(Scope of the work were increased as per the instructions from SPV)**

**Achieved progress as on 12-08-2022 - 95%**

**Last week progress - 94%**

**Current week progress -1%**

**Current Bill Status :15th bill submitted amount:2,02,42,253.35/-**

**Current Financial Progress :79.42%**

**Status of Work in terms of components:**

- GF Slab completed
- FF slab completed
- GF Block work completed
- GF plastering completed
- GF primer work 100% Completed
- GF Electrical work completed
- GF plumbing work 100% completed
- FF Block Work 100% completed
- FF Ceiling work 100% completed
- FF plastering 100% completed
- FF Elec- concealed work completed
- GF Tile work 100%
- FF primer work 100% completed
- **Fire fighting works-delayed due to pending of approval from KASE (SPV)**

**Works done in the last week**

- Paving tile painting
- Entrance glass partition
- cleaning works
- A/C commissioning

Hon. Chief Minister of kerala **Sri Pinarayi Vijayan** Inaugurated the International ITI Dhanuvachapuram (Which is the 1st completed ITI project over all 10 ITIs in kerala) Hon. Minister for Labour and education **Sri. V Shivankutty** presided the function. Parassala MLA sri C K Hareendran, Sri K Ansalan MLA, Sri K B Sathesh MLA, Sri K Gopalakrishnan IAS, Principal in charge Sri S V Anilkumar etc were attended the function.



## LIST OF TOURISM DEPARTMENT COMPLETED PROJECTS

(PHYSICAL PROGRESS 100%)

SL No.	Name of Project	Financial Progress	Remarks
1	Karappuzha Phase III - Construction of Viewing Tower, Bamboo Pavilion and Bridge (Wayanad)	100.00%	-
2	Karappuzha Phase III - Construction of Pathway, Fishing Dock, Pond, Gazebo, Parking yard and Landscaping (Wayanad)	100.00%	-
3	Development of Peruvannamuzhi Dam Tourism Project in Kozhikode District	65.22%	4 <sup>th</sup> and final bill amounting to ₹1,07,88,549.00 submitted to Department of Tourism for release of payment on 20.04.2022.
4	Additional Work I of Eco Lodge Construction at Idukki	100.00%	-
5	Additional Work II of Eco Lodge, Idukki	0.00%	First and part bill amounting to ₹36,81,648.00 submitted to Department of Tourism on 14.03.2022. (Contract PAC: ₹45,85,722.41). Revised Estimate preparation under progress.
6	Providing Temporary Rest Room cum Store (Container Type) for Life Guards at Alappuzha Beach	0.00%	First and final bill amounting to ₹11,96,272.00 submitted to Department of Tourism on 23.03.2022.
