



KIIDC WEEKLY PROGRESS REPORT



KIIDC

PROJECTS IN KANNUR DISTRICT

**ITI KANNUR
(KASE)**

UPGRADATION OF GOVT. ITI KANNUR ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer : Joel J Varghese

Name of Project Coordinator : Visakh A.K

Name of contractor : Shameer M A
Agreement date : 26-08-2020
Agreed Amount :Rs.3,40,93,937.97
Agreed Amount With GST : Rs.3,64,82,353.00
Site Handover date : 04-09-2020
Project duration : 8 months
Scheduled Date of Completion : 03-05-2021
Expected Date of completion : 17-05-2022

Status of Work in terms of components:

Footing works 100 % completed

Stub columns, Grade beam concreting 100% completed

Ground floor columns concreting 100% completed

Block Work 95%

Internal Plastering 90%

External Plastering 80%

Work done in last week

Front gate and security cabin
Lintel
Roofslab
Brick work
Internal floor tiling
Plumbing work

Scheduled progress as on 12-11-2022 65%

Achieved progress as on 12-11-2022 56%

progress up to last week 55 %

Current week progress 1%

Current Bill Status : 2nd Bill submitted

Current Financial Progress :31%

Images of works done at Site during last week (with time stamp)



**REGULATOR
ANCHARAKANDY
RIVER AT
PARAPRAM (KIIFB)**

**KIIFB -CONSTRUCTION OF
REGULATOR WITH LOCK ACROSS
ANCHARAKANDY RIVER AT
PARAPRAM IN PINARAYI
PANCHAYATH, KANNUR DISTRICT**

Name of Project Engineer : Sijo Varghese

Name of Project Coordinator : Visakh A K

Name of contractor : PGCC
Agreement date :06-11-2020
Agreed Amount : ₹44.49 Cr
Agreed Amount With GST : Rs. 498,385,551.00
Site Handover date : 16-11-2020
Project duration : 18 months
Scheduled Date of Completion : 15-05-2022 (extended to 21-11-2022)
Expected Date of completion : 30-06-2023

Status of Work in terms of components:

- Regulator - 73%
- Foot Bridge - 70%
- Lock Portion -95%
- Side Protection -90%
- Mechanical Works -10%
- Generator Cum Watchman Room -90%
- Electrical Works -

Works done in the last week

- Pier,P4 to P5 , Foot bridge slab and beam completed.
- Pier,P6 , upto level +8.4 Completed.
- Abutment, A2 , upto level +6.4 , Completed.
- And Wing walls , concreted upto level +2.5
- P5 to P6 , Foot Slab Concrete completed.

Scheduled progress as on 14-11-2022 100%

Achieved progress as on 14-11-2022 - 73%

progress up to last week - 72%

Current week progress - 1%

Current Bill Status : Nine Part Bill submitted

Current Financial Progress : 62%

Images of works done at Site during last week (with time stamp)



**REGULATOR
UMMENCHIRA RIVER
AT
CHEKKUPALAM(KIIFB)**

**KIIFB - CONSTRUCTION OF REGULATOR
CUM BRIDGE ACROSS UMMENCHIRA
RIVER AT CHEKKUPALAM IN PINARAYI
PANCHAYATH,KANNUR DISTRICT**

Name of Project Engineer : Joel J Varghese

Name of Project Coordinator : Visakh A K

Name of contractor : PGCC
Agreement date : 04-05-2022
Agreed Amount : ₹34.47Cr
Site Handover date : 13-05-2022
Project duration : 18 months
Scheduled Date of Completion : 13-11-2023
Expected Date of completion : 13-11-2023

Scheduled progress as on 12-11-2022 - 7%

Achieved progress as on 12-11-2022 - 7%

Progress up to last week-3%

Current week progress - 5%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Regulator -
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

GPS survey has been completed for geo reference map in presence of kotiyur reserve forest officers and the details has been uploaded in PARIVESH website

Got Permissive sanction from KWA land Acquisition details sent to Government for according sanction



**RCB KUPPAM RIVER
IN
KOOVERY-KATTAM
PALLY (KIIFB)**

**CONSTRUCTION OF REGULATOR
CUM BRIDGE ACROSS KUPPAM
RIVER IN KOOVERY-KATTAMPALLY
IN CHAPPARAPADAVU PANCHAYAT ,
THALIPARAMBA TALUK, KANNUR
DISTRICT**

Name of Project Engineer: Sijo Varghese

Name of contractor : Infab Infrastructures Ltd
Agreement date :15-10-2019
Agreed Amount : ₹ 18,57,64,823.98
Agreed Amount With GST : 22,03,74,512.96 (as per RE)
Site Handover date : 07-11-2019
Project duration : 18 months
Scheduled Date of Completion : 07-05-2021
Expected Date of completion : NA

Status of Work

- The contractor has filed a Writ Petition No 1217/2021 in the Hon'ble High Court of Kerala to stay all coercive steps like termination pursuant to the demand for extension of Bank Guarantee as seen in Ext.P17,till the disposal of this Writ petition.Court directed the 6th respondent(vigilance) to submit report on the matter.Vigilance made an enquiry regarding the matter and they will submit the report to the honourable court.Final decision will be taken according to the verdict from the court.

Scheduled progress as on 14-11-2022 100%

Achieved progress as on 14-11-2022 - 0%

Progress up to last week-0 %

Current week progress - 0%

Current Bill Status :NA

Current Financial Progress :0%

Images of works done at Site during last week (with time stamp)



**THALASSERY HERITAGE PROJECT
(KIIFB-TOURISM)**

Total AS amount – 78.162

Phase 1
14 projects
AS received – 40.95 Cr

Phase 2
14 projects
AS received – 37.212 Cr

Work started

Selection
notice
issued

Tender to
be
finalised

To be
retendered

Work started

To be tendered

To be retendered

1. Pindali kalari
2. Andalurkav Temple
3. Kottiyor siva temple-Streetscape
4. Kottiyor siva temple-Tourist amenities
5. Lokanarkav temple
6. Makreri Subramanyaswami temple
7. Illikunnu church
8. Jagannath temple

1. Thiruvangad Ramaswamy temple

1. Municipal Stadium
2. Kakkulangara Mosque


1. Thirunelli Temple
2. Thrissillery Temple
3. Odathil Mosque – Paris Hotel Street

1. Puralimala temple
2. Pazhassiraja smrithimandapam
3. Valliyoorkavu temple
4. Chirakkakavu temple


1. Vairighathaka Temple
2. Arakkal kettu
3. Sree Oorpazhassi kavu Temple
4. Padinjare Kovilakam-Pazhasi Smrithi Mandapam
5. Valliyoorkavu convention centre

1. Thacholi Manikoth Temple
2. Vadakara Tazhe angadi
3. Peralassery Temple
4. Thalakkal Chandu Museum – Panamaram
5. Kadirur Surya Narayana Temple
6. Sree Mridanga Saileswari Temple
7. Thodeekalam Siva Temple


Pazhassi Circuit




Cultural Circuit



Harbour Town Circuit

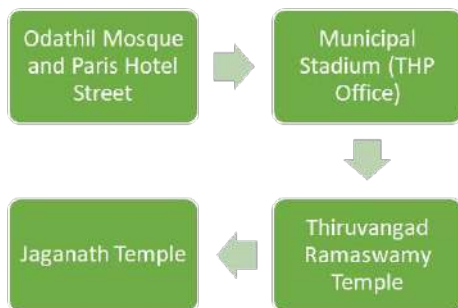

Folklore Circuit



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT - PHASE 1 -
Cultural Circuit -Andalur Kavvu**

Name of Project Engineer: Ebin solomon

Name of Project Coordinator : Visakh A.K

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.5189 Cr
Agreed Amount With GST : Rs. 1.701cr
Site Handover date : 08/03/21
Project duration : 12 months
Scheduled Date of Completion : 26-02-2022
Expected Date of completion : 21/02/2023

Status of Work in terms of components:

- Pathway
- Chuttambalam Roofing
- Lighting
- Street Development
- Electrification

Work done in last week

- Roof truss work and tile work.

Scheduled progress as on 14-11-2022 : 100%

Achieved progress as 14-11-2022 - 34%


Progress up to last week - 32%

Current week progress -2%

Current Bill Status : first bill submitted

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

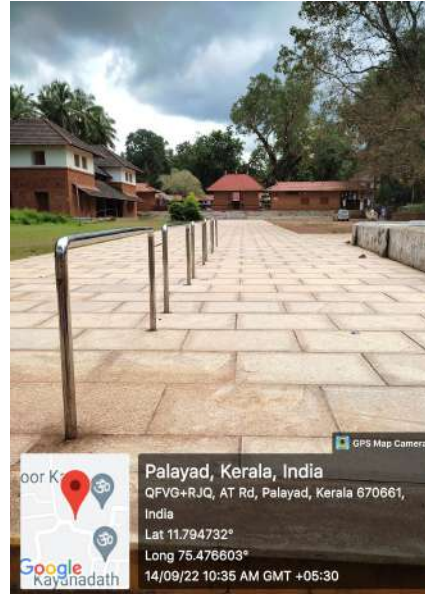

**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -illikunnu

Name of Project Engineer: Ebin solomon

Name of Project Coordinator : Visakh A.K

Name of contractor : Sri. Varkeychan Vallamattam
Agreement date : 26/02/2021
Agreed Amount : ₹ 8300000
Site Handover date : 08/03/2021
Project duration : 12 months
Scheduled Date of Completion : 26/02/2022
Expected Date of completion : 09/02/2023

Status of Work in terms of components of cemetery :

- Land scaping of cemetery area
- Lighting
- Conservation of ceiling, wood work, joinery

Work done in last week

- Old plastering demolition work
- Church building outside plastering work



Scheduled progress as on 14-11-2022 : 100%

Achieved progress as on 14-11-2022 - 47%

Progress upto last week - 45%

Current week progress -2%

Current Bill Status : 1st bill submitted

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB PROJECT - THALASSERY HERITAGE PROJECT - PHASE 1 -Jaganath Temple

Name of Project Engineer: Ebin solomon

Name of Project Coordinator : Visakh A.K

Name of contractor : Sri. R.V Joseph
Agreement date : 26/02/2021
Agreed Amount : ₹ 1,48,17,938.56
Agreed Amount With GST : 1.56cr
Site Handover date : 08/03/2021
Project duration : 12 months
Scheduled Date of Completion : 08/03/2022
Expected Date of completion : 26/02/2023

Status of Work in terms of components :

- Pathway
- Rivival of pond
- Compound wall
- Landscaping

Work done in last week

- Sadarhalli paving pointing clearing work
- Chira compound wall demolition work completed
- Chira compound wall plith beam concreted.

Scheduled progress as on 14-11-2022 : 100%

Achieved progress as 14-11-2022 - 32%

Progress upto last week- 28%

Current week progress 4%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT-Makreri
Subramanyaswami Temple (Cultural
Circuit)**

**Name of Project Engineer: Sijo Varghese
Name of Project Coordinator : Visakh A.K**

Name of contractor : M/S Saaj Constructions
Agreement date : 17/06/2021
Agreed Amount : ₹ 1,83,50,573.45/-
Agreed Amount With GST : 2,05,52,642.26/-
Site Handover date : 27.06.2021
Project duration : 12 months
Scheduled Date of Completion : 27/06/2022
Expected Date of completion :

Status of Work in terms of components :

- Oottupura
- Toilet block
- Landscaping
- Water supply and Sanitary Arrangements
- street scape of Paving of Chuttambalam
- Stone paving
- Conservation of pond
- Electrification

Work done in last week

- Satharhalli , paving in nadapanthal works Completed.
- Oottupura, Compound wall works completed.
- Pathway, side , Excavation completed, PCC completed.
- Oottupura laterite, work progressing.

Scheduled progress as on 14-11-2022 : 100 %

Achieved progress as 14-11-2022 - 35%

Last week progress - 33%

Current week progress -2%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT-PHASE 2 -
Pazhassi Circuit - Puralimala Temple
at Maloor in Kannur District**

Name of Project Engineer: Sijo Varghese

Name of Project Coordinator : Visakh A.K

Name of contractor : Veda Constructions
Agreement date : 28.10.2021
Agreed Amount : ₹ 62,79,215.13/-
Site Handover date : 05.11.2021
Project duration : 12 months
Scheduled Date of Completion : 28.10.2022
Expected Date of completion :

Status of Work in terms of components :

- Nadapanthal
- Waiting shed
- Office
- Toilet
- Pathway
- Watertank
- Demolishing Shed
- Plumbing
- Landscape
- Electrical Work

Work done in last week

- Setting out for Office & Toilet Completed.
- Earthwork Excavation for Office & Toilet Completed.

Scheduled progress as on 14-11-2022 : 100 %

Achieved progress as 14-11-2022 - 1%

Last week progress - 1%

Current week progress 1%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT - THALASSERY
HERITAGE PROJECT - PHASE 1
-Pazhassi Circuit - Pindali Kalari
House(Pathway,Conservation of
Kalarithara,Pond restoration ,Seating,
Landscaping ,Electrification)at
Iritty,Kannur**

Name of Project Engineer:Joel J Varghese

Name of Project Coordinator : Visakh A.K

Name of contractor : M/s Classic Builders
Agreement date : 17-02-2021
Agreed Amount : ₹ 0.6238 Cr
Agreed Amount With GST : Rs. 6987127.71
Site Handover date :
Project duration : 12 months
Scheduled Date of Completion : 27-02-2022
Expected Date of completion :

Scheduled progress as on 12-11-2022 : 59%

Achieved progress as on 12-11-2022 - 53%

Progress upto last week - 0%

Current week progress -0%

Current Bill Status : Ready for Part 1 bill

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

Gallery Work 100 %
completed

Kalarithara 50%

Kalasaamandaapam 25%
Pond 50%

Work done in last week

No works done



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY HERITAGE
PROJECT-PHASE 1-pazhassi circuit –kottiyoor shiva
temple(streetscape,landscaping,agrashala,carpark
ing,stage and electrical work at kottiyoor shiva
temple in irrity,Kannur district)**

Name of Project Engineer :EBIN SOLOMON

Name of Project Coordinator : Visakh A.K

Name of contractor : M/s Rubicon construction
Agreement date : 05/10/2021
Agreed Amount : ₹ 1.21 cr
Agreed Amount With GST : RS 1,36,06,740.60
Site Handover date : 14/10/2021
Project duration : 12 months
Scheduled Date of Completion : 13-10-2022
Expected Date of completion : 13/03/2023

Status of Work in terms of components:

- Streetscape
- Landscaping
- Agrashala
- Car parking
- Stage
- electrification

Work done in last week

agrashala-inside and outside
plastering work completed
Stone pillar work in progress

Scheduled progress as on 14/11/2022 : 80%

Achieved progress as 14/11/2022 - 60%

Last week progress - 60%

Current week progress -0-%

Current Bill Status : 2nd bill submitted

Current Financial Progress : 17%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY HERITAGE
PROJECT-PHASE 2-cultural circuit**

**Sree Chirakka kavu Bhagavathi Temple at
Thalassery,Kannur district**

Name of Project Engineer :Don Baby

Name of Project Coordinator : Visakh A.K

Name of contractor : Saaj constructions
Agreement date : 22/08/2022
Agreed Amount : ₹1,60,17,996.76
Site Handover date : 01/09/2022
Project duration : 12 months
Scheduled Date of Completion : 01-09-2023
Expected Date of completion : 01/09/2023

Status of Work in terms of components:

- Paving of road
- Gallery & dining
- Toilet blocks
- street lighting & parking yard
- Office
- Landscaping
- Electrical work

Work done in last week

work will start on 16/11/2022

Scheduled progress as on 14/11/2022 :8%

Achieved progress as 14/11/2022 - 0%

Last week progress - 0%

Current week progress -0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

**COMPREHENSIVE
DEVELOPMENT OF
MUZHAPPILANGAD
AND DHARMADAM
BEACH IN KANNUR
DISTRICT**

**KIIFB PROJECT –COMPREHENSIVE DEVELOPMENT
OF MUZHAPPILANGAD AND DHARMADAM BEACH
IN KANNUR DISTRICT**

Name of Project Engineer :Vishnu R

Name of Project Coordinator : Visakh A.K

Name of contractor : The Uralungal Labour Contract
Co-Operative Society
Agreement date : 26/09/2022
Agreed Amount : ₹616288142.16
Site Handover date : 26/09/2022
Project duration : 18 months
Scheduled Date of Completion : 26-02-2024
Expected Date of completion : 26/02/2024

Status of Work in terms of components:

- Appendix -A
CHARACTER AREA- 1
Demolishing and dismantling of existing structures are in progress.
- 3 nos of test piling completed.

Work done in last week

- 1.Pre measurement for the existing structures
2. Setting out of alignment for the promenade structures
- 3.Steel work for the piles

Scheduled progress as on 15/11/2022 :5%

Achieved progress as 15/11/2022 - 2%

Last week progress - 0%

Current week progress -0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)



**PAZHASSI
PADIYOOR
ECOTOURISM
(TOURISM)**

ECO TOURISM DEVELOPMENT AT PAZHASSI DAM AND SURROUNDING AREA, PADIYOOR

Name of Project Engineer: Don Baby

Name of Project Coordinator : Visakh A.K.

Name of contractor : Sri. Joseph R. V.
Agreement date : 19.10.2022
Agreed Amount : Rs.3,99,91,828.23
Agreed Amount With GST : Rs.4,71,90,357.31
Site Handover date : 29.10.2022
Project duration : 18 months
Scheduled Date of Completion : 29.04.2024
Expected Date of completion : 29.04.2024

Status of Work in terms of components:

- Road Work
- Restaurant, Wooden Deck, Entrance Gate
- Toilet Block and Sanitary
- Electrification

Works done in the last week

- Jungle clearance,survey in progress.
- Work started on 29.10.2022
- Survey for road done on 10/11/2022

Scheduled progress as on 14.11.2022-1%

Achieved progress as on 14.11.2022 -0.9%

Last week progress :0.5%

Current week progress :0.4%

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week



PROJECTS IN WAYANAD DISTRICT

**Community micro
irrigation at
Athichal
Mundankolly
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Athichal
Mundankolly in Ambalavayal
Panchayath Wayanad district -
CMI Part**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Visakh Ak

Name of contractor : M/S Mahindra EPC Irrigation limited
Agreement date : 13-04-2022
Agreed Amount : 2.14 Crores
Agreed Amount With GST :
Site Handover date : 22-04-2022
Project duration : 6 months
Scheduled Date of Completion : 21-10-2022
Expected Date of completion : 21-10-2022

Scheduled progress as on 14/11/2022 - 100%

Achieved progress as on 14/11/2022 - 21%

Last week progress in : 21%

Current week progress : 0%

Current Bill Status : Nil

Current Financial Progress : Nil


Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main line - 10 %
- Submain line - 10%
- Automation - 0%

Works done in the last week

- Survey completed
- Alignment marking is restarted
- Peg marking completed
- Trenching is scheduled to start this week

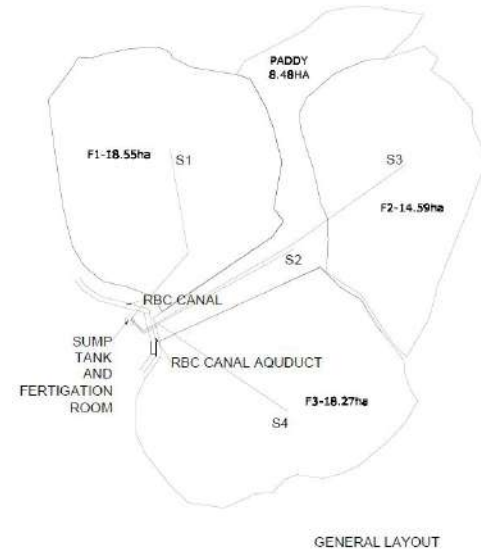

**Community micro
irrigation at
Athichal
Mundankolly
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Athichal
Mundankolly in Ambalavayal
Panchayath Wayanad district -
Civil**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Visakh Ak

Name of contractor : Shri Saji mathew
Agreement date : 04-04-2022
Agreed Amount : 25.05 Lakhs
Agreed Amount With GST :
Site Handover date : 13-04-2022
Project duration : 4 months
Scheduled Date of Completion :12-08-2022
Expected Date of completion :12-08-2022

Status of Work in terms of components:

- Irrigation room - 70%
- Sump tank - 90%
- Electrical Works - 0%

Works done in the last week

- Lintel concrete for fertigation room
- Brick work for fertigation room

Scheduled progress as on 14/11/2022 - 100 %

Achieved progress as on 14/11/2022 - 80 %

Last week progress in : 70%

Current week progress : 10%

Current Bill Status :

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE PROJECT
(KIIFB-TOURISM)**

KIIFB Project - KIIFB Project- Thalassery Heritage Project - Phase 2 - Pazhassi Circuit -Valliyoorkavu temple - Streetscape (Stone steps to temple, Lamp Post, Electrification) at Mananthavady in Wayanad District – Conducting test on given samples of cement, Aggregate, Laterite and Sadarhalli granite stone

Name of Project Engineer :Athul ashar

Name of Project Coordinator : Visakh A.K

Name of contractor : Shri. Ameer Ali N
Agreement date : 30 -04-2022
Agreed Amount : 3673949.76
Agreed Amount With GST :
Site Handover date : 12/05/2021
Project duration : 6 months
Scheduled Date of Completion : 11-11-2022
Expected Date of completion :11-11-2022

Status of Work in terms of components:

- Stone steps to temple - 98 %
- Lamp post - 80%
- electrification - 50%

Work done in last week

- Plastering completed
- Sadarahalli stone paving ongoing

Scheduled progress as on 14/11/2022 : 100%

Achieved progress as 14/10/2022 - 93%

Last week progress -85%

Current week progress :8%

Current Bill Status : 1st & part under preparation

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)



PROJECTS IN KOZHIKODE DISTRICT

**RCB ACROSS
POONUR
PUZHA-POOLAKAD
AVU (KIIFB)**

**KIIFB PROJECT CONSTRUCTION
OF RCB ACROSS POONUR PUZHA
NEAR KWA PUMPING HOUSE AT
POOLAKADAVU IN KURUVATTOOR
PANCHAYATH**

Name of Project Engineer: Athul Ashar

Name of Project Coordinator : Bibin Giri

Name of contractor : ULCCS Ltd.
Agreement date : 18-08-2021
Agreed Amount : ₹22,68,45,702.29
Agreed Amount With GST : Rs.
Site Handover date : 27-08-2021
Project duration : 18 months
Scheduled Date of Completion : 26-02-2023
Expected Date of completion : 26-02-2023

Status of Work in terms of components:

- Regulator -25%
- Side Protection -0%
- Approach Road - LA Ongoing
- Mechanical Works - 4 shutter fabrication completed
- Generator Cum Watchman Room -LA ongoing
- Electrical Works -0%

Works done in the last week

- Bar bending for Pile cap and Pile
- Fabrication of shutter
- piling work at right bank
-

Scheduled progress as on 14-11-2022 - 45%

Achieved progress as on 14-11-2022- 25%

Progress upto last week- 22%

Current week progress - 3 %

Current Bill Status : CC First and part bill submitted

Current Financial Progress : nil

Images of works done at Site during last week (with time stamp)



**ITI KOYILANDY
(KASE)**

UPGRADATION OF GOVT. ITI KOYILANDY ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer : Vishnu R

**Name of Project Coordinator : Sethumadhavan K.P
(Additional charge)**

Name of contractor : ULCCS Ltd.
Agreement date : 14-08-2020
Agreed Amount : ₹4.22 Cr
Agreed Amount With GST : Rs. 4,22,86,606
Site Handover date : 14-08-2020
Project duration : 12 months
Scheduled Date of Completion :31-12-2022
Expected Date of completion :31-12-2022

Status of Work in terms of components:

- Main Building Civil works – 95%
- Main Building Electrical works – 90%
- Main Building ELV Works - 82%

Works done in the last week

- Electrical work in progress
- Belt -above retaining wall concreting
- Road works
- Plumbing works

Scheduled progress as on 15-11-2022- 100%

Achieved progress as on 15-11-2022 - 92%

Last week progress- 5%

Current week progress - 5%

Current Bill Status : CC 4th and part submitted

Current Financial Progress : 70%

Images of works done at Site during last week (with time stamp)



**THALASSERY
HERITAGE
PROJECT
(KIIFB-TOURISM)**

**KIIFB PROJECT –THALASSERY
HERITAGE PROJECT-PHASE 1-pazhassi
circuit**

Lokanarkavu Temple (Conservation of Thantrimadom,
Folklore, Oottupura, Chiras, Plumbing and Electrification
at Lokanarkavu Temple in Vadakara, Kozhikode District)

Name of Project Engineer: Vishnu R

Name of Project Coordinator : Visakh Ak

Name of contractor : Saaj Constructions
Agreement date : 17-06-2021
Agreed Amount : ₹ 3,78,74,574.27/-
Site Handover date : 26-06-2021
Project duration : 12 months
Scheduled Date of Completion :25/10/2022
Expected Date of completion :31/03/2023

Scheduled progress as on 15-11-2022- 90%

Achieved progress as on 15-11-2022 - 35%

Last week progress- 2%

Current week progress - 5%

Current Bill Status : Part -1 bill submitted

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- thanthrimadam inside plastering on progress.
- Oottupura retaining wall works on progress.
- compound wall coping plastering work

Workshops done in the last week

- 1.Oottupura retaining wall excavation and PCC work
- 2.Thandrimadam -Grinding works
- 3.steel work for Plinth beam oottupura



**RCB
PERINCHERIKADAVU
(KIIFB)**

**CONSTRUCTION OF REGULATOR CUM
BRIDGE AT U/S OF
PERINCHERIKADAVU IN KUTTIADY
RIVER (GULIKAPUZHA) AT KOZHIKODE
DISTRICT**

Name of Project Engineer : RAHEES P

**Name of Project Coordinator : Sethumadhavan K.P
(Additional charge)**

Name of contractor : TBAS – EKK Consortium
Agreement date : 07-09-2020
Agreed Amount : ₹ 61,13,34,133.18/-
Agreed Amount With GST : ₹ 68,46,94,229/-
Site Handover date : 17-09-2020
Project duration : 18 months
Scheduled Date of Completion :16-03-2022 (Extended to 15-04-2023)
Expected Date of completion :01-03-2024

Scheduled progress as on 15-11-2022 - 85%

Achieved progress as on 15-11-2022 - 31%

Progress upto last week-30%

Current week progress 1%

Current Bill Status : 3rd bill submitted

Current Financial Progress : 17%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Regulator -15%
- Lock Portion -
- Side Protection -40%
- Deck Slab -
- Approach Road -
- Mechanical Works-
- Generator Cum Watchman Room-
- Electrical Works -

Works done in last week

L/S- D/S retaining wall chainage 25m-50m second lift concreted

Gabion work progressing on A1-P1 section

A1 final lift concreted Tie beam and weir between A1-P1 started



**PROJECTS IN
MALAPPURAM
DISTRICT**

**Puzhankavu
Regulator
(KIIFB)**

KIIFB Project - Construction of Regulator at Puzhankavu across Kadalundi River

Name of Project Engineer : RAHEES.P

Name of Project Coordinator :

Name of contractor : Infab Infrastructure Pvt Ltd
Agreement date : 17-12-2019
Agreed Amount : ₹ 9,79,65,435.62
Agreed Amount With GST : Rs. 10,97,21,287.89
Site Handover date : 17-12-2019
Project duration : 18 months
Scheduled Date of Completion :16/06/2021-(Extended to 21-11-2022)
Expected Date of completion :21-11-2022

Status of Work in terms of components:

- Regulator -100%
- Side Protection -95%
- Mechanical Works -95%
- Generator Cum Watchman Room -80%
- Electrical Works -0%

Works done in the last week.

- Continuing Heavy flow of water at site.
- Guard room plastering completed.
- KIIFB done routine inspection.

Scheduled progress as on 15-11-2022- 100%

Achieved progress as on 15-11-2022 -95.8%

Progress upto last week -95.80%

Current week progress - 0.10%

Current Bill Status : Total Bill submitted ₹7.68 Crores (10th part bill)

Current Financial Progress in :81.06%

Images of works done at Site during last week



**RCB
Moothikkayam
(KIIFB)**

KIIFB - Construction of Regulator cum Bridge across thoothapuzha keezhmurikadavu moothikkayam in moorkanad panchayath

Name of Project Engineer: Sethu Madhavan

Name of Project Coordinator : Lakhan Murari

Name of contractor	: M/s PGCC Pvt,Ltd
Agreement date	: 18/09/2020
Agreed Amount	: ₹57.56 Cr
Agreed Amount With GST	: Rs. 64.46 crore
Site Handover date	: 26-09-2020
Project duration	: 18 months
Scheduled Date of Completion	:26-03-2022 (Extended to 31-05-2023)
Expected Date of completion	:31-05-2023

Scheduled progress as on 12--11-2022 - 100%

Achieved progress as on 12-11-2022 - 37.7%

Progress upto last week -37.82%

Current week progress -0.01%

Current Bill Status : Fifth bill submitted

Current Financial Progress : 24.84%

Images of works done at Site during last week (with time stamp)

STATUS OF WORK IN TERMS OF COMPONENTS

- Regulator - 45%
- Side Protection - 40%
- Deck Slab - 60%
- Mechanical Works - 17%
- Generator Cum Watchman Room -
- Electrical Works -

Work done in the last week

- Ongoing excavation for abutment.
- Remaining civil works were affected due to heavy rain and consequent flood

Mechanical Works

- 6 no's shutter delivered to site.



PROJECTS IN PALAKKAD DISTRICT

**ITI MALAMPUZHA
(KASE)**

UPGRADATION OF GOVT. ITI MALAMPUZHA ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer:NITHISH. C

Name of Project Coordinator : Lakhan Murari

Name of contractor : M/S. PERFECT ENGINEERS
Agreement date : 05/03/2020
Agreed Amount : Rs.11,61,93,745/-
Agreed Amount With GST : Rs. 13,01,36,994.40/-
Site Handover date :06/03/2020
Project duration : 18 months
Scheduled Date of Completion. : 05/09/2021
Expected Date of completion. : 02/06/22

Status of Work in terms of components

- Smart classroom promethean and writing board fixing completed
- Part 3&4 UGF roof slab till expansion joint completed.
- Block work part 1 portion completed.
- Instrumental workshop area roof slab concreting completed

Works done in the last week

- Tile fixing at smart classroom
- Expansion joint covering
- Electrical work
- External wall plastering
- AAC block work at FF
- Cable pulling
- Internal plastering at FF
- Tile fixing in toilet wall at FF

Scheduled progress as on 12/11/2022- 100%

Achieved progress as on 12/11/2022 - 78.50 %

Last week progress - 75%

Current week progress - 70%

Current Bill Status : no of bill submitted - 6,amount:4,21,29,262

Current Financial Progress : 36.26%

Images of works done at Site during last week (with time stamp)



VADAKARAPALLY
REGULATOR
(KIIFB)

Construction of Regulator across Chittur
Puzha at Vadakarapally Palathulli in
Peruvembu Grama Panchayt in Palakkad
District

Name of Project Engineer:NITHIN J B

Name of Project Coordinator : Lakhan Murari

Name of contractor : Poonam grah nirman Pvt ltd
Agreement date : 04-01-2021
Agreed Amount : ₹18.95 Cr
Agreed Amount With GST : Rs. 21,23,18,001.2
Site Handover date : 12-01-2021
Project duration : 18 months
Scheduled Date of Completion : 12-07-2022
Expected Date of completion : 12-11-2022

Status of Work in terms of components:

- Regulator - 90%
- Side Protection - 75%
- Generator Cum Watchman Room -
- Mechanical Works - 85%
- Electrical Works -

Works done in the last week

- U/S LHS retaining wall concrete.
- Fabrication of hoisting bridge mechanism.
- Secondary concrete on piers.
- Preparation of platform for erection of shutters.
- Joining of shutters and implementation of rubber seal on shutters.
- Placement of shutters.

Scheduled progress as on 14/11/2022 - 100%

Achieved progress as on 14/11/2022 - 96%

progress up to last week - 93%

Current week progress - 3%

Current Bill Status : Seventh and part bill submitted.

Current Financial Progress : 50.92%

Images of works done at Site during last week



**Moongilmada LIS
(Civil)
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Moongilmada
LIS in eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of Project Coordinator : Lakhan Murari

Name of contractor : M/s Vallamattam constructions
Agreement date : 18-09-2020
Agreed Amount : ₹15422222 Crores
Agreed Amount With GST : Rs. 18198221.96/-
Site Handover date : 03-06-2021
Project duration : 6 months
Scheduled Date of Completion :03-12-2021
Expected Date of completion :31-05-2022

Status of Work in terms of components:

- Pump House
- Conversion of abandoned RBC to water storage.
- Electrical Works

Works done in the last week

Electrical works ongoing

PWD road crossing completed

Desilting work carried out by MGNREGS

canal lining work can only start after the completion of desilting

Scheduled progress as on 13/11/2022 - 100%

Achieved progress as on 13/11/2022 - 90%

Last week progress in : 90%

Current week progress : 0%

Current Bill Status : Part Bill-2

Current Financial Progress : 53%

Images of works done at Site during last week (with time stamp)



**Valiyeri LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at Valiyeri LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd
Agreement date : 24-06-2021
Agreed Amount : ₹31004000 Rupees
Agreed Amount With GST : Rs. 36581180/-
Site Handover date : 25-06-2021
Project duration : 12 months
Scheduled Date of Completion :25-06-2022
Expected Date of completion :31-05-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

AUTOMATION WORKS can be completed after the installation of pumpset

Scheduled progress as on 13/11/2022 - 100%

Achieved progress as on 13/11/2022 - 96 %

Last week progress in : 96%

Current week progress : 0%

Current Bill Status : Part Bill-2

Current Financial Progress : 64%

Images of works done at Site during last week (with time stamp)



**Navithankulam LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at
Navithankulam LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Jain Irrigation Systems Pvt Ltd
Agreement date : 24-06-2021
Agreed Amount : ₹16327047.54 Rupees
Agreed Amount With GST : Rs. 19265916.09/-
Site Handover date : 25-06-2021
Project duration : 12 months
Scheduled Date of Completion :25-06-2022
Expected Date of completion :31-06-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

WAITING TO COMPLETE CIVIL WORKS

Scheduled progress as on 13/11/2022 - 100%

Achieved progress as on 13/11/2022 - 84 %

Last week progress in : 83%

Current week progress : 1%

Current Bill Status : Nil

Current Financial Progress : first bill

Images of works done at Site during last week (with time stamp)



**Kunnamkatupathy
LIS
WRD-RKI**

**KIIDC-Providing Community
micro irrigation at
Kunnamkatupathy LIS in
eruthenpathy Panchayath
palakkad district**

Name of Project Engineer: Amal Padmu LP

Name of contractor : M/s Mahendra Pvt Ltd
Agreement date : 18-11-2021
Agreed Amount : ₹36068276 Rupees
Agreed Amount With GST : Rs. 42560565.68/-
Site Handover date : 27-11-2021
Project duration : 6 months
Scheduled Date of Completion :29-05-2022
Expected Date of completion :31-06-2022

Status of Work in terms of components:

- Automation Unit
- Main Line Works
- Submain Line Works
- Laying Of Laterals

Works done in the last week

submain and mainline work

Automation works can be completed after the completion of Irrigation room

Scheduled progress as on 13/11/2022 - 100%

Achieved progress as on 13/11/2022 - 89 %

Last week progress in : 89%

Current week progress : 0%

Current Bill Status : Partbill-4

Current Financial Progress : 34%

Images of works done at Site during last week (with time stamp)



**MOOLATHARA
RIGHT BANK CANAL
PHASE 1 FROM
KORAYAR TO
VARATTAYAR
(KIIFB)**

**KIIFB-Extension of Moolathara
right bank canal phase 1 from
korayar to varattayar**

Name of Project Engineer: NITHISH.C

Name of contractor : M/s Prathmesh & K.K.Constructions
Agreement date : 23-12-2021
Estimate P.A.C : Rs.158,50,00,000/-
CONTRACT P.A.C : Rs. 174,34,95000/-
Site Handover date : 31-12-2021
Project duration : 30 months
Scheduled Date of Completion : 23-06-2024
Expected Date of completion : 23-06-2024

Scheduled progress as on 13/11/2022 - Nil

Achieved progress as on 13/11/2022- 1.5%

Progress up to last week : 1%

Current week progress : 0.5%

Current Bill Status : Submitted a bill of Rs.4.35 Cr to KIIDC

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work

1. Revised Hydraulic particulars submitted by the contractor on 17/08/2022 was approved by the Design Evaluation Committee constituted for MRBC Phase 1, on 06/09/2022.
2. Revised design based on the approved hydraulic particulars on 16-09-2022 is under the scrutiny of Design Evaluation Committee.
3. Tunnel profile set out is in progress
4. Almost 556 trees has been cut down.Auction of the same is in progress.



**DESILTATION OF
VELLIYANKALLU
RCB ON TURN KEY
BASIS.**

DESILTATION OF VELLIYANKALLU RCB ON TURN KEY BASIS

**Name of Project Engineer: RAHUL V R
Name of Project Coordinator : GOPAKUMAR**

Name of contractor : M Unnikrishnan, Moorthodiyil (H)
Agreement date : 20-05-2022
Estimate P.A.C : Rs.2,57,11,350/-
CONTRACT P.A.C : Rs.2,85,15,000/-
Site Handover date : 28-05-2022
Project duration : 6 months
Scheduled Date of Completion : 30/11/2022
Expected Date of completion :

Scheduled progress as on 12/11/2022 - 90%

Achieved progress as on 12/11/2022- 5%

Last week progress in : Nil

Current week progress : Nil

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

Amount payable to KIIDC by bidder for removing the river sand as is where is condition from the demarcated area using the most appropriate and latest technologies.

Works done in the last week

Initial levels have been reported to CTE



PROJECTS IN THRISSUR DISTRICT

**REGULATOR CUM
BRIDGE ACROSS
KURUMALI PUZHA
IN THRISSUR
DISTRICT.**

**CONSTRUCTION OF
KANATHODU REGULATOR CUM
BRIDGE ACROSS KURUMALI
PUZHA AT KUNDUKADAVU IN
PUDUKAD PANCHAYATH,
THRISSUR DISTRICT.**

**Name of Project Engineer: RAHUL V R
Name of Project Coordinator : Gopakumar**

Name of contractor : PGCC
Agreement date :05-01-2022
Agreed Amount : 262383481.27
Agreed Amount With GST : Rs.293869499.022
Site Handover date : 13-01-2022
Project duration : 18 months
Scheduled Date of Completion : 13-07-2023
Expected Date of completion : 13-07-2023

Scheduled progress as on 12/11/2022- 48%

Achiever progress as on 12/11/2022 - 6%

Progress up to last week- 6%

Current week progress -0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Ring bund- 6%
- Regulator -
- Side Protection -
- Deck Slab -
- Approach Road -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

- Revised GFC drawings was issued on 02-04-2022
- River boundary survey was completed on 18-02-2022
- Initial levels also been taken
- **Work delayed since 27/06/2022 due to heavy rain and rise in water level in the River**
- **Ring bund dismantled due to Rise in water level**
- Due to the non availability of earth for ring bund work, the work has delayed for the past few weeks



**ITI CHALAKUDY
KIIFB-KASE**

UP GRADATION OF GOVT ITI CHALAKUDY ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: RAHUL V R

Name of contractor : Sidheek, M/S Sitco Associates
Agreement date : 28-10-2020
Agreed Amount : ₹ 7,47,51,405.13
Agreed Amount With GST : ₹ 8,37,21,573.74
Site Handover date : 06-11-2020
Project duration : 12 months
Scheduled Date of Completion : 05-11-2021
Expected Date of Completion :

Scheduled progress as on 12/11/2022- 0 %

Achieved progress as on 12/11/2022 - 0 %

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building (0%)
- Front gate with security cabin (0%)
- Compound wall (0%)
- Road and ancillary works(0%)
- Land development (0%)
- External water supply (0%)
- External sewerage system (0%)
- Rain water drainage (0%)
- Rain water drainage (0%)
- External fire protection system (0%)
- Existing class room converted to smart class rooms (0%)
- External lighting
- New smart class room works (0%)
- signages and boards (0%)

Works done in the last week

As per drawings building setbacks are not available at the site. The proposed building and setbacks drawings were redesigned according to existing boundary condition

A site visit was conducted by KASE and KIIDC officials for setting out of the proposed building, but due to the vegetative cover and trees, it was impossible to enter into the proposed building plot. ITI authority has agreed to clear the plot as soon as possible. Detailed report will be prepared once the site is cleared.



PROJECTS IN ERNAKULAM DISTRICT

**CHELLANAM
COASTAL
PROTECTION
[KIIFB]**

**KIIFB PROJECT- REFORMATION OF DAMAGED
SUNKEN SEA WALL AT CHELLANAM USING
TETRAPODS AND RUBBLE IN BETWEEN CP
STONE 976 AND 1052 FOR 10 KM STRETCHES
ALONG CHELLANAM COAST IN ERNAKULAM
DISTRICT - PHASE I FOR A LENGTH OF 7/350
KM IN BETWEEN CP 986 AND CP 1026**

**Name of Project Engineer : SREELAKSHMI S
Name of Project Coordinator : Mahadevan**

Name of contractor : M/s Uralungal Labour Contract Co-operative

Agreement date : 30-12-2021

Agreed Amount : ₹ 256,89,67,441.29

Agreed Amount With GST : ₹ 287,72,43,534.25

Site Handover date : 03-01-2022

Project duration : 16 months

Scheduled Date of Completion : 02-05-2023

Expected Date of Completion : 02-05-2023

Scheduled progress as on 13/11//2022- 64.88%

Achieved progress as on 13/11/2022- 66.63%

Progress up to last week- 64.87 %

Current week progress- 1.76%

Current Bill Status : C.C 4th and Part Bill submitted. Amount: 58.61Cr Total Bill Amount = 188.79 Cr. (including 18% GST)

Current Financial Progress : 56.64%

Status of Work :

- 51700nos of 2T tetrapods cast.
- 39197nos of 3.5T tetrapods cast.
- 2T Tetrapod placed : 45024nos
- 3.5T Tetrapod placed : 36213nos

Total Boulders Supplied till 10.11.2022

- Core layer (10-50kg) = 133539.845 T
- Toe (200 to 400kg) = 78838.819 T
- Underlayer (150-200kg) = 99851.037 T
- Toe (250-350kg) = 178315.593 T
- Toe (350-700kg) = 82625.889 T
- Primary layer(500-800kg)= 25423.48 T

Works done in the last week

- Supplying and laying of boulders for Seawall in progress Sub Reach 1 to 15.
- Bathymetry survey- Bazar Groyne field carried out.
- Dismantling of old existing seawall (Ch: 0/000 to 0/150)

Images of works done at Site during last week



**RCB
KONOTHUPUZHA
(KIIFB)**

**Construction of Regulator with
lock across Konothupuzha at
Puthenkavu in Udayamperoor
Panchayath in Ernakulam
District**

**Name of Project Engineer: Remya P R
Name of Project Coordinator : Bibin Giri**

Name of contractor : Marymatha construction
Agreement date : 04-01-2021
Agreed Amount : ₹24.36 Cr
Agreed Amount With GST : Rs. 272,843,729.92
Site Handover date : 14-01-2021
Project duration : 18 months
Scheduled Date of Completion : 13-07-2022
Expected Date of completion : 15-04-2023

Scheduled progress as on 14-11-2022 - 45%

Achieved progress as on 14-11-2022- 27%

Progress upto last week- 26.00%

Current week progress - 1.00%

Current Bill Status :cc 1st,2nd & 3rd approved.(5.62cr without GST)

Current Financial Progress :23 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:


- Regulator - 10%
- Lock Portion - 17%
- Side Protection -
- Mechanical Works -
- Generator Cum Watchman Room -
- Electrical Works -

Works done in the last week

Piling works -Lock portin- 56 piles, Pier 1 , Pier 2 & Pier 3- 12nos piles completed.Left abutment- 4 no.s completed.Total -72 piles(Piling works completed).

*The Earthwork excavation of pile cap for lockwall portion,pile chipping,laying of PCC works below pilecap are in progress.

***But the unexpected rain affects the progress of the work.**

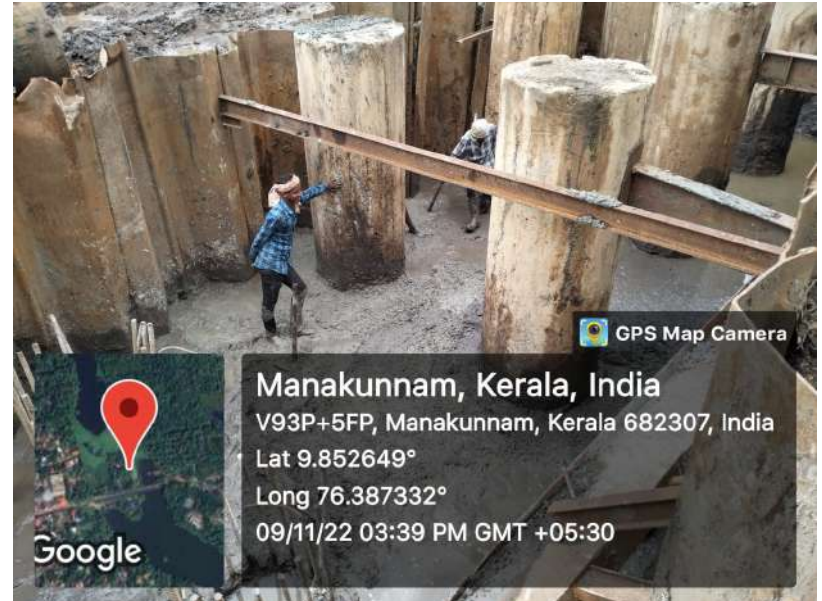

**ANTHAKARATHO
DU CANAL
(KIIFB)**

IMPROVEMENTS TO ANTHAKARATHODE IN THRIPPUNITHURA MUNICIPALITY

Name of Project Engineer: Princy Abraham

Name of Project Coordinator : Bibin Giri

Name of contractor : Southern Tech
Agreement date : 29-09-2018
Agreed Amount : ₹8.35 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 08-10-2018
Project duration : 15 months
Scheduled Date of Completion : 07-01-2021
Expected Date of completion : 31-10-2022

Scheduled progress as on 14-11-2022 - 98.5%

Achieved progress as on 14-11-2022 - 94%

Last week progress - 0.2%

Current week progress 0.2%

Current Bill Status : 4th bill approved

Current Financial Progress : 80%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Cleaning & desilting- 75% (cleaning was done once. It will be done again before final hand over.)
- Side protection work- 96%
- Road and walkway formation- 75%
- Removing hyacinth - 75%
- Boat jetty -100%
- Skew bridge -100%
- Foot bridge-100%
-

Works done in the last week

- Anchor beam & anchor block work in Right Bank and Left bank completed.
- Fencing post fixing work in progress
- Coconut pile stacking completed



**ELECTRICAL
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIPPUNITHURA
MUNICIPALITY—PROVIDING STREET
LIGHTS ALONG THE PATHWAYS OF
ANTHAKARATHODE**

Name of Project Engineer: Princy Abraham

Name of Project Coordinator : Vishnu

Name of contractor : Essjay Electro links
Agreement date : 31-12-2020
Agreed Amount : ₹50.27 lakhs
Agreed Amount With GST : Rs. 5630313.00
Site Handover date : 10-01-2021
Project duration : 5 months
Scheduled Date of Completion : 30-05-2021
Expected Date of completion : 15-11-2022

Scheduled progress as on 14-11-2022- 100%

Achieved progress as on 14-11-2022- 93.1%

Last week progress - 0%

Current week progress 0%

Current Bill Status : RE submitted, Applied for ToC extension

Current Financial Progress : 82%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Earthing with GI earth plate - 99%
- Erection of Cast Iron lamp post & LED, Excavation of earth for foundation, Installation of feeder pillar, Laying of DWC pipe including excavation & refilling, RCC formwork & concreting - 100%
- Plastering & painting - 50%
- Supplying & laying of armoured cable - 90%

Works done in the last week

- Presently, work is delayed due to delay in completing the civil works.
- The remaining work depends on civil work (pathway).



**BEAUTIFICATION
ANTHAKARATHODU**

**IMPROVEMENT WORKS TO
ANTHAKARATHODE IN
THRIIPPUNITHURA
MUNICIPALITY–LANDSCAPING &
ARBORICULTURE, CONSTRUCTION OF
KIOSK AND TOILET AND OPERATION &
MAINTENANCE FOR ONE YEAR**

Name of Project Engineer: Princy Abraham

Name of Project Coordinator : Bibin Giri

Name of contractor : GRIDS,Digital Surveyors and
Engineering Consultants
Agreement date : 24-06-2021
Agreed Amount : ₹76.62 lakhs
Agreed Amount With GST : Rs. 8581690.00
Site Handover date : 03-07-2021
Project duration : 3 months
Scheduled Date of Completion : 02-10-2021
Expected Date of completion : 02-01-2022

**Status of Work in
terms of components:**

- Landscaping & tress-6%
- Construction of Kiosk & Toilet-0%

Works done in the last week

Presently, no work.
The remaining work can be started only after completion of civil works (pathway).

Scheduled progress as on 14-11-2022- 40%

Achieved progress as on 14-11-2022- 6%

Last week progress - 0%

Current week progress - 0%

Current Bill Status : Nil

Current Financial Progress : 0 %

Images of works done at Site during last week (with time stamp)



PROJECTS IN IDUKKI DISTRICT

**ITI
KATTAPPANA
(KASE)**

UP GRADATION OF GOVT ITI KATTAPPANA ON PAR WITH INTERNATIONAL STANDARDS

**Name of Project Engineer: TEENU AUGUSTINE
Name of Project Coordinator : Bibin Giri**

Name of contractor : Anchanical constructions
Agreement date : 16.10.2020
Agreed Amount : Rs 4,76,87,560.83
Agreed Amount With GST : Rs 5,34,10,068.1
Site Handover date : 04-12-2019
Project duration : 08 months
Scheduled Date of Completion : 31-08-2022
Expected Date of completion : 31- 12-2022

Status of Work in terms of components:

- Brickwork-70%.
- plastering works-58%
- Electrical works-22.2%
- Grade beam concrete-100%
- Grade slab Concrete - 100%
- Roof beams and slab - 100%

Works done in the last week

- window fixing
- gate and security cabin works started
- floor cleaning works



Scheduled progress as on 14.11.2022- 100%

Achieved progress as on 14.11.2022 - 63.1%

Last week progress : 63%

Current week progress :0.1%

Current Bill Status : 4th and part bill submitted

Current Financial Progress :48 %

Images of works done at Site during last week



**ECO-LODGE
IDUKKI
ADDITIONAL
WORKS – III
(TOURISM)**

**ADDITIONAL WORK III OF ECO LODGE
CONSTRUCTION AT IDUKKI
(CONSTRUCTION OF MODULAR
KITCHEN,DRAINAGE,PARKING
YARD,SIDE WALL,WOOD WORK
POLISHING,ELECTRICAL WORKS &
GENERATOR ROOM).**

Name of Project Engineer:TEENU AUGUSTINE

Name of Project Coordinator : Bibin Giri

Name of contractor : M/S VJ Raju and Co.
Agreement date : 21.10.2021
Agreed Amount : Rs.71,96,599.18
Agreed Amount With GST : Rs. 80,60,191.08
Site Handover date : 31-10-2021
Project duration : 03 months
Scheduled Date of Completion : 31-03-2022
Expected Date of completion : 14-05-2022

Status of Work in terms of components:

- Modular kitchen-100%
- Wood work polishing - 100%
- Electrical works - 100%
- Generator room-100%
- Drainage-100%
- Parking yard-100%
- Handrail- 100%

Works done in the last week

- Physical works completed.Only financial progress remaining.

Scheduled progress as on 18.09.2022- 100%

Achieved progress as on 18.09.2022 - 100%

Last week progress : 100%

Current week progress : 0%

Current Bill Status : 1st & Part Bill : ₹49,46,902.00 (incl.GST) submitted to Tourism Department on 14.03.2022

Current Financial Progress : 58.25%

Images of works done at Site during last week



PEERMADE
GUEST HOUSE
RENOVATION
(TOURISM)

**UPGRADATION AND RENOVATION OF
GOVERNMENT GUEST HOUSE,
PEERUMEDU**

Name of Project Engineer: TEENU AUGUSTINE

Name of Project Coordinator : Sarath S R

Name of contractor :SRI BIBY SCARIA
Agreement date : 30-06-2020
Agreed Amount : Rs.1,45,51,908.00
Agreed Amount With GST : Rs. 1,71,71,251.44
Site Handover date : 13-07-2020
Project duration : 9 months
Scheduled Date of Completion :13-04-2021
Expected Date of completion : 31-10-2022

Scheduled progress as on 14-11-2022- 100 %

Achieved progress as on 14-11-2022 - 68 %

Last week progress -67 %

Current week progress - 1%

Current Bill Status : 2nd & Part Bill

Current Financial Progress : 40.19%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Guest house renovation - 16%
- Service block renovation - 100%
- Water tank - 85%
- Parking shed - 35%
- Conference hall - 80%

Works done in the last week

Dismantling old plaster and tile of guest house
- Plastering works of main guest house



PANCHALIMEDU
(TOURISM)

**PANCHALIMEDU TOURISM PROJECT
PHASE – 2
PERUVANTHANAM VILLAGE,
PEERUMEDU TALUK**

**Name of Project Engineer: TEENU AUGUSTINE
Name of Project Coordinator : Sarath S R**

Name of contractor : EASY INFRA INC, TVM
Agreement date : 22/12/2020
Agreed Amount : ₹2,43,99,440.78
Agreed Amount With GST : Rs. 2,73,27,373.67
Site Handover date : 01-01-2021
Project duration : 12 months
Scheduled Date of Completion : 31-12-2021
Expected Date of completion : TOE applied till 31.03.2022

Status of Work in terms of components:

- Renovation of panchalikulam - 50%
- Construction of pathway - 50%
- Proposed check dam - 25%
- Proposed lighting system - 0%
- Sitting benches - 0%
- Landscaping - 0%
- Rope cycling - 0%

Works done in the last week

- Check dam concreting for foundation

Scheduled progress as on 15-11-2022 - 50 %

Achieved progress as on 15-11-2022 - 22 %

Last week progress - 21 %

Current week progress - 1 %

Current Bill Status : 2nd & Part Bill submitted

Current Financial Progress : 11.10%

Images of works done at Site during last week (with time stamp)



PEERUMEDU
(TOURISM)

**ADDITIONAL WORK AT ECOLODGE
CONSTRUCTED AT PEERUMEDU
(CONSTRUCTION OF PARKING YARD,
COMPOUND FENCING, SERVICE
BLOCK, AMBIENT LIGHTING AND
MODULAR KITCHEN AT ECOLODGE
PEERUMEDU)**

Name of Project Engineer: TEENU AUGUSTINE

Name of Project Coordinator : Sarath S R

Name of contractor : Outlook communications pvt.ltd.
Agreement date : 08-10-2021
Agreed Amount : ₹80,27,681.98
Agreed Amount With GST : Rs.9472664.74
Site Handover date : 11-10-2021
Project duration : 12 months
Scheduled Date of Completion : 10-10-2022
Expected Date of completion : 31-01-2022

Scheduled progress as on 14-11-2022 - 100 %

Achieved progress as on 14-11-2022 - 51 %

Last week progress - 65 %

Current week progress - 3 %

Current Bill Status : 1st & Part Bill

Current Financial Progress : 28.90%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Fencing - 50%
- Service block - 85%
- Security cabin - 85%
- Diesel generator - 70%
- Modular kitchen - 90%
- Generator room - 50%
- Electrical works - 0%
- Civil work for lamp post - 0%

Works done in the last week

- **Fencing works**



PROJECTS IN KOTTAYAM DISTRICT

**ITI
ETTUMANOOR
(KASE)**

UP GRADATION OF GOVT ITI ETTUMANOOR ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: Atheesh P Mohan

Name of Project Coordinator : Sarath S R

Name of contractor : Swathy Construction
Agreement date : 30-07-2020
Agreed Amount : ₹ 6,95,25,557.81
Agreed Amount With GST : ₹ 7,78,68,624.74
Site Handover date : 10-08-2020
Project duration : 12 months
Scheduled Date of Completion : 09-08-2021
Expected Date of Completion : with in. 05.11.2022

Status of Work in terms of components:

- Main building civil works (99%)
- Existing class room converted to smart class rooms (Civil works -100%)
- Sump tank ,Front gate with security cabin civil works (100%)
- Road and ancillary works, compound wall (100%)
- Land development (90%)
- External water supply, sewerage system (100%)
- Rain water drainage (98%)
- Main building electrical works,ELV ,HVAC (75%)
- Fire protection works (99%)
- Furniture for main building and renovated smart class rooms (100%)

Works were done in the last week - Main building civil works

- Contractor restarted the electrical works at site.
- Resident engineer visited the site.

Scheduled progress as on 12-11-2022 - 98 %

Achieved progress as on 12-11-2022 -93.5 % (As per revised Estimate)


Last week progress - 93%

Current week progress - 0.5%

**Current Bill Status : CC 8th and part bill submitted for scrutiny and pass.
Amount:Rs. 43,52,039.910**

Current Financial Progress : 82%

Images of works done at Site during last week (with time stamp)

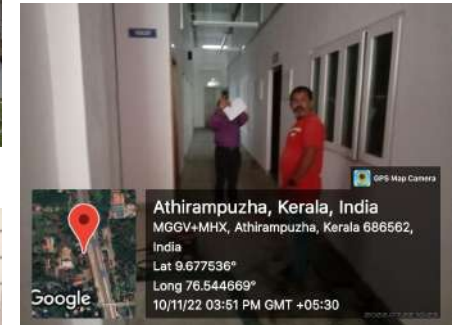

**SIHM PALA
(TOURISM)**

**SETTING UP OF STATE INSTITUTE
OF HOTEL MANAGEMENT
STUDIES AT PALA, KOTTAYAM
DISTRICT, CONSTRUCTION OF
ACADEMIC BLOCK**

Name of Project Engineer: DON BABY

Name of Project Coordinator : Gopakumar

Name of contractor : SITCO Associates
Agreement date : 01-03-2016
Agreed Amount : ₹13.48 Cr
Site Handover date : 10-03-2016
Project duration : 18 months
Scheduled Date of Completion : 31/10/2017
Expected Date of completion : 31/12/2021

Scheduled progress as on 12-11-2022 - 90%

Achieved progress as on 12-11-2022 - 77%

Last week progress -77%

Current week progress - 0%

Current Bill Status : Total bill amount (1st & Part Bill to 13th & Part Bill) ₹ 11,35,31,433.00

Current Financial Progress : 77 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Academic structural works completed
- Solid block partition work not started-0%
- Plastering work not started
- Overhead water tank work-40 %

Works were done in the last week

- Decision regarding AS revalidation received from tourism department and informed the contractor. No reply from contractor side
- contractor stopped the whole works since bills are pending



PROJECTS IN ALAPPUZHA DISTRICT

**ITI
CHENGANNUR
(KASE)**

**UP-GRADATION OF GOVT ITI
CHENGANNUR ON PAR WITH
INTERNATIONAL
STANDARDS - PHASE 1- REV 3**

**Name of Project Engineer: LEKSHMY GOPAN
Name of Project Coordinator : Omanakuttan**

Name of contractor : Creators Construction
Agreement date : 15/10/2020
Agreed Amount : Rs 18 Cr
Agreed Amount With GST : Rs20,64,45672/-
Site Handover date : 31.10.2021
Project duration :18 months
Scheduled Date of Completion : 29/04/2023
Expected Date of completion :20/07/2023

Scheduled progress as on 14/11/2022 : 58%

Achieved progress as on 14/11/2022 : 43%

Last week progress in :1%

Current week progress in:1%

Current Bill Status : cc 2nd and part bill amounting 1.67Cr passed.

Current Financial Progress : 16.5%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works (45%)
- Existing class room converted to smart classrooms (0%)
- Sump tank , substation works (1%)
- Road and ancillary works(1%)
- Land development (0%)
- External water supply, sewerage system (0%)
- Rain water drainage (0%)
- Main building electrical works,ELV ,HVAC (5%)
- External lighting & fire protection works (0%)
- Furniture for existing smart class room
Converted to smart classrooms (0%)

Works done in the last week :

- . Main building - AAC block works, ceiling & wall plastering, SF roof slab reinforcement works.
- . Hostel building - AAC block works, ceiling & wall plastering.
- Sump tank- excavation started



**ALAPPUZHA
CANALS
PHASE.01
(KIIFB)**

MODERNIZING WATER TRANSPORT IN ALAPPUZHA CANALS-PHASE 01

**Name of Project Engineer: Stephy Sebastian
Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva
Agreement date : 15-02-2019
Agreed Amount : ₹48.35 Cr
Agreed Amount With GST : Rs. 54,15,71,596.79
Site Handover date : 19-02-2019
Project duration : 12 months
Scheduled Date of Completion : 18-02-2020
Expected Date of completion : 30-08-2022

Status of Work in terms of components:

- All agreed works has been completed
- The repair of sunken road(near Pagoda resorts) is under progress.
- Construction of damaged road using interlock paver tiles in progress

Works done in the last week

- Laying of GSB for road in progress.
- WMM - final level achieved. interlock works will be progressed soon.
- Interlock work is completed
- some finishing work only pending

Scheduled progress as on 12-11-2022 - 100%

Achieved progress as on 12-11-2022 - 100%

Last week progress in 100%

Current week progress- 100%

Current Bill Status : Rs.47,65,31,121 upto 6th bill (Balance -5,86,02,883.67)last RE is submitted in KIIFB for approval

Current Financial Progress :90%

Images of works done at Site during last week (with time stamp)



**ALAPPUZHA
CANALS PHASE II
(KIIFB)**

**BEAUTIFICATION OF CANALS
IN ALAPPUZHA MODERNIZING
WATER TRANSPORT IN
ALAPPUZHA TOWN CANALS
AND CLEANING OF
KAPPITHODE -PHASE II**

**Name of Project Engineer: Atheesh P Mohan
Name of Project Coordinator : Gopakumar. K**

Name of contractor : TBAS Construction, Aluva
Agreement date : 16-05-2022
Agreed Amount : ₹40.95 Cr
Site Handover date : 24-05-2022
Project duration : 18 months
Scheduled Date of Completion : 25-11-2023
Expected Date of completion : 23-11-2023

Scheduled progress as on 12-11-2022 - 10 %

Achieved progress as on 12-11-2022 - 6.5 %

Last week progress in 6 %

Current week progress- 0.5 %

Current Bill Status : Nil

Current Financial Progress : Nil

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Retaining wall construction 10%
- canal cleaning works- 2%
- Survey - 10%
- culverts- not started
- Geo- textile works- not started

Works done in the last week

- Sub canals Surveying works are ongoing.
- DR masonry works for retaining wall in AS canal is progressing
- canal cleaning works of Pazhaveed ward started.



**PUNNAMADA
(TOURISM WORK)**

Punnamada- Starting Point Pathway and Boat Landing at Alappuzha District.

**Name of Project Engineer: Stephy Sebastian
Name of Project Coordinator : Gopakumar**

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 1.11 Cr
Agreed Amount With GST : Rs. 1,23,77,355.31
Site Handover date : 05-05-2021
Project duration : 6 months
Scheduled Date of Completion : 30-08-2022
Expected Date of completion : 30-09-2022

Scheduled progress as on 12-11-2022- 99%

Achieved progress as on 12-11-2022- 91%

Last week progress - 90%

Current week progress - 1%

Current Bill Status : 1st & Part Bill ₹50,02,073.00 (incl. GST) and 2nd & Part Bill ₹57,94,300.00 (incl. GST) submitted to Tourism on 26.03.2022 and 24.06.2022 respectively.

Current Financial Progress : 82.79%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Pathway
Solar Lighting

Works done in the last week

- Laying GSB
- Laying paver blocks
- Landscaping works
- Erection of solar LightLights
- Truss work for waiting sheds
- All work completed as per schedule some RE work is only pending.
- coconut pile casting is included in the Revised estimate.
- Letter regarding the same is given to DD of tourism and work can be proceed only after getting intimation from Tourism dept



**CHUNGAM
(TOURISM WORK)**

**CHUNGAM (CHAKREPURAKKAL)-
KAYALCHIRA PATHWAY
DEVELOPMENT AND BOAT
LANDING BY THE SIDE OF
PUNNAMADA RIVER, At
ALAPPUZHA DISTRICT**

Name of Project Engineer: Stephy Sebastian

Name of Project Coordinator : Gopakumar

Name of contractor : TBAS Construction, Aluva
Agreement date : 26-02-2021
Agreed Amount : ₹ 2.99 Cr
Agreed Amount With GST : Rs. 3,34,07,087.37
Site Handover date : 05-05-2021
Project duration : 9 months
Scheduled Date of Completion : 04-02-2022
Expected Date of completion : 24-09-2022

Scheduled progress as on 12-11-2022- 100%

Achieved progress as on 12-11-2022 - 83.5%

Last week progress - 80%

Current week progress - 3.5%

Current Bill Status : 1st & Part Bill ₹91,65,612.00 (incl. GST) and 2nd & Part Bill ₹1,29,06,381.00 (incl. GST) submitted to Tourism on 07.03.2022 and 21.06.2022 respectively.

Current Financial Progress : 62.71%


Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Walkway
- Boat Landing
- Pile & Slab retaining wall
- Solar Lighting

Works done in the last week

- Backfilling fully completed
- Anchor belt and beam- 69 completed. 30 to be completed.
- Filling of pavement completed using earth
- final levels of the quarry muck filling has been taken in accompany with initial level of GSB
- Filling of quarry muck and red earth had been completed.
- GSB laying on walkway is completed
- RE -2 is in preparation and will be submitted soon.
- TOC completed and extension shall be submitted with RE

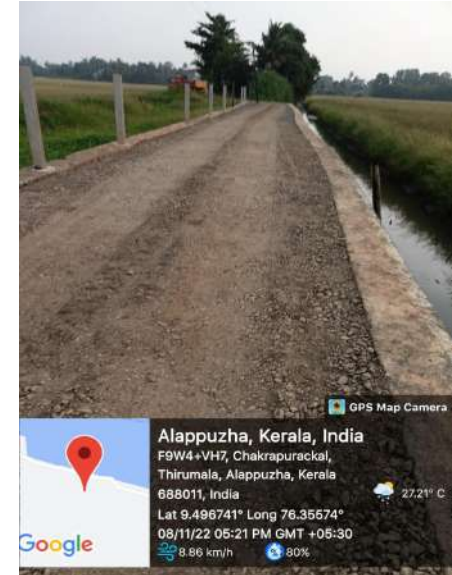

**PUNNAMADA
(TOURISM WORK)**

RENOVATION OF PUNNAMADA PARKING AREA AND PREMISES AT ALAPPUZHA DISTRICT

Name of Project Engineer: Stephy Sebastian

Name of contractor : TBAS Construction, Aluva
Agreement date : 11/01/2022
Agreed Amount : Rs 87,81,166.60
Agreed Amount With GST : Rs 98,34,906.59
Site Handover date : 21/01/2022
Project duration : 12 months
Scheduled Date of Completion : 20/01/2023
Expected Date of completion : 20/12/2022

Scheduled progress as on :12-11-2022-80%

Achieved progress as on : 12-11-2022- 50%

Last week progress - 40%

Current week progress - 10%

Current Bill Status : Nil

Current Financial Progress : 0%


Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Parking Area
- Landscaping
- Plumbing

Works done in the last week

- Clearing the site
- Removing the interlock
- Initial Level of quarry muck filling levelling completed at ABCDE, and FG
- The GSB laying completed for ABCD and FG
- Interlock completed at FG
- Final levels for ABCD has been taken and calculation in progress
- GSB laying completed
- Brick work of the plot completed
- Kerb stone work also completed.

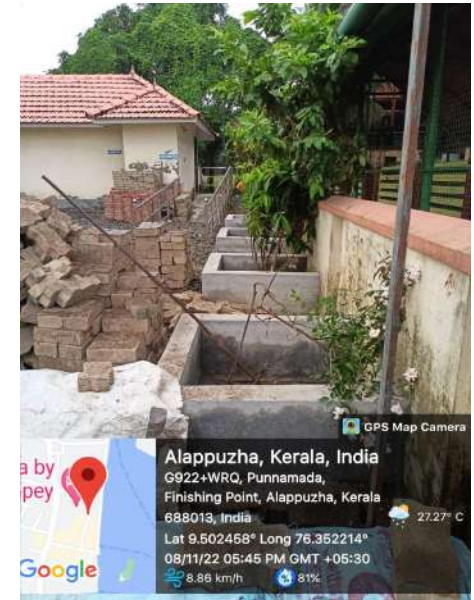

**GROYNES AT
AMBALAPUZHA
(KIIFB)**

**Construction of 30 nos. Groyne Between CЕСCP
645 and 672 (Ch 77.34 km to Ch. 82.74 km) at
Ambalapuzha South, North panchayath and
Punnapra South Panchayath**

Name of Project Engineer: SILPA R

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 51.3 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 31-01-2023 as per EOT
Expected Date of completion : 31-01-2023

Scheduled progress as on 13-11-2022 – 100 %

Achieved progress as on 13-11-2022 - 80 %

Last week progress - 0%

Current week progress -0%

Current Bill Status : 8 th bill submitted for an Amt of Rs.33843747.40
Total bill amount - Rs. 483071273.22

Current Financial Progress : 79%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groynes – 5 nos- 2completed
- 30M GROYNES -7nos- 4completed.
- 40M GROYNES – 9 nos -6completed.
- 50M GROYNES – 9 nos -6completed.
- Sea wall length-305 m – not started
- 172805.452 MT boulders reached out of 178922 MT (100 %)
- 2T TETRAPODS –23151nos. casted out of 23902 nos. (96.86%)
- 5T TETRAPODS – 2955 nos. casted out of 2956 nos.(99.9 %)
- Earthwork Excavation – 23131.66 m3 completed out of 45955.7 M3 (43%)

Works done in the last week

The total no.of tetrapods casted
2T-0& 5T-0nos

- Supplying and Laying of Boulders -0 MT
- 2361 Nos 5T tetrapods layed
- 12541 Nos 2T layed.
- 18Nos Groynes completed out of 30Nos, 7nos are in progress and 5nos are to be started. To carry out the rest of the Groynes fields with more numbers of tetrapods, sanction of the revised estimate is essential.



**GROYNES AT
ARATTUPUZHA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
21NOS GROYNES AT
ARATTUPUZHA IN BET.CH.56.6
TO 57.8 KM AT ARATTUPUZHA**

Name of Project Engineer: M A FASEELA NASAR

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹ 26. 23Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :31-01-2023 as per EOT
Expected Date of completion :31-01-2023

Scheduled progress as on 12-11-2022- 100 %

Achieved progress as on 12-11-2022-56%

Last week progress - 55%

Current week progress - 1 %

Current Bill Status: 6 part bill submitted for an amount of Rs 20,08,01,159/-

Current Financial Progress : 55 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 6 NOS- 3 completed
- 25M GROYNES - 15 NOS- 3 cmplt, 10 started
- SEA WALL LENGTH - 40m –Not started
- TOTAL QUANTITY OF BOULDERS - 63982 T (68%) 94497 MT
- 2T TETRAPODS - 10075 (100%) nos casted out of 9874 NOS
- 5T TETRAPODS - 2461 (100 %) nos casted out of 2385 NOS
- GEOMAT - 64739 M2 (not done)
- EARTHWORK EXCAVATION - 3290 M3(not done)

Works done in the last week

- 1252 5T tetrapod layed
- 2980 2T tetrapod layed
- Boulder work has been restarted last week (3024 T layed)
- Out of 21 no. 6 numbers of groynes are complt. another 10 numbers of groynes are started.



**GROYNE SITE
AT
PATHIYANKARA
(KIIFB)**

**KIIFB
PROJECT-CONSTRUCTION OF
13NOS GROUYNE AT
PATHIYANKARA IN BET.CH.60.1
TO 61.6KM AT
THRIKKUNNAPUZHA.**

Name of Project Engineer: SILPA R

Name of Project Coordinator : RAJASEKHARAN PILLAI

Name of contractor : Ramalingam construction Company Pvt. Lmted.
Agreement date : 22.07.2020
Agreed Amount : ₹20.08Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 31-01-2023 as per EOT
Expected Date of completion : 31-01-2023

Status of Work in terms of components:

1. 20M GROYNES - 2 NOS-One is completed
2. 30MGROYNES -4 NOS-2completed and 1nos is in progress
3. 50M GROYNES - 7 NOS- 3completed and 2nos is in progress
4. 61876.225MT boulders reached out of 74546 MT(83%)
5. 2T TETRAPODS -8930casted out of 8930NOS(100%)
6. 5T TETRAPODS - 1190nos casted out of 1199NOS(99%)
7. GEOMAT - 43835M2
8. EARTHWORK EXCAVATION- 4154.29 M3

Works done in the last week -

- . Groynes G1,G2 ,G3, G5&G6 are completed, **3nos are in progress and 4nos are to be started.**
- . Supplying and laying of boulders-OT
- . 772 5T tetrapod layed
- . 4160 2T tetrapod layed
- . **no work can be done without RE sanction due to the design changes and change of various items.**

Scheduled progress as on 13-11-2022 - 100%

Achieved progress as on 13-11-2022 -66 %

Last week progress in -0%

Current week progress in 0%

Current Bill Status :7th part bill submitted for an Amt of Rs. 12811052.37
Total bill amount - Rs. 170854619.44

Current Financial Progress in :64 %

Images of works done at Site during last week (with time stamp)



**GROYNE SITE
AT.
VATTACHAL
(KIIFB)**

**KIIFB
PROJECT – CONSTRUCTION OF
16 NOS GROUYNE AT
VATTACHAL IN BET. CH.53.4 TO
CH.55.2 KM(1.8KM)
AT ARATTUPUZHA GP**

**Name of Project Engineer: M A FASEELA NASAR
Name of Project Coordinator : RAJASEKHARAN PILLAI**

Name of contractor : Ramalingam construction Company Pvt. Ltd.
Agreement date : 22.07.2020
Agreed Amount : ₹28. 83Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion :31-01-2023 as per EOT
Expected Date of completion :31-01-2023

Scheduled progress as on 12-11-2022 - 100 %

Achieved progress as on 12-11-2022 - 72 %

Last week progress - 72%

Current week progress - 0 %

Current Status : 8 part bills submitted for an amt of Rs 23,13,12,922/-

Current Financial Progress in % : 71.8 %

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20M GROYNES - 2 NOS- 2 cmpltd
- 30M GROYNES - 10 NOS- 10 cmpltd
- 40M T GROYNE - 4 Nos - 4 started
- TOTAL QUANTITY OF BOULDERS - 93927 MT (92.5 %) reached out of 101487 MT
- 2T TETRAPODS - 8941(100 %) nos casted out of 8941 NOS
- 5T TETRAPODS - 3518 (102 %) nos casted out of 3432 NOS
- GEOMAT - 5638 m2 (6 %) layed out of 76299 M2
- EARTHWORK EXCAVATION - (8191.37 m3 out of 62380 M3)

Works done in the last week

- Out of 16 no. 12 numbers of groynes are completed. another 4 numbers of T groynes are started.
- 2077 5T tetrapods layed
- 6956 2T layed.
- **Agreement quantity completed last week, hence no work in the site. To carry out the rest of the Groynes fields (4 T groynes) with more numbers of tetrapods, sanction of the revised estimate is**



**GROYNES SITE AT
KATTOOR
(KIIFB)**

**Construction of 34 nos. Groyne
at Kattoor from Ch.168.465KM
TO CH 171.627KM (Old CH
96.643KM TO CH 9.535 KM)**

Name of Project Engineer: SILPA R

Name of Project Coordinator : Mahadevan P

Name of contractor : Ramalingam Construction Company Pvt Ltd.
Agreement date : 22-07-2020
Agreed Amount : ₹ 49.04 Cr
Agreed Amount With GST : Rs.
Site Handover date : 30-07-2020
Project duration : 18 months
Scheduled Date of Completion : 31-01-2023 as per EoT
Expected Date of completion : 31-01-2023

Scheduled progress as on 13-11-2022–100% (as per EoT given)

Achieved progress as on 13-11-2022- 81%

Last week progress - .0.5%

Current week progress -0.5%

Current Bill Status :8th bill submitted for an Amount of Rs.47715746.89/- .Total bill amount - Rs. 451641352.92

Current Financial Progress :71.3%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- 20m groyne - 3 nos completed out of 3
- 30m Groyne-5 nos completed out of 7
- 40m groyne - 14 nos completed out of 24
- Total boulders quantity - 174010.85 MT boulders reached out of 174010 MT (100%)
- 2T TETRAPODS – 21553 nos (99.95%) casted out of 21562 nos.
- 5T TETRAPODS – 3144 (100%) nos. casted out of 3144 nos.
- Geomat - 15981.50m²
- Earthwork Excavation - 42106.863m³ out of 42122 M³

Works done in the last week

- 22Nos Groyne are completed out of 34 nos, 7nos are in progress and 5 nos are to be started. Only tetrapod laying is progressing on Groyne where the boulders have already been completed. To carry out the rest of the Groyne fields with more numbers of tetrapods, sanction of the revised estimate is essential
- 2T & 5T casting are completed
- Supplying and Laying of Boulders - nil
- 2548 Nos 5T tetrapods laid
- 13891Nos 2T laid.
- 3090 nos 5T laid



PROJECTS IN KOLLAM DISTRICT

**ITI CHANDANATHOPE
(KASE)**

**UPGRADATION OF GOVT. ITI
CHANDANATHOPE ON PAR
WITH INTERNATIONAL
STANDARDS**

Name of Project Engineer:MEENU E S

Name of Project Coordinator : Omanakuttan

Name of contractor : Asian Constructions
Agreement date : 16-12-2020
Agreed Amount : ₹3.65 Cr
Agreed Amount With GST : Rs. 4,09,28,822.77
Site Handover date : 24-12-2020
Project duration : 8 months
Scheduled Date of Completion :23/08/2021
Expected Date of completion : 30/10/2022

Scheduled progress as on 12/11/2022 - 100%

Achieved progress as on 12/11/2022 - 85%

Last week progress : 44%

Current week progress :5%

Current Bill Status:4th Bill submitted to KASE

Current Financial Progress : 56%



Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Main building civil works –87%
- Front gate with security cabin – 89%
- Compound wall – 99%
- Widening of existing roads and ancillary works – 0%
- External water supply & external sewerage – 0%
- Electrical, elv, hvac & fire fighting works –3%
- Existing classrooms converted to smart classrooms – 50%
- Signage & boards – 0%
- Furniture for main building & existing classrooms – 0%

Works done in the last week

- . Main building
- . Electrical works on going DG set and LT PANEL COMMISSIONING in progress
- . Road work completed

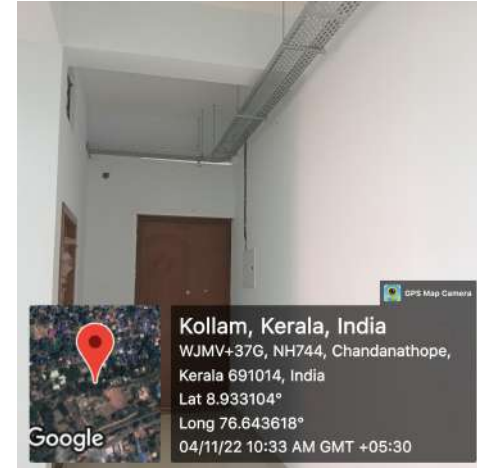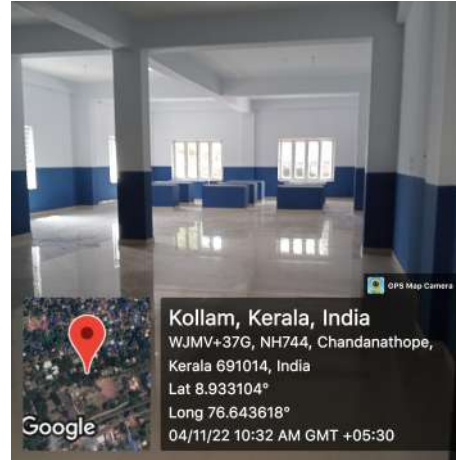

**Thenmala
(Tourism Project)**

IMPROVEMENT AND DEVELOPING ECO-TOURISM AT THENMALA DAM IN KOLLAM DISTRICT

Name of Project Engineer: Meenu ES

Name of Project Coordinator : OMANAKUTTAN

Name of contractor : Tomy Vallamattom
Construction
Agreement date : 29-10-2020
Agreed Amount : ₹3,45,61,108.96
Agreed Amount With GST : ₹4,07,82,108.57
Site Handover date : 09-11-2020
Project duration : 15 months
Scheduled Date of Completion : 08-02-2022
Expected Date of completion : 30-11-2022

Scheduled progress as on 12/11/2022- 100%

Achieved progress as on 12/11/2022-66%

Last week progress -54%

Current week progress -10%

Current Bill Status : part bill submitted to KIIDC

Current Financial Progress : 58%

Images of works done at Site during last week (with time stamp)

Status of Work in terms of components:

- Shop (9%)
- Shed to shop (40%)
- Building Renovation (15%)
- Children play (1%)
- Water tank (40%)
- Security cabin (2%)
- Toilet and cloak room (7%)
pavilion(50%)

Works done in the last week

1. Toilet, security room and cloak room-tile work completed.
2. Shed to shop-tile work completed
3. Children's play area -back side retaining wall completed
4. Seating area block work completed.plastering in progress
5. Handrail welding work in progress..and fixing in progress



**ITI
DHANUVACHAPU
RAM
(KASE)**

UPGRADATION OF GOVT. ITI DHANUVACHAPURAM ON PAR WITH INTERNATIONAL STANDARDS

Name of Project Engineer: ATHEESH P MOHAN

Name of Project Coordinator : Sarath S R

Name of contractor : Heather Construction
Agreement date : 25-11-2019
Agreed Amount : ₹11.18 Cr
Agreed Amount With GST : Rs. 12,52,34,417.4
Site Handover date : 04-12-2019
Project duration : 20 months
Scheduled Date of Completion :30-09-2022
Expected Date of completion 31.12-2022

Status of Work in terms of components:

- Civil works as per BOQ completed (98%)
- Electrical works as per BOQ Completed(98%)
- Mechanical Works (fire fighting works not done since pending approval of RE-2 from KASE)-(60%)
- Fire fighting works-delayed due to pending of approval from KASE (SPV)

Works done in the last week

work stopped by the contractor since the Revised estima-2 is not get approval from SPV(KASE)

Scheduled progress as on 12-11-2022- 95 % (Scope of the work were increased as per the instructions from SPV)

Achieved progress as on 12-11-2022 - 95%


Last week progress - 95%

Current week progress -0%

Current Bill Status :17th bill submitted.

Current Financial Progress :93.31%

Images of works done at Site during last week (with time stamp)

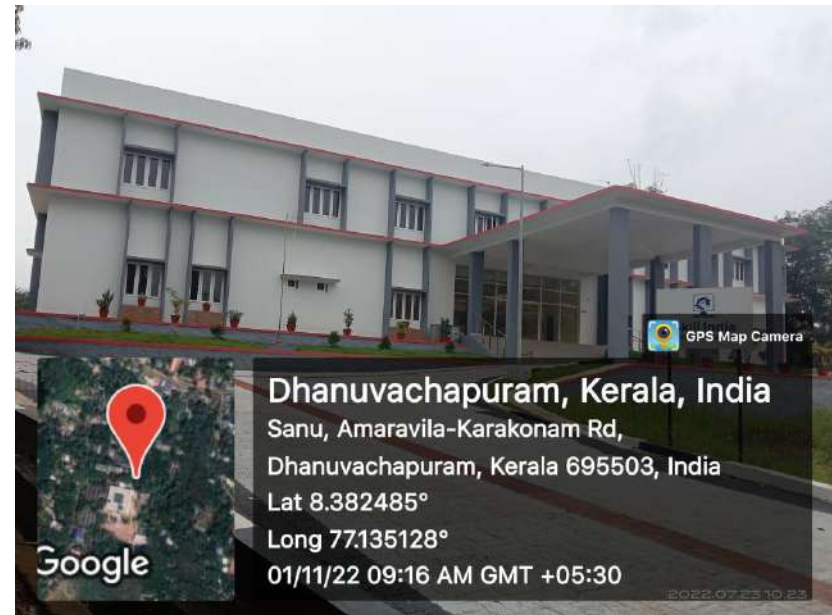

LIST OF COMPLETED WORKS – DEPARTMENT OF TOURISM

Sl. No.	Name of the Work	A.S. Amount	
1	Karappuzha Phase III – Construction of Viewing Tower, Bamboo Pavilion and Bridge	₹	4,00,00,000.00
2	Karappuzha Phase III – Construction of Pathway, Fishing Dock, Pond, Gazebo, Parking yard and Landscaping		
3	Development of Peruvannamuzhi Dam Tourism Project in Kozhikode District	₹	3,13,88,620.00
4	Additional Work I of Eco Lodge Construction at Idukki	₹	90,00,000.00
5	Additional Work II of Eco Lodge, Idukki	₹	59,85,426.00
6	Additional Work III of Eco Lodge, Idukki	₹	97,45,000.00
7	Kumarakom Cheepunkal Destination Development Project at Aymanam Panchayat in Kottayam District	₹	1,44,00,000.00
8	Providing Temporary Rest Room cum Store (Container Type) for Life Guards at Alappuzha Beach	₹	11,40,000.00
9	Cleaning Water Hyacinth at Nalupanku, Kumarakom	₹	7,97,832.00
